




**ETHEKWINI MUNICIPALITY**  
**Occupational Health & Safety Unit**

**BASELINE RISK ASSESSMENT**

Document Title	Baseline Risk Assessment
Client	eThekwini Municipality – Human settlements
Project	Construction of 976 row attached duplex BNG top-structure units at Cornubia Phase 2B
Contract Number	1H-32115
Internal reference	BRA19/10/2025
Compiled by (Safety officer)	Name and surname: Siya Nkosi Signature:  Date: 14/10/2025
Reviewed by (Manager: Safety & Risk)	Name and surname: Arty Zondi Signature:  Date: 14/10/2025

## **BASELINE RISK ASSESSMENT**

**1. INTRODUCTION:** In accordance with the Occupational Health and Safety Act, (Act 85 of 1993) the Legislator places specific requirements on an Employer. One of these is prescribed in Section 8(i) of the Act where it requires the Employer to ascertain the risks and dangers which may occur within the workplace or section of the workplace and then goes on to establish working procedures or practices.

**2. PURPOSE:** This is conducted to create a benchmark of the potential risks that apply to the whole project or business operation.

**3. SCOPE:** This assessment could be approached on a site, regional or national level concerning any facet of the business operation or process or activity.

### **4. REVIEW AND MONITORING PLAN**


The risk assessment form part of the health and safety plan to be applied on the site and must include the following:

- (a) The identification of the risk and hazards to which persons may be exposed.
- (b) An analysis and evaluation of the risk and hazards identified based on a documented method,
- (c) A documented plan and applicable safe work procedures to mitigate, reduce or control the risks and hazards that have been identified;
- (d) A monitoring plan; and
- (e) A review plan

### **5. REFERENCES**

- (a) Tender document number 1H-32115
- (b) Occupational Health & Safety Act and its Regulations

## 6. LOCALITY PLAN

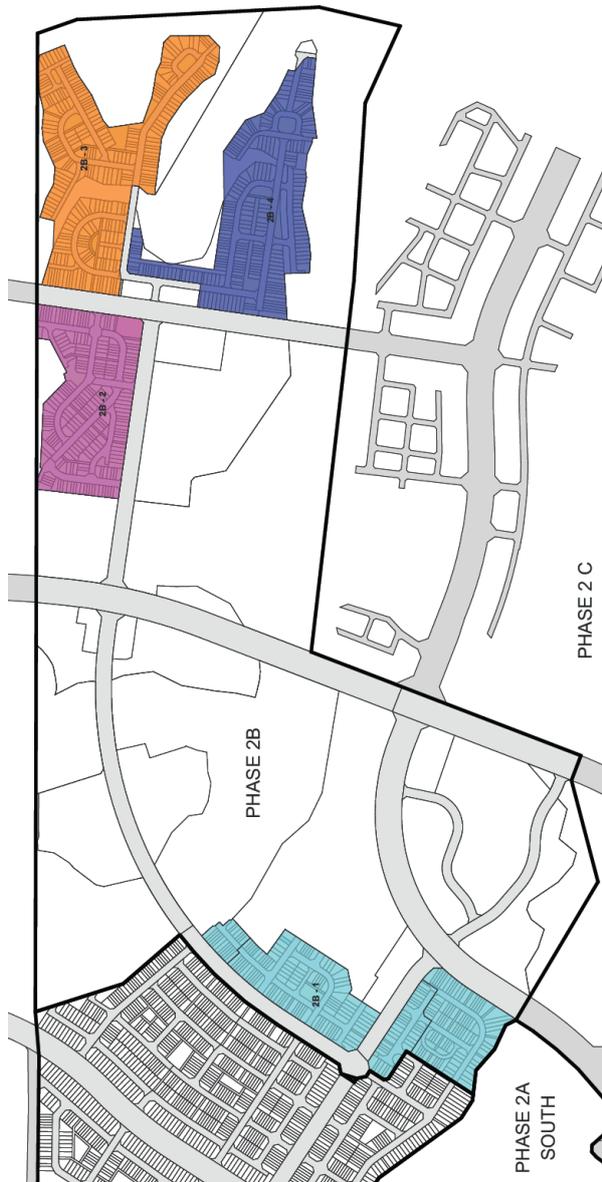

## **SCOPE OF WORK**

Site establishment

Site clearing

Electrical installations

Hand tools and electrical tools

Construction vehicles and mobile plants

Public safety

Elevated positions

Excavations

Concrete works

Blockwork

Roof work

Temporary works

# 1. RISK ESTIMATION AND EVALUATION

## RISK CLASSIFICATION USING A RISK SCORE TECHNIQUE

<b>Exposure (E) How frequently does the hazardous event occur</b>		<b>Risk level</b>
Continuously .....		10
Frequently (daily) .....		6
Occasionally (weekly) .....		3
Unusually (monthly) .....		2
Rarely (few a year) .....		1

<b>Probability (P) The probability of a loss when the hazardous event does occur</b>		<b>Risk level</b>
Frequent (happens often) .....		10
Probable (quite possible) .....		6
Occasional (unusual, but possible) .....		3
Remotely possible (has happened somewhere) .....		1
Improbable (practically impossible) .....		0.5

<b>Severity (S) Consequences of the hazardous event</b>		<b>Risk level</b>
<b>Catastrophic</b> many fatalities; or interruption of longer than 2 weeks; or asset or environmental damage (or both) exceeding R100m .....		100
<b>Disaster</b> (few fatalities; or interruption between one and 2 weeks; or asset or environmental damage (or both) exceeding R10m) .....		40
<b>Very serious</b> (one fatality; or interruption of 6 days; or asset or environmental damage (or both) exceeding R100,000 .....		7
<b>Important</b> (temporary disability; or interruption between 6 and 24 hours; or damage exceeding R10,000 .....		3
<b>Noticeable</b> (first aid needed; or interruption of less than 6 hours; damage exceeding R1000) .....		1

<b>Risk classification (Risk score = E x P x S )</b>	
<b>Risk score</b>	<b>Risk level</b>
Over 400-----5	Very high risk – discontinue operation or activity
200 to 400 ----- 4	High risk – immediate correction needed
70 to 200----- 3	Substantial risk – correction needed
20 to 70----- 2	Possible risk – attention needed
Under 20 ----- 1	Risk accepted

**BASELINE RISK ASSESSMENT WORKSHEET: IDENTIFYING EXISTING & POTENTIAL RISKS**

	Activity	Hazard	Risk	Risk Evaluation			Risk Score	Risk level
				E	P	S		
<b>1</b>	<b>Site establishment</b>							
	Manual and mechanical clearing of the land. Off-loading and positioning of containers by mobile crane. Fencing. Installation of temporary water supply, electricity, ablution facilities	<ul style="list-style-type: none"> <li>Incompetent construction mobile plant operator. Manual Handling of equipment and materials. Uneven surfaces. Driving on dangerous and undulating terrain. Reckless driving. Electrocutation. Incorrect/ poor connection of temporary services</li> </ul>	<ul style="list-style-type: none"> <li>Body injuries/ Accidents. Destruction of services. Burns/ death</li> </ul>	2	6	3	36	2
<b>2</b>	<b>Site clearing</b>							
	Clearing of the site using construction mobile plant and hand tools	<ul style="list-style-type: none"> <li>Incompetent driver/ operator; Unsafe</li> </ul>	<ul style="list-style-type: none"> <li>Accident; property damage; machinery running out of control; Injury to body;</li> </ul>	3	6	7	126	3

		<ul style="list-style-type: none"> <li>construction mobile plant/ hand tools;</li> <li>Petrol and oil spillages;</li> <li>Existing services; Noise</li> </ul>	<ul style="list-style-type: none"> <li>Environmental contamination;</li> <li>Noise induced hearing loss</li> </ul>							
<b>3</b>	<b>Electrical installations</b>									
		<ul style="list-style-type: none"> <li>Incompetent personnel. Unsafe hand-tools/ electrical tools. Unsafe ladder. Electrocutation</li> </ul>	<ul style="list-style-type: none"> <li>Improper installation of electricity/ non-compliance with safety standards. Injury to hands. Burns; electric shock</li> </ul>	3	3	7	63		2	
<b>4</b>	<b>Hand tools and electrical tools</b>									
		<ul style="list-style-type: none"> <li>Unsafe tools; Untrained or unauthorized operator;</li> </ul>	<ul style="list-style-type: none"> <li>Injury to body; damage of tools</li> </ul>	6	3	1	18		1	
<b>5</b>	<b>Construction mobile plant and vehicles</b>									
		<ul style="list-style-type: none"> <li>Untrained operator or driver; noise; dust; vibration; other vehicles</li> </ul>	<ul style="list-style-type: none"> <li>Collision with other vehicles; damage to property; noise induced hearing loss; body pain; death; disablement ect.</li> </ul>	6	6	7	252		4	
<b>6</b>	<b>Public safety</b>									

		<ul style="list-style-type: none"> <li>Public exposure to construction activities; fighting over resources</li> </ul>	<ul style="list-style-type: none"> <li>Injury to body; work stoppage; Legal claims</li> </ul>	6	6	7	252	4
<b>7</b>	<b>Elevated positions</b>							
		<ul style="list-style-type: none"> <li>Falling from; falling into</li> </ul>	<ul style="list-style-type: none"> <li>Death; Broken bone; Disablement</li> </ul>	6	6	7	252	4
<b>8</b>	<b>Excavations</b>							
	<ul style="list-style-type: none"> <li>Manual and mechanical excavation of trenches using construction mobile plants and hand tools</li> </ul>	<ul style="list-style-type: none"> <li>Unsafe machinery/ hand tools/ Unprotected trenches/ People exposure to excavations</li> </ul>	<ul style="list-style-type: none"> <li>Broken bone/ dislocation/ Accidents/ injuries to hands/ Falling into excavation/ claims and prosecutions</li> </ul>	3	6	3	54	2
<b>9</b>	<b>Concrete works</b>							
		<ul style="list-style-type: none"> <li>Concrete spillage/ Concrete contact with body</li> </ul>	<ul style="list-style-type: none"> <li>Soil contamination/ Skin problems</li> </ul>	3	3	3	27	2
<b>10</b>	<b>Blockwork</b>							
		<ul style="list-style-type: none"> <li>Unsafe working at height platforms; Unsafe hand tools; Contact with mortar</li> </ul>	<ul style="list-style-type: none"> <li>Fall risk; broken bone; dislocation; Injury to hands; Skin dermatitis</li> </ul>	6	6	3	108	3

<b>11</b>	<b>Roof work</b>							
		<ul style="list-style-type: none"> <li>Working on fall risk position; Unsafe roof access; Untrained roof erectors; No/ poor roof work planning; Collapsing of the roof; Falling objects</li> </ul>	<ul style="list-style-type: none"> <li>Falling from; Falling into; broken borne; death; disablement; Head injuries</li> </ul>	6	6	7	252	4
<b>12</b>	<b>Temporary works</b>							
		<ul style="list-style-type: none"> <li>Collapsing of temporary structure; Incompetent temporary supervision; Noncompliance with engineers drawing/ instruction; Unsafe temporary works</li> </ul>	<ul style="list-style-type: none"> <li>Death; temporary or permanent disable; incorrect erection of temporary works; Injuries to body</li> </ul>	3	6	7	126	3

## RISK PROFILE:

### Construction of 976 row attached duplex BNG top-structure units at Cornubia Phase 2B

