



public works
& infrastructure

22/08/2025

BOOK 1 OF 2

Department:
Public Works and Infrastructure
REPUBLIC OF SOUTH AFRICA

**ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36
MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL,
MECHANICAL, ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)**

WCS: 056397

TENDER NUMBER: H25/008 AI

REFERENCE NUMBER: WCS 056397

TENDER DOCUMENT

AUGUST 2025


ISSUED BY:

THE DIRECTOR-GENERAL
Department of Public Works and Infrastructure
Central Government Offices
C/o Bosman & Madiba streets
Pretoria
0001

Name of Tenderer:.....

RETURNABLE DOCUMENT

REPAIR AND MAINTENANCE PROGRAMME CONTRACT
DOCUMENT BREAKDOWN STRUCTURE

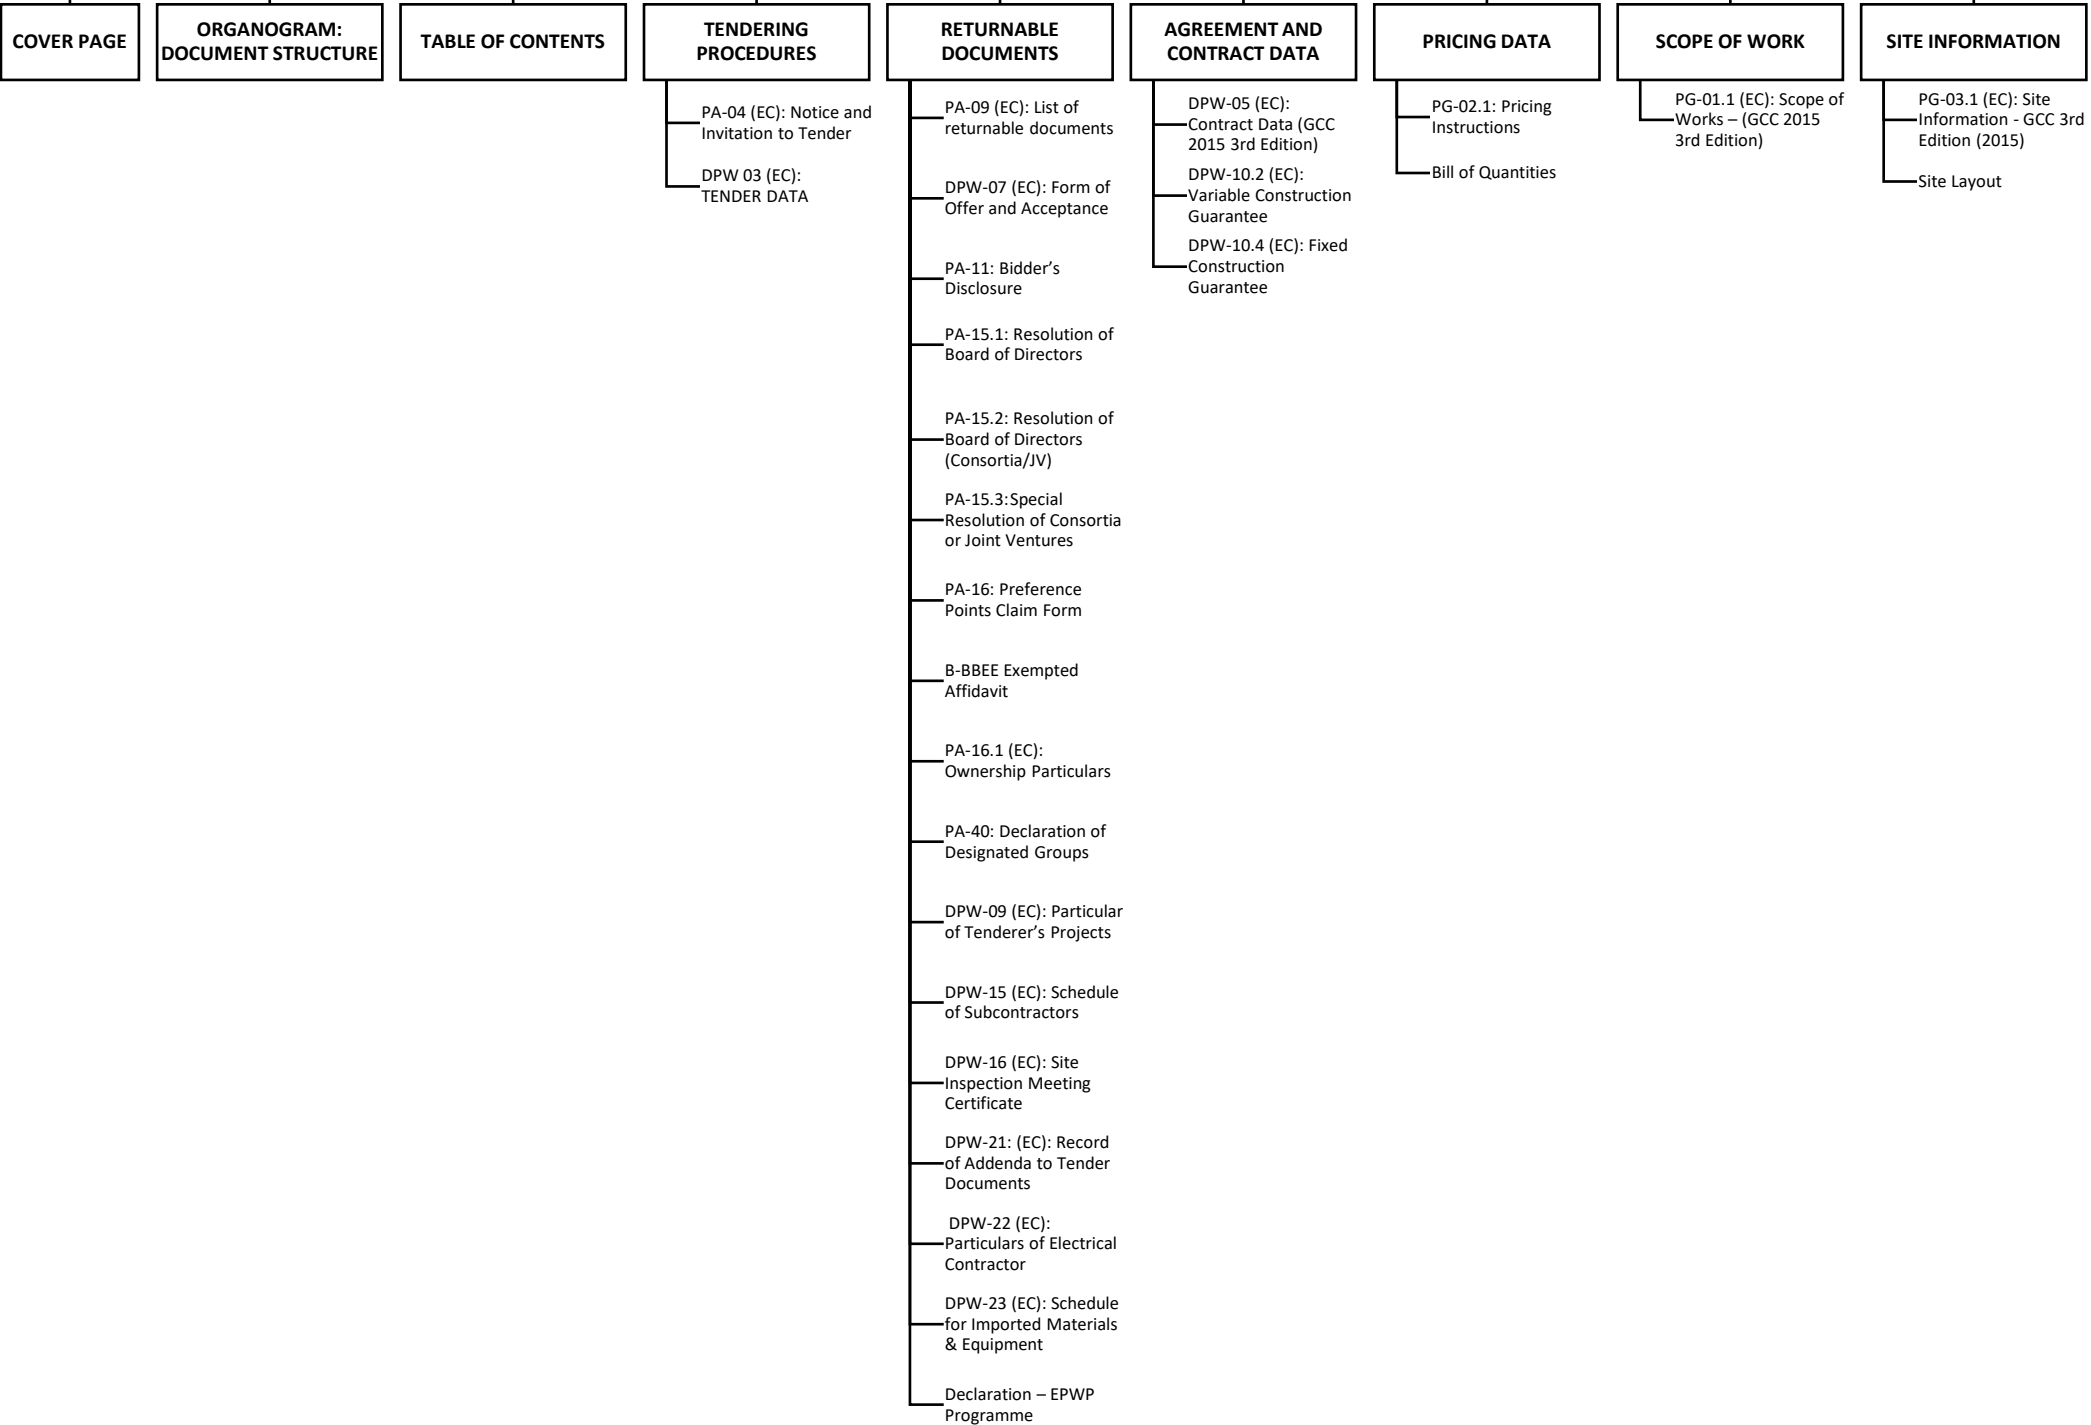

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

TABLE OF CONTENTS

BOOK 1 OF 2
THE TENDER

PART T1 TENDERING PROCEDURES

T1.1	PA-04 (EC)	Notice and Invitation to Tender
T1.2	DPW-03 (EC)	Tender Data

PART T2 RETURNABLE DOCUMENTS

T2.1	PA-09 (EC)	List of returnable documents
T2.2	DPW-07 (EC)	Form of Offer and Acceptance
T2.3	PA-11	Bidder's Disclosure
T2.4	PA-15.1	Resolution of Board of Directors
T2.5	PA-15.2	Resolution of Board of Directors (Consortia/JV)
T2.6	PA-15.3	Special Resolution of Consortia or JV's
T2.7	PA-16	Preference Points Claim Form in Terms of the Preferential Procurement Regulations 2022
T2.8		B-BBEE Exempted Affidavit for Exempted Micro Enterprises (Issued in terms of the amended construction sector code)
T2.9	PA-16.1 (EC)	Ownership Particulars
T2.10	PA-40	Declaration of Designated Groups
T2.11	DPW-09 (EC)	Particular of Tenderer's Projects
T2.12	DPW-15 (EC)	Schedule of Subcontractors
T2.13	DPW-16 (EC)	Site Inspection Meeting Certificate
T2.14	DPW-21 (EC)	Record of Addenda to Tender Documents
T2.15	DPW-22 (EC)	Particulars of Electrical Contractor
T2.16	DPW-23 (EC)	Schedule for Imported Materials & Equipment
T2.17		Declaration – EPWP Programme

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

THE CONTRACT

PART C1 AGREEMENT AND CONTRACT DATA

C1.1	DPW-05 (EC)	Contract Data (GCC 2015 3 rd Edition)
C1.2	DPW-10.2 (EC)	Variable Construction Guarantee
C1.3	DPW-10.4 (EC)	Fixed Construction Guarantee

PART C2 PRICING DATA

C2.1	PG-02.1	Pricing Instructions
C2.2		Bill of Quantities

PART C3 SCOPE OF WORK

C3.1	PG-01.1 (EC)	Scope of Works – (GCC 2015 3 rd Edition)

PART C4 SITE INFORMATION

C4.1	PG-03.1 (EC)	Site Information – (GCC 2015 3 rd Edition)
C4.2		Site Layouts

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

THE TENDER

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

PART T1: TENDERING PROCEDURES

PA-04 (EC): NOTICE AND INVITATION TO TENDER

THE DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE INVITES TENDERS FOR:

Project title:	Alexander Bay, Vioolsdrift & Onseepkans Land Ports of Entry: 36 Months Infrastructure Maintenance and Repairs of Buildings, Civil, Mechanical, Electrical and Installation (Appointment of a Contractor)

Tender no:	H25/008 AI	Reference no:	WCS 056397
Advertising date:	22 August 2025	Closing date:	15 September 2025
Closing time:	11:00	Validity period:	84 Calendar days

1. REQUIRED CIDB GRADING

It is estimated that tenderers should have a CIDB contractor grading designation of **7 CE or 7 GB*** or higher.

** Delete "or select tender value range select class of construction works" where only one class of construction works is applicable*

It is estimated that potentially emerging enterprises should have a CIDB contractor grading designation of **select tender value range select class of construction works PE or select tender value range select class of construction works PE*** or higher.

** Delete "or select tender value range select class of construction works PE" where only one class of construction works is applicable*

2. FUNCTIONALITY CRITERIA APPLICABLE YES ☒ NO ☐

Note 1: Failure to meet minimum functionality score will result in the tenderer being disqualified.

Functionality criteria¹:	Weighting factor:

¹The points allocated to each functionality criterion should not be generic but should be determined separately for each tender on a case by case basis.

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

9.1 PROJECT WORK FORCE:

The bidders are to provide proof of the proposed Work Force in the form of a project organogram that will be employed for the duration of this project.

The proposal to include ALL of the following required Key Personnel listed below (If not, a score of ZERO will be given):

- (i) Construction Manager with a minimum qualification of a National Diploma or higher in Built Environment.
- (ii) Site Agent with a minimum qualification of Diploma in Built Environment.
- (iii) 2 x Plumbers (with a minimum NQF Level 1 or Higher or an Artisan Recognition of Prior Learning (ARPL)
- (iv) Process Controllers Class III, Class IV, and Class V (Supervisor) (All required)
- (v) 2 x Electricians
- (vi) 2 x Air- Conditioner Technicians
- (vii) Health and Safety Officer or Health and Safety Manager. Health and Safety Officer or Manager must be registered with SACPCMP as professionals.

NB: If any of the above services are to be sub-contracted, the bidder must attach the CSD report of the subcontractor(s) and should indicate the details of the subcontractor(s) on the DPW 15 (EC) and DPW 22 (EC) forms and submit all necessary documents for key personnel as listed below.

Bidders are to provide the following as listed below, for ALL above-mentioned key personnel (If not, a score of ZERO will be given):

- CVs of each key personnel to be involved in this project
- Copies of qualifications for all key personnel to be involved in this project.
- Trade certificates for Electricians, Plumbers, and Air - Conditioner Technicians.
- Copies of Certificates for Process Controllers.
- Construction Manager's proof of registration as a professional with SACPCMP or ECSA.
- Health and Safety Officer or Health and Safety Manager with proof of registration as a professional with SACPCMP as a Construction Health and Safety Officer or Construction Health and Safety Manager.

NB: All Certifications for key personnel should be valid or active.

1. More than 5 Years experience for each key personnel as listed above = 5 points
2. More than 4 - 5 Years experience for each key personnel as listed above = 4 points
3. More than 3 - 4 Years experience for each key personnel as listed above = 3 points
4. More than 2 - 3 Years experience for each key personnel as listed above = 2 points
5. 1 - 2 Years experience for each key personnel as listed above = 1 point

Insufficient information or less than 1 Year experience = 0 points

Notes: The service provider will receive points equal to the lowest years experience.

For example: If all key personnel have more than 5 Years, but one of the key personnel has more than 4 - 5 years experience, then a score of 4 will be allocated instead of a score of 5.

35

9.2 RELEVANT EXPERIENCE OF THE COMPANY: Bidders are to provide and submit a list of comparable projects of a similar nature and monetary value of CIDB Grade 6 and above with contactable references for repair and maintenance type projects currently engaged in and or completed during the past 10 years. Projects to be listed in DPW-09 (EC) form. For completed projects bidders are to submit together with the tender document completion certificates, and for current projects, bidders are to submit together with the tender document appointment letters. (i) Five or more completed/current projects = 5 points (ii) Four completed/current projects = 4 points (iii) Three completed/current projects = 3 points (iv) Two completed/current projects = 2 points (v) One completed/current project = 1 point No information submitted = 0 points	25
9.3 EQUIPMENT: The bidders are to provide evidence of cleaning equipment, hand tools, machinery, utility vehicles, and instrumentations owned or to be hired/rented in order to carry out the project. Bidders are to complete and sign ANNEXURE A for cleaning equipment, Instrumentations, hand tools, machinery, and utility vehicles. Bidders are to submit proof of equipment and hand tools owned or to be rented/hired from suppliers. Copies of vehicle(s) registrations must be submitted or agreement. An agreement between the bidder and supplier for rentals/hired items must be submitted. (You're required to submit your firm's asset register or agreement between bidder and supplier for rentals) i. Cleaning Equipments ii. Instrumentations iii. Utility vehicles iv. Machinery v. Hand tools 1. Information submitted for all five (5) items listed above = 5 points 2. Information submitted for any four (4) items listed above = 4 points 3. Information submitted for any three (3) items listed above = 3 points 4. Information submitted for any two (2) items listed above = 2 points 5. Information submitted for any one (1) item listed above = 1 point No information submitted = 0 points	15

9.4 BANK RATING The bidder to provide and submit an original bank stamped rating letter or certified copy of such a letter which is not older than 3 months on the closing date of the tender. i) Bank rating of A = 5 points ii) Bank rating of B = 4 points iii) Bank rating of C = 3 points iv) Bank rating of D = 2 points v) Bank rating of E = 1 point NB: Bidders will only be scored based on the banking rating submitted of (A,B,C,D or E). NB: If a stamped bank letter with no ratings (A,B,C,D or E) is provided , the bidder will receive 0 points. NB: In the case of JV, both bidders will need to submit their bank rating letters, and the JV will be scored the average points from the 2 scores, rounded off to the nearest whole number.	25
Total	100 Points

(Weights for functionality must add up to 100. Weightings will be multiplied by the scores allocated during the evaluation process to arrive at the total functionality points)

Minimum functionality score to qualify for further evaluation:	65

(Total minimum qualifying score for functionality is 50 Percent, any deviation below or above the 50 Percent, provide motivation below)

Land Ports of Entry are categorized as National Key Points, therefore any service provider appointed must meet the high quality standards in terms of performance and service delivery within the prescribed scope, time, cost, and quality.

3. THE FOLLOWING EVALUATION METHOD FOR RESPONSIVE BIDS WILL BE APPLICABLE:

☐ Method 1 (Financial offer)	☒ Method 2 (Financial and Preference offer)

3.1. Indicate which preference points scoring system is applicable for this bid:

☐ 80/20 Preference points scoring system	☒ 90/10 Preference points scoring system	☐ Either 80/20 or 90/10 Preference points scoring system

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

Page 4 of

4. RESPONSIVENESS CRITERIA

4.1. Indicate substantive responsiveness criteria applicable for this tender. Failure to comply with the criteria stated hereunder **shall** result in the tender offer being disqualified from further consideration:

1	☒	Only those tenderers who satisfy the eligibility criteria stated in the Tender Data may submit tenders.
2	☒	Tender offer must be properly received on the tender closing date and time specified on the invitation, completed either electronically (if issued in electronic format), or by writing legibly in non-erasable ink. (All as per Standard Conditions of Tender).
3	☒	Use of correction fluid is prohibited.
4	☒	Submission of a signed bid offer as per the DPW-07 (EC).
5	☐	Submission of DPW-09 (EC): Particulars of Tenderer's Projects.
6	☐	Bidders must comply with DPW-21 (EC): Record of Addenda to tender documents, if any.
7	☐	Submission of DPW-16 signed by the authorised official and completion of bid briefing attendance register.
8	☐	The tenderer shall submit his fully priced Bills of Quantities / Lump Sum Document (complete document inclusive of all parts) together with his tender.
9	☐	The tenderer shall submit his fully priced and completed sectional summary- and final summary pages with the tender.
10	☒	Bidders should be registered and active on CIDB with grading designated of 7CE or 7GB or higher at the closing date of the tender. In case of JV, all entities must be registered and active on CIDB.
11	☒	Attendance of compulsory briefing meeting and signing of the attendance register. Service Providers to familiarize themselves with the conditions of the site and the distance/road conditions to and from the site. This will enable them to submit a more realistic offer (tender) amount, therefore the clarification meeting is declared compulsory.
12	☒	The tenderer shall submit his/her fully priced Bills of Quantities (complete document inclusive of all parts) together with his/her tender. This project has now been classified as an emergency, and the urgent procurement of the follow-on RAMP project/contract is critical to ensure seamless and continuous implementation of the RAMP project. This will help avoid any gaps between the current and follow-on contracts, thereby maintaining the momentum and progress of the overall RAMP initiative.
13	☐	Specify other responsiveness criteria
14	☐	Specify other responsiveness criteria
15	☐	Specify other responsiveness criteria

4.2. Indicate administrative requirements applicable for this tender. Tenderers may be required to submit the below documents where applicable.

The Employer reserves the right to request further information regarding the undermentioned criteria. Failing to submit further clarification and/or documentation within seven (7) calendar days from request or as specifically indicated, will disqualify the tender offer from further consideration.

1	☒	Any correction to be initialled by the person authorised to sign the tender documentation as per PA 15.1 or PA 15.2 resolution of board/s of directors / or PA15.3 Special Resolution of Consortia or JV's.
2	☒	Submission of applicable (PA-15.1, PA-15.2, PA-15.3): Resolution by the legal entity, or consortium / joint venture, authorising a dedicated person(s) to sign documents on behalf of the firm / consortium / joint venture.
3	☒	All parts of tender documents submitted must be fully completed in ink and signed where required.
4	☒	Submission of (PA-11): Bidder's disclosure
5	☒	Submission of PA-16.1 (EC): Ownership Particulars
6	☒	Submission of documentation relating to risk assessment criteria as contained in C 2.1 of DPW-03 Tender Data.
7	☒	Submission of (PA 40): Declaration of Designated Groups.
8	☒	Submission of proof of Registration on National Treasury's Central Supplier Database (CSD). Insert the Supplier Registration Number on the form of offer, including proposed sub-contractors if any
9	☒	Data provided by the tenderer in Part 2 of DPW-04 Contract Data (JBCC 2018) or DPW-05 Contract Data (GCC 2015) whichever applicable to be fully completed.
10	☐	The tenderer shall submit his fully priced Bills of Quantities (complete document inclusive of all parts) within 14 calendar days from request.
11	☒	Upon request, submission of fingerprints obtainable from local SAPS including any other additional documentation and information required for vetting purposes.
12	☒	Upon request, submission of a fully completed security clearance application form with supporting documentation and information as required. The security clearance form will be provided by the Employer for projects requiring a security clearance.
13	☒	Submission of DPW- 09 (EC): Particulars of Tenderer's Projects
14	☒	Bidders must comply with DPW-21 (EC): Record of Addenda to tender documents, if any
15	☒	Submission of DPW-16 signed (Site inspection meeting certificate) by the authorised official and completion of bid briefing attendance register.
16	☒	Role players of references to be indicated in the DPW- 09 (EC) Particulars of Tender's Projects should be User Clients, Consultants and Principals agents. Only contactable reference numbers to appear in the DPW-09 (EC) form.
17	☒	Sworn affidavit for the full-time employment of work force for the duration of the project, indicating clearly that similar qualified personnel will be employed after award of the tender if personnel are lost due to any reason.
18	☒	Submission of copies of Identity Documents for all key personnel who will be involved in this project and the submission of registration certificates for Construction Manager , Health and Safety Officer and or Safety Manager from SACPCMP or ECSA.

4.3. Indicate administrative requirements applicable for specific goals, Tenderers will not be required to submit the below document if not provided in the original tender proposals, Failure to comply with the criteria stated hereunder shall result in the tenderer not allocated points for specific goals.

1	☒	Submission of (PA-16): Preference Points Claim Form in terms of the Preferential Procurement Regulations 2022
2	☒	A trust, consortium or joint venture (including unincorporated consortia and joint ventures) must submit a consolidated B-BBEE Certificate issued by a SANAS accredited service provider

5. METHOD TO BE USED TO CALCULATE POINTS FOR SPECIFIC GOALS:



5.1. For procurement transaction with rand value greater than R1 Million and up to R50 Million (Inclusive of all applicable taxes) the specific goals listed in table 1 below are applicable.

Table 1

Serial No	Specific Goals	Preference Points Allocated out of 20	Documentation to be submitted by bidders to validate their claim
1.	An EME or QSE which is at least 51% owned by black people (Mandatory)	10	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be done or services to be rendered in that area (Mandatory)	2	- Official Municipal Rates Statement which is in the name of the bidder. Or - Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder. Or - Lease Agreement which is in the name of the bidder.
3.	An EME or QSE or any entity which is at least 51% owned by black women (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
4.	An EME or QSE or any entity which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent. Or - South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or National Council for Persons with Physical Disability in South Africa registration (NCPDSA).

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

5.	An EME or QSE or any entity which is at least 51% owned by black youth (Mandatory)	2	ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.

8.2. For procurement transaction with rand value greater than R50 Million (Inclusive of all applicable taxes) the specific goals listed in table 2 below are applicable.



NB. The use of one of goal numbers' 4 or 5 is mandatory. The BSC must select either one of the two, but not both.

Table 2

Serial No	Specific Goals	Preference Points Allocated out of 10	Documentation to be submitted by bidders to validate their claim
1.	An EME or QSE or any entity which is at least 51% owned by black people (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be done or services to be rendered in that area (Mandatory)	2	- Official Municipal Rates Statement which is in the name of the bidder. Or - Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder. Or - Lease Agreement which is in the name of the bidder.
3.	An EME or QSE or any entity which is at least 51% owned by black women (mandatory)	2	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
4. ☐	An EME or QSE or any entity which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent.

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

Page 8 of

	OR			Or South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).
		5. ☒ An EME or QSE or any entity which is at least 51% owned by black youth (Mandatory)	2	ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.

Black people mean Africans, Coloureds and Indians, who - (a) are citizens of the Republic of South Africa by birth or descent; or (b) became citizens of the Republic of South Africa by naturalisation - (i) before 27 April 1994; or (ii) on or after 27 April 1994 and who would have been entitled to acquire citizenship by naturalisation prior to that date. (BROAD-BASED BLACK ECONOMIC EMPOWERMENT ACT No 25899, 2003 of 9 JANUARY 2004).

6. BID EVALUATION METHOD

This bid will be evaluated according to the preferential procurement model in the PPPFA: (Tick applicable preference point scoring system)

☐ 80/20 Preference points scoring system	☒ 90/10 Preference points scoring system	☐ Either 80/20 or 90/10 Preference points scoring system

In case where below/above R 50 000 000 is selected, the lowest acceptable tender will be used to determine the applicable preference point system.

7. ELIGIBILITY IN RESPECT OF RISK TO THE EMPLOYER:

Standard risk management assessment criteria in respect of tenders received for routine projects in the engineering and construction works environments:

Tender offers will be evaluated by an Evaluation Committee based on the technical and commercial risk criteria listed hereunder. Each criterion carries the same weight / importance and will be evaluated individually based on reports presented to the Bid Evaluation Committee by the Professional Team appointed on the project. A tender offer will be declared non-responsive and removed from any further evaluation if any one criterion is found to present an unacceptable risk to the Employer.

In order for the evaluation reports to be prepared by the Professional Team, the Tenderer is obliged to provide comprehensive information on form DPW-09 (EC). Failure to complete the said form will cause the tender to be declared non-responsive and removed from any further consideration. The Employer reserves the right to request additional information over and above that which is provided by the Tenderer on said form. The information must be provided by the Tenderer within the stipulated time as determined by the Bid Evaluation Committee, failing which the tender offer will *mutatis mutandis* be declared non-responsive.

7.1 Technical risks:

Criterion 1: Experience on comparable projects during the past 10 years.

The tendering Service Provider's experience on comparable projects during the past 10 years. The number of current and previous comparable projects performed by the Tenderer as per the evaluation report prepared by the Consultant Team, based on its research and inspection of a representative sample of the Tenderer's current and previous work as reflected on form DPW-09 (EC), as well as, if necessary, of any additional work executed by the Tenderer, not reflected on form DPW-09 (EC). Failing to provide contactable references will result in the tender offer will be *mutatis mutandis* declared non-responsive.

Aspects to be regarded as "comparable" includes (but may be extended according to circumstances): size of projects (measured against monetary value or other project quantifying parameters), nature of projects (building, engineering, high/low rise, etc.), locality/area of execution (site-specific influences, knowledge of local conditions, etc.), complexity of project, projects for similar client department irrespective of end purpose of buildings/facilities created or in progress of being created and time scales of projects (normal, fast track, etc.) and stage of its/their development.

Criterion 2: Contractual commitment and quality of performance on comparable projects during the past 10 years.

Adherence to contractual commitments and quality of performance of comparable current and previous projects performed by the Tenderer during the past 10 years as per the evaluation report prepared by the Consultant Team, based on its research and inspection of a representative sample of the Tenderer's current and previous work as reflected on form DPW-09 (EC), as well as, if necessary, of any additional work executed by the Tenderer, not reflected on form DPW-09 (EC). Failing to provide contactable references will result in the tender offer be *mutatis mutandis* declared non-responsive.

Aspects to be considered include, but are not limited to the following:

1. The level of progress on current projects in relation to the project programme or, if such is not available/applicable, to the contractual construction period in general;
2. The degree to which previous projects have been completed within the contractual completion periods and/or extensions thereto, and the extend of penalties imposed;
3. Project performance: time management & programming of works, timeous ordering of materials and appointment of subcontractors;
4. Financial management: payment to suppliers and cash flow problems;
5. Quality of workmanship: extent of reworks and timeous attention to remedial works;
6. Personnel resources: suitably qualified and experienced, turnover in site staff and labour force, specifically site manager and foreman;
7. Personnel management: extent of labour disputes and ability to resolving labour disputes amicably;
8. Sub-contractors: extent of turnover in subcontractors, general liaison and payment problems experienced;
9. Contract administration: contractual aspects such as complying to laws and regulations, insurances, security, submission of required documentation timeously, reaction to written contract instructions, appointments of subcontractors, etc. as can generally be expected in standard/normal conditions of contract.
10. Health & Safety: adherence to regulations and compliance, and number of transgressions & serious incidents.
11. Plant & equipment: sufficient resources on site and in time.
12. Delays: extent of causing delays, submission of claims timeously, and abuse of or exaggerated delay claims.
13. Final account: extent to which the contractor assisted in finalising the final account.

Criterion 3: Suitably qualified and appropriately experienced human resources

Allocation of suitably qualified and appropriately experienced human resources, both in respect of principals and/or other staff (contract manager, site agent, site foreman including other professional, technical and/or administrative) of the tendering Service Provider to the project, as proof that the tendering Service Provider will be able to react/respond appropriately to the Services required herein. The Company Organogram with CV's and certified ID's of all principals and employed workforce as well as proof of Professional Registration

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

will be verified. Current and future workload of the tenderer in relation to capacity and capability will also be considered. The tenderer should demonstrate that he or she possesses the necessary professional and technical qualifications and -competence in relation to the scope of work and work to be undertaken.

Criterion 4: Attendance of compulsory bid clarification meeting, if applicable

If applicable, submission of confirmation of DPW-16.1 (PSB) attendance of compulsory bid clarification meeting or proof of attending the compulsory virtual meeting by a suitably qualified and experienced representative of the tenderer in terms of PA-04 (EC): Notice and Invitation to Tender.

7.2 Commercial risks:

The financial viability assessment evaluates the risk over the life of the construction period, as to whether the tenderer will be able to deliver the goods and services which are specified in the contract and / or be able to fulfil guarantees or warranties provided for in the contract in order to complete the project successfully for the amount tendered.

Aspects to be considered include but are not limited to, the respective rates tendered, bank rating, financial capability and capacity whether the tenderer has or has access to sufficient financial resources to deliver the goods or services described in the tender documentation (including fulfilling any guarantees or warranty claims), whether the tenderer is not subject to any current or impending legal action (either formal proceedings or notification of legal action) which could impact on the financial standing of the tenderer or the delivery of the goods or services, financial report from auditors as proof of current liquidity, and company or any parent company or investor guarantee/s and financial statements.

8. CONTRACT PARTICIPATION GOAL TARGETS AND CIDB B.U.I.L.D. PROGRAMME

The contractor shall achieve in the performance of the contract the following Contract Participation Goals (CPGs) as described in PG-01.2 (EC): Scope of Work and PG-02.2 (EC): Pricing Assumptions and in accordance with the feasibility study, which forms part of the specifications in the CPG Section of the Specification of this contract.

(a)	Minimum Targeted Local Manufacturers of Material Contract Participation Goal, in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	Applicable
(b)	Minimum Targeted Local Building Material Suppliers Contract Participation Goal in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	Applicable
(c)	Minimum Targeted Local Labour Skills Development Contract Participation Goal in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	Applicable
(d)	cidb BUILD Programme: Minimum Targeted Enterprise Development Contract Participation Goal in accordance with the cidb Standard for Indirect Targeting for Enterprise Development through Construction Works Contracts, No 36190 Government Gazette, 25 February 2013, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	Applicable

(e)	cidb BUILD Programme: Minimum Targeted Local Labour Skills Development Contract Participation Goal in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 48491 of 28 April 2023 and the cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.– Condition of Contract	Applicable
(f)	DPWI National Youth Service training and development programme (NYS) – Condition of Contract.	Not applicable
(g)	Labour Intensive Works – Condition of Contract. (Applicable to all CE projects and all GB Projects ≥ R 30 million where applicable.)	Applicable
(h)		Select
(i)		Select

9. COLLECTION OF TENDER DOCUMENTS

☒ Bid documents are available for free download on Departmental website (www.publicworks.gov.za) and on e-Tender portal (www.etenders.gov.za)

☒ Alternatively; Bid documents may be collected during working hours at the following address 256 Madiba Street, Central Government Offices (CGO). A non-refundable bid deposit of R 800.00 is payable (cash only) on collection of the bid documents.

10. SITE INSPECTION MEETING

A pre-tender site inspection meeting will **be** held in respect of this tender.
Attendance of said pre- tender site inspection meeting is **compulsory**

The particulars for said pre- tender site inspection meeting or virtual bid clarification / site inspection meeting. are:

Venue:	Vioolsdrift LPoE		
Virtual meeting link:	N/A		
Date:	02 September 2025	Starting time:	11:00 am

11. ENQUIRIES

11.1. Technical enquiries may be addressed to:

DPWI Project Manager	Mr. Herman Sagner	Telephone no:	(012) 406 1122
Cellular phone no	082 908 0577	Fax no:	N/A
E-mail	herman.sagner@dpw.gov.za		

11.2. SCM enquiries may be addressed to:

SCM Official	Mr. Tsebisio Molatudi	Telephone no:	(012) 406 1374
Cellular phone no	072 344 7516	Fax no:	N/A
E-mail	tsebisio.molatudi@dpw.gov.za		

12. DEPOSIT / RETURN OF TENDER DOCUMENTS

Telegraphic, telephonic, telex, facsimile, electronic and / or late tenders will not be accepted.

Requirements for sealing, addressing, delivery, opening and assessment of tenders are stated in the Tender Data.

All tenders must be completed in non-erasable ink and submitted on the official forms – (forms not to be re-typed).

Tender documents may be posted to: The Director-General Department of Public Works and Infrastructure Private Bag X 65 Pretoria 0001 Attention: Procurement section: Room 121	OR	Deposited in the tender box at: 256 Madiba Street Central Government Offices (CGO) Madiba Street 121

DPW-03 (EC): TENDER DATA

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)
Reference no:	WCS 056397

Tender / Quotation no:	H25/008 AI	Closing date:	15 September 2025
Closing time:	11:00	Validity period:	12 Weeks (84 Calendar days)

Clause number:	
	The conditions of tender are the Standard Conditions of Tender as contained in Annex C of the CIDB Standard for Uniformity in Construction Procurement as per Government Notice No. 423 published in Government Gazette No. 42622 of 8 August 2019 and as amended from time to time. (see www.cidb.org.za). The Standard Conditions of Tender make several references to the Tender Data for details that apply specifically to this tender. The Tender Data shall have precedence in the interpretation of any ambiguity or inconsistency between it and the Standard Conditions of Tender. Each item of data given below is cross-referenced to the clause marked "C" in the above mentioned Standard Conditions of Tender.
C.1.1	The employer is the Government of the Republic of South Africa in its Department of Public Works and Infrastructure.
C.1.2	For this contract the three volume approach is adopted. This procurement document has been formatted and compiled under the headings as contained in the CIDB's "Standard for Uniformity in Construction Procurement." The three volume procurement document issued by the employer comprises the following: Volume 1: Tendering procedures T1.1 - Notice and invitation to tender (PA-04 EC) T1.2 - Tender data (DPW-03 EC) Volume 2: Returnable documents T2.1 - List of returnable documents (PA-09 EC) C1.1 - Form of offer and acceptance (DPW-07 EC) C1.2 – Contract Data T2.2 - Returnable schedules Volume 3: Contract Part C1: Agreement and contract data C1.2 - Contract data (Part 1: Data provided by employer) (DPW-04 EC or DPW-05 EC) C1.3 - Form of guarantee (DPW-10.1 EC / DPW-10.3EC or DPW-10.2 EC/DPW-10.4 EC) Part C2: Pricing data C2.1 - Pricing Assumptions (PG-02.2 EC or PG-02.1EC) C2.2 - Bills of Quantities / Lump sum document (if not a returnable document) Part C3: Scope of work C3 - Scope of work (PG-01.2 EC or PG-01.1EC) Part C4: Site information C4 - Site information (PG-03.2 EC or PG03.1EC)

Tender no: H25/008 AI

C.1.4	The Employer's agent is:	
	Name:	Mr Antony Marunga
	Capacity:	Private Project Manager
	Address:	Prociv-KNA JV Unit 6, CMA Office and Conference Park No.1 2nd Road, Halfway House Estate Midrand 1685
	Tel:	011 656 9473
	Fax:	N/A
	E-mail:	amarunga@prociv.co.za

C.2.1 C.3.11	A. <u>ELIGIBILITY IN RESPECT OF CIDB REGISTRATION:</u>
	The following tenderers who are registered with the CIDB, or are *capable of being so registered prior to the evaluation of submissions, are eligible to have their tenders evaluated (* tenderers who are capable of being so registered, or who have applied for registration but have not yet received confirmation of such registration, must provide, <u>with this tender</u>, acceptable documentary proof thereof): a) contractors who have a contractor grading designation equal to or higher than a contractor grading designation determined in accordance with the sum tendered, or a value determined in accordance with Regulation 25 (1B) or 25 (7A) of the Construction Industry Development Regulations, for a 7 CE or 7 GB** class of construction work; and b) contractors registered as potentially emerging enterprises with the CIDB who are registered in one contractor grading designation lower than that required in terms of a) above: Not applicable Joint ventures are eligible to submit tenders provided that: 1. every member of the joint venture is registered with the CIDB; 2. the lead partner has a contractor grading designation in the 7 CE or 7 GB** class of construction work; and 3. the combined contractor grading designation calculated in accordance with the Construction Industry Development Regulations is equal to or higher than a contractor grading designation determined in accordance with the sum tendered, or a value determined in accordance with Regulation 25 (1B) or 25 (7A) of the Construction Industry Development Regulations for a 7 CE or 7 GB** class of construction work ** Delete "or select tender value range select class of construction works" where only one class of construction works is applicable
A contract will be entered into with a tenderer who has in his employ management and supervisory staff satisfying the requirements of the scope of work for labour intensive competencies for supervisory and management staff: Applicable	

Tender no: H25/008 AI

C. FUNCTIONALITY WEIGHTING APPLICABLE TO THIS BID:

Note: Failure to meet minimum functionality score will result in the tenderer being disqualified.

Functionality Criteria	Weighting Factor
9.1 PROJECT WORK FORCE: The bidders are to provide proof of the proposed Work Force in the form of a project organogram that will be employed for the duration of this project. The proposal to include ALL of the following required Key Personnel listed below (If not, a score of ZERO will be given): (i) Construction Manager with a minimum qualification of a National Diploma or higher in Built Environment. (ii) Site Agent with a minimum qualification of Diploma in Built Environment. (iii) 2 x Plumbers (with a minimum NQF Level 1 or Higher or an Artisan Recognition of Prior Learning (ARPL) (iv) Process Controllers Class III, Class IV, and Class V (Supervisor) (All required) (v) 2 x Electricians (vi) 2 x Air- Conditioner Technicians (vii) Health and Safety Officer or Health and Safety Manager. Health and Safety Officer or Manager must be registered with SACPCMP as professionals. NB: If any of the above services are to be sub-contracted, the bidder must attach the CSD report of the subcontractor(s) and should indicate the details of the subcontractor(s) on the DPW 15 (EC) and DPW 22 (EC) forms and submit all necessary documents for key personnel as listed below. Bidders are to provide the following as listed below, for ALL above-mentioned key personnel (If not, a score of ZERO will be given): • CVs of each key personnel to be involved in this project • Copies of qualifications for all key personnel to be involved in this project. • Trade certificates for Electricians, Plumbers, and Air - Conditioner Technicians. • Copies of Certificates for Process Controllers. • Construction Manager's proof of registration as a professional with SACPCMP or ECSA. • Health and Safety Officer or Health and Safety Manager with proof of registration as a professional with SACPCMP as a Construction Health and Safety Officer or Construction Health and Safety Manager. NB: All Certifications for key personnel should be valid or active. 1. More than 5 Years experience for each key personnel as listed above = 5 points 2. More than 4 - 5 Years experience for each key personnel as listed above = 4 points	35

	3. More than 3 - 4 Years experience for each key personnel as listed above = 3 points 4. More than 2 - 3 Years experience for each key personnel as listed above = 2 points 5. 1 - 2 Years experience for each key personnel as listed above = 1 point Insufficient information or less than 1 Year experience = 0 points Notes: The service provider will receive points equal to the lowest years experience. For example: If all key personnel have more than 5 Years, but one of the key personnel has more than 4 - 5 years experience, then a score of 4 will be allocated instead of a score of 5.	
	9.2 RELEVANT EXPERIENCE OF THE COMPANY: Bidders are to provide and submit a list of comparable projects of a similar nature and monetary value of CIDB Grade 6 and above with contactable references for repair and maintenance type projects currently engaged in and or completed during the past 10 years. Projects to be listed in DPW-09 (EC) form. For completed projects bidders are to submit together with the tender document completion certificates, and for current projects, bidders are to submit together with the tender document appointment letters. (i) Five or more completed/current projects = 5 points (ii) Four completed/current projects = 4 points (iii) Three completed/current projects = 3 points (iv) Two completed/current projects = 2 points (v) One completed/current project = 1 point No information submitted = 0 points	25
	9.3 EQUIPMENT: The bidders are to provide evidence of cleaning equipment, hand tools, machinery, utility vehicles, and instrumentations owned or to be hired/rented in order to carry out the project. Bidders are to complete and sign ANNEXURE A for cleaning equipment, Instrumentations, hand tools, machinery, and utility vehicles. Bidders are to submit proof of equipment and hand tools owned or to be rented/hired from suppliers. Copies of vehicle(s) registrations must be submitted or agreement. An agreement between the bidder and supplier for rentals/hired items must be submitted. (You're required to submit your firm's asset register or agreement between bidder and supplier for rentals) i. Cleaning Equipments ii. Instrumentations iii. Utility vehicles iv. Machinery v. Hand tools 1. Information submitted for all five (5) items listed above = 5 points	15

	2. Information submitted for any four (4) items listed above = 4 points 3. Information submitted for any three (3) items listed above = 3 points 4. Information submitted for any two (2) items listed above = 2 points 5. Information submitted for any one (1) item listed above = 1 point No information submitted = 0 points	
	9.4 BANK RATING The bidder to provide and submit an original bank stamped rating letter or certified copy of such a letter which is not older than 3 months on the closing date of the tender. i) Bank rating of A = 5 points ii) Bank rating of B = 4 points iii) Bank rating of C = 3 points iv) Bank rating of D = 2 points v) Bank rating of E = 1 point NB: Bidders will only be scored based on the banking rating submitted of (A,B,C,D or E). NB: If a stamped bank letter with no ratings (A,B,C,D or E) is provided , the bidder wil receive 0 points. NB: In the case of JV, both bidders will need to submit their bank rating letters, and the JV will be scored the average points from the 2 scores, rounded off to the nearest whole number.	25
	Total	100 Points
(Weightings will be multiplied by the scores allocated during the evaluation process to arrive at the total functionality points)		
Minimum functionality score to qualify for further evaluation:		65

☐	D. METHOD TO BE USED TO CALCULATE POINTS FOR SPECIFIC GOALS			
	D1. For procurement transaction with rand value greater than R2 000,00 and up to R1 Million (Inclusive of all applicable taxes) the specific goals listed below are applicable.			
	Table 1			
	Serial No	Specific Goals	Preference Points Allocated out of 20	Documentation to be submitted by bidders to validate their claim
1.	An EME or QSE which is at least 51% owned by black people (Mandatory)	10	• SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.	
2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be	2	• Official Municipal Rates Statement which is in the name of the bidder.	

	done or services to be rendered in that area (Mandatory)		Or - Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder. Or - Lease Agreement which is in the name of the bidder.
3.	An EME or QSE which is at least 51% owned by black women (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
4.	An EME or QSE which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent. Or - South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or - National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).
5.	An EME or QSE which is at least 51% owned by black youth (Mandatory)	2	ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.

☐
D2. For procurement transaction with rand value greater than R1 Million and up to R50 Million (Inclusive of all applicable taxes) the specific goals listed in table 1 below are applicable.

Table 2

Serial No	Specific Goals	Preference Points Allocated out of 20	Documentation to be submitted bidders to validate their claim
1.	An EME or QSE or any entity which is at least 51% owned by black people (Mandatory)	10	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.

	2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be done or services to be rendered in that area (Mandatory)	2	- Official Municipal Rates Statement which is in the name of the bidder Or - Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder Or - Lease Agreement which is in the name of the bidder.	
	3.	An EME or QSE or any entity which is at least 51% owned by black women (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.	
	4.	An EME or QSE or any entity which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent. Or - South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).	
	5.	An EME or QSE or any entity which is at least 51% owned by black youth (Mandatory)	2	ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.	

☒

D3. For procurement transaction with rand value greater than R50 Million (Inclusive of all applicable taxes) the specific goals listed in table 2 below are applicable.

NB. The use of one of goal numbers' 4 or 5 is mandatory. The BSC must select either one of the two, but not both.

Table 3

Serial No	Specific Goals	Preference Points Allocated out of 10	Documentation to be submitted in bidders to validate their claim

	1.	An EME or QSE or any entity which is at least 51% owned by black people (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.	
	2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be done or services to be rendered in that area (Mandatory)	2	- Official Municipal Rates Statement which is in the name of the bidder. Or - Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder. Or - Lease Agreement which is in the name of the bidder.	
	3.	An EME or QSE or any entity which is at least 51% owned by black women (mandatory)	2	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.	
	4. ☒	An EME or QSE or any entity which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent. Or - South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).	
	OR				
	5. ☒	An EME or QSE or any entity which is at least 51% owned by black youth (Mandatory)	2	ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.	

Black people mean Africans, Coloureds and Indians, who - (a) are citizens of the Republic of South Africa by birth or descent; or (b) became citizens of the Republic of South Africa by naturalisation - (i) before 27 April 1994; or (ii) on or after 27 April 1994 and who would have been entitled to acquire citizenship by naturalisation prior to that date. (BROAD-BASED BLACK ECONOMIC EMPOWERMENT ACT No 25899, 2003 of 9 JANUARY 2004).

Tender no: H25/008 AI

E. ELIGIBILITY IN RESPECT OF RISK TO EMPLOYER:

Standard risk management assessment criteria in respect of tenders received for routine projects in the engineering and construction works environments:

Tender offers will be evaluated by an Evaluation Committee based on the technical and commercial risk criteria listed hereunder. Each criterion carries the same weight / importance and will be evaluated individually based on reports presented to the Bid Evaluation Committee by the Professional Team appointed on the project. A tender offer will be declared non-responsive and removed from any further evaluation if any one criterion is found to present an unacceptable risk to the Employer.

In order for the evaluation reports to be prepared by the Professional Team, the Tenderer is obliged to provide comprehensive information on form DPW-09 (EC). Failure to complete the said form will cause the tender to be declared non-responsive and removed from any further consideration. The Employer reserves the right to request additional information over and above that which is provided by the Tenderer on said form. The information must be provided by the Tenderer within the stipulated time as determined by the Bid Evaluation Committee, failing which the tender offer will *mutatis mutandis* be declared non-responsive.

E.1 Technical risks:

Criterion 1: Experience on comparable projects during the past 10 years.

The tendering Service Provider's experience on comparable projects during the past 10 years. The number of current and previous comparable projects performed by the Tenderer as per the evaluation report prepared by the Consultant Team, based on its research and inspection of a representative sample of the Tenderer's current and previous work as reflected on form DPW-09 (EC), as well as, if necessary, of any additional work executed by the Tenderer, not reflected on form DPW-09 (EC). Failing to provide contactable references will result in the tender offer will be *mutatis mutandis* declared non-responsive.

Aspects to be regarded as "comparable" includes (but may be extended according to circumstances): size of projects (measured against monetary value or other project quantifying parameters), nature of projects (building, engineering, high/low rise, etc.), locality/area of execution (site-specific influences, knowledge of local conditions, etc.), complexity of project, projects for similar client department irrespective of end purpose of buildings/facilities created or in progress of being created and time scales of projects (normal, fast track, etc.) and stage of its/their development.

Criterion 2: Contractual commitment and quality of performance on comparable projects during the past 10 years.

Adherence to contractual commitments and quality of performance of comparable current and previous projects performed by the Tenderer on comparable projects during the past 10 years as per the evaluation report prepared by the Consultant Team, based on its research and inspection of a representative sample of the Tenderer's current and previous work as reflected on form DPW-09 (EC), as well as, if necessary, of any additional work executed by the Tenderer, not reflected on form DPW-09 (EC). Failing to provide contactable references will result in the tender offer be *mutatis mutandis* declared non-responsive.

Aspects to be considered include, but are not limited to the following:

1. The level of progress on current projects in relation to the project programme or, if such is not available/applicable, to the contractual construction period in general;
2. The degree to which previous projects have been completed within the contractual completion periods and/or extensions thereto, and the extend of penalties imposed;

Tender no: H25/008 AI

	3. Project performance: time management & programming of works, timeous ordering of materials and appointment of subcontractors; 4. Financial management: payment to suppliers and cash flow problems; 5. Quality of workmanship: extent of reworks and timeous attention to remedial works; 6. Personnel resources: suitably qualified and experienced, turnover in site staff and labour force, specifically site manager and foreman; 7. Personnel management: extent of labour disputes and ability to resolving labour disputes amicably; 8. Sub-contractors: extent of turnover in subcontractors, general liaison and payment problems experienced; 9. Contract administration: contractual aspects such as complying to laws and regulations, insurances, security, submission of required documentation timeously, reaction to written contract instructions, appointments of subcontractors, etc. as can generally be expected in standard/normal conditions of contract. 10. Health & Safety: adherence to regulations and compliance, and number of transgressions & serious incidents. 11. Plant & equipment: sufficient resources on site and in time. 12. Delays: extent of causing delays, submission of claims timeously, and abuse of or exaggerated delay claims. 13. Final account: extent to which the contractor assisted in finalising the final account. Criterion 3: Suitably qualified and appropriately experienced human resources Allocation of suitably qualified and appropriately experienced human resources, both in respect of principals and/or other staff (contract manager, site agent, site foreman including other professional, technical and/or administrative) of the tendering Service Provider to the project, as proof that the tendering Service Provider will be able to react/respond appropriately to the Services required herein. The Company Organogram with CV's and certified ID's of all principals and employed workforce as well as proof of Professional Registration will be verified. Current and future workload of the tenderer in relation to capacity and capability will also be considered. The tenderer should demonstrate that he or she possesses the necessary professional and technical qualifications and -competence in relation to the scope of work and work to be undertaken. Criterion 4: Attendance of compulsory bid clarification meeting, if applicable If applicable, submission of confirmation of DPW-16.1 (PSB) attendance of compulsory bid clarification meeting or proof of attending the compulsory virtual meeting by a suitably qualified and experienced representative of the tenderer in terms of PA-04 (EC): Notice and Invitation to Tender. E.2 Commercial risks: The financial viability assessment evaluates the risk over the life of the construction period, as to whether the tenderer will be able to deliver the goods and services which are specified in the contract and / or be able to fulfil guarantees or warranties provided for in the contract in order to complete the project successfully for the amount tendered. Aspects to be considered include but are not limited to, the respective rates tendered, bank rating, financial capability and capacity whether the tenderer has or has access to sufficient financial resources to deliver the goods or services described in the tender documentation (including fulfilling any guarantees or warranty claims), whether the tenderer is not subject to any current or impending legal action (either formal proceedings or notification of legal action) which could impact on the financial standing of the tenderer or the delivery of the goods or services, financial report from auditors as proof of current liquidity, and company or any parent company or investor guarantee/s and financial statements.
C.2.7	For particulars regarding a pre-tender site inspection meeting, see Notice and Invitation to Tender T1.1

Tender no: H25/008 AI

C.2.12	If a tenderer wishes to submit an alternative tender offer, the only criteria permitted for such alternative tender offer is that it demonstrably satisfies the Employer's standards and requirements. A tenderer may submit alternative tender offers only if a main tender offer, strictly in accordance with all the requirements of the tender documents, is also submitted. Provided that the tenderer's main tender offer is according to specification and would under normal circumstances be recommended for acceptance, his alternative tender offer may also be considered for the purpose of the award of the contract. Calculations, drawings and all other pertinent technical information and characteristics as well as modified or proposed Pricing Data must be submitted with the alternative tender offer to enable the Employer to evaluate the efficacy of the alternative and its principal elements, to take a view on the degree to which the alternative complies with the Employer's standards and requirements and to evaluate the acceptability of the pricing proposals. Calculations must be set out in a clear and logical sequence and must clearly reflect all design assumptions. Pricing Data must reflect all assumptions in the development of the pricing proposal. Acceptance of an alternative tender offer will mean acceptance in principle of the offer. It will be an obligation of the contract for the tenderer, in the event that the alternative is accepted, to accept full responsibility and liability that the alternative offer complies in all respects with the Employer's standards and requirements. The modified Pricing Data must include an amount equal to 5% of the amount tendered for the alternative offer to cover the Employer's costs of confirming the acceptability of the detailed design before it is constructed. Alternative tender offer permitted: Yes ☐ No ☒
C.2.13.2	The list of Returnable Documents identifies which of the documents a tenderer must complete when submitting a tender offer. The tenderer must submit his tender offer by completing the Returnable Documents, signing the "Offer" section in the "Form of Offer and Acceptance" and delivering the Returnable Documents back to the Department.
C.2.13.5	The Employer's address for delivery of tender offers and identification details to be shown on each tender offer package are as per Notice and Invitation to Tender T1.1.
C.2.13.6 C.3.5	A two-envelope procedure will not be followed.
C.2.15	The closing time for submission of tender offers is as per Notice and Invitation to Tender T1.1.
C.2.16	The tender offer validity period is as per Notice and Invitation to Tender T1.1.
C2.16.3	Omit the wording of the last sentence for those projects which are subject to CPAP
C.2.18	The tenderer will be required to submit his fully priced Bills of Quantities / Lump Sum Document (complete document inclusive of all parts): ☒ Together with his tender; or ☐ The tenderer shall submit his fully priced and completed sectional summary- and final summary pages with the tender and thereafter submit the fully completed Bills of Quantities within fourteen (14) calendar days of the date requested to do so prior to the award of the contract.
C.2.19	Access shall be provided for inspections, tests and analysis as may be required by the Employer.
C.3.4.1 C.3.4.2	The location for opening of the tender offers, immediately after the closing time thereof shall be at: Central Government Offices, cnr Bosman and Madiba Streets, Room 121, 1ST Floor, Pretoria, 0001
C.3.8	The words "responsive tender" and "acceptable tender" shall be construed to have the same meaning.

Tender no: H25/008 AI

C.3.9.3	Omit the wording and replace with the following: “Notify the tenderer of all errors, omissions and/or rate imbalances that are identified in the tender offer and request the tenderer to, within a stipulated time, accept the total of prices as corrected in accordance with C.3.9.4.”
C.3.9.4	Omit the wording of the first sentence and replace with the following: “In cases where tender offers contain errors, omissions and/or rate imbalances, these are to be corrected as follows:”
C.3.9.4	Add sub paragraph c) to C.3.9.4, as follows: “c) If the tenderer does not accept the corrected tender offer, or cannot reach consensus with the Employer on a corrected tender offer, the tender is to be classified as not acceptable/non responsive and removed from further contention.”
C.3.11.1	The procedure for the evaluation of responsive tenders is Method 2: Financial Offer and Preference.
C.3.13	Add the following to sub paragraph a), as follows: The tenderer or any of its directors is not listed on the Register of Tender Defaulters in terms of the Prevention and Combating of Corrupt Activities Act, 2004 (Act No. 12 of 2004) as a person prohibited from doing business with the public sector;
C.3.17	Provide to the successful tenderer one copy of the signed contract document.

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

PART T2 RETURNABLE DOCUMENTS

PA-09 (EC): LIST OF RETURNABLE DOCUMENTS

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender / Quotation no:	H25/008 AI	Reference no:	WCS 056397
Receipt Number:			

1. RETURNABLE DOCUMENTS REQUIRED FOR TENDER EVALUATION PURPOSES

Note: Failure to submit the applicable documents will result in the tender offer being disqualified from further consideration.

Tender document name	Number of pages issued	Returnable document
Form of Offer and Acceptance (DPW-07 EC)	4 Pages	Yes
Submission of Bidder's disclosure (PA-11)	3 Pages	Yes
Resolution of Board of Directors (PA-15.1) <i>(if applicable)</i>	1 Page	Yes
Resolution of Board of Directors to enter into Consortia or JV's (PA-15.2) <i>(if applicable)</i>	2 Pages	Yes
Special Resolution of Consortia or JV's (PA-15.3) <i>(if applicable)</i>	3 Pages	Yes
Preference points claim form in terms of the Preferential Procurement Regulations 2017 (PA – 16.1)	5 Pages	Yes
Declaration Certificate for Local Production and Content for designated sectors (PA – 36 and Annexure/s C)	-	N/A
Fully completed Declaration of Designated Groups for Preferential Procurement (PA 40)	2 Pages	Yes
Registration on National Treasury's Central Supplier Database (CSD).	-	Yes
Particulars of Tenderer's Projects (DPW-09 EC)	2 Pages	Yes
Site Inspection Meeting Certificate (DPW-16 EC) <i>(if applicable)</i> .	1 Page	YES
Record of attending compulsory virtual bid clarification / site inspection meeting <i>(if applicable)</i> .	1 Page	YES
Record of Addenda to tender documents (DPW-21 EC)	1 Page	Yes
Proof of 30% Subcontracting participation and related documents in terms of the Preferential Procurement Regulations 2017 <i>(if applicable)</i> .	-	N/A
Submission of DPW-15 (EC): Schedule of Proposed Sub-contractors <i>(Only if applicable)</i>	1	YES
EPWP Declaration: Fully Complete and sign EPWP Programme Declaration to ensure compliance	1	YES

* In compliance with the requirements of the cidb SFU Annexure G

Tender / Quotation no: *Error! Reference source not found.*

2. ADDITIONAL RETURNABLE DOCUMENTS REQUIRED FOR TENDER EVALUATION PURPOSES

Note: Failure to submit the applicable documents will result in the Tenderer having to submit same upon request within a stipulated time and if not complied with, will result in the tender offer being disqualified from further consideration. [See also C.2.18 of the Standard Conditions of Tender]

Tender document name	Number of pages issued	Returnable document
Any <u>additional</u> information required to complete a risk assessment (<i>if applicable</i>)	-	Yes
Any correction to be initialled by the person authorised to sign the tender documentation as per PA 15.1 or PA 15.2 resolution of board/s of directors / or PA15.3 Special Resolution of Consortia or JV's .		YES
Submission of applicable (PA-15.1, PA-15.2, PA-15.3): Resolution by the legal entity, or consortium / joint venture, authorising a dedicated person(s) to sign documents on behalf of the firm / consortium / joint venture.		YES

3. RETURNABLE DOCUMENTS THAT WILL BE INCORPORATED INTO THE CONTRACT

Note: Failure to submit the applicable documents will result in the Tenderer having to submit same upon request within a stipulated time and if not complied with, will result in the tender offer being disqualified from further consideration. [See also C.2.18 of the Standard Conditions of Tender]

Tender document name	Number of pages issued	Returnable document
Schedule of proposed sub-contractors (DPW-15 EC) (<i>if applicable</i>)	1 Page	Yes
Particulars of Electrical Contractor (DPW-22 EC) (<i>if applicable</i>)	1 Page	Yes
Mechanical / Electrical / Security Work material and equipment schedules (<i>if applicable</i>)	Pages	Yes
Schedule for Imported Materials and Equipment (DPW-23 EC) (<i>if applicable</i>)	1 Page	Yes

4. OTHER DOCUMENTS THAT WILL BE INCORPORATED INTO THE CONTRACT

(Insert a tick in the "Returnable document" column to indicate which documents must be returned with the tender)

Note: Failure to submit the applicable documents will result in the tender offer being disqualified from further consideration.

Tender document name	Number of pages issued	Returnable document
Priced Bills of Quantities / Lump Sum Document (complete document inclusive of all parts)	Pages	☒ Yes ☐ No
Fully priced and completed sectional summary- and final summary pages with the tender.	4 Pages	☐ Yes ☒ No

Tender / Quotation no: Error! Reference source not found.

Tender document name	Number of pages issued	Returnable document
<i>insert document name</i>	Pages	☐ Yes ☐ No
<i>insert document name</i>	Pages	☐ Yes ☐ No

5. ADDITIONAL INFORMATION THAT MAY BE REQUIRED FOR TENDER EVALUATION PURPOSES

Legal Status of Tendering Entity: If the Tendering Entity is:	Documentation to be submitted with the tender, or which may be required during the tender evaluation:
a. A close corporation, incorporated prior to 1 May 2011 under the Close Corporations Act, 1984 (Act 69 of 1984, as amended)	Copies of the Founding Statement – CK1
b. A profit company duly registered as a private company. [including a profit company that meets the criteria for a private company, whose Memorandum of Incorporation states that the company is a personal liability company in terms of Section 8(2)(c) of the Companies Act, 2008 (Act 71 of 2008, as amended)].	Copies of: i. Certificate of Incorporation – CM1; ii. Shareholding Certificates of all Shareholders of the company, plus a signed statement of the company's Auditor, certifying each Shareholder's ownership / shareholding percentage relative to the total; and/or iii. Memorandum of Incorporation in the case of a personal liability company.
c. A profit company duly registered as a private company in which any, or all, shares are held by one or more other close corporation(s) or company(ies) duly registered as profit or non-profit company(ies).	Copies of documents referred to in a. and/or b. above in respect of all such close corporation(s) and/or company(ies).
d. A profit company duly registered as a public company.	Copy of Certificate of Incorporation – CM1, and a signed statement of the company's Secretary or Auditor confirming that the company is a public company.
e. A non-profit company, incorporated in terms of Section 10 and Schedule 1 of the Companies Act, 2008 (Act 71 of 2008, as amended).	Copies of: i the Founding Statement – CK1; and ii the Memorandum of Incorporation setting out the object of the company, indicating the public benefit, cultural or social activity, or communal or group interest.
f. A natural person, sole proprietor or a Partnership	Copy(ies) of the Identity Document(s) of: i. such natural person/ sole proprietor, or each of the Partners to the Partnership.
g. A Trust	Deed of Trust duly indicating names of the Trustee(s) and Beneficiary (ies) as well as the purpose of the Trust and the mandate of the Trustees.

Signed by the Tenderer

Name of representative	Signature	Date

DPW-07 (EC): FORM OF OFFER AND ACCEPTANCE

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender / Quotation no:	H25/008 AI	Reference no:	WCS 056397

OFFER

The Employer, identified in the acceptance signature block, has solicited offers to enter into a contract for the procurement of:

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

The Tenderer, identified in the offer signature block, has examined the documents listed in the tender data and addenda thereto as listed in the returnable schedules, and by submitting this offer has accepted the conditions of tender.

By the representative of the Tenderer, deemed to be duly authorized, signing this part of this form of offer and acceptance, the Tenderer offers to perform all of the obligations and liabilities of the Contractor under the contract including compliance with all its terms and conditions according to their true intent and meaning for an amount to be determined in accordance with the conditions of contract identified in the contract data.

THE TOTAL OFFER INCLUSIVE OF ALL APPLICABLE TAXES ("All applicable taxes" includes value- added tax, pay as you earn, income tax, unemployment insurance fund contributions and skills development levies) **IS:**

Rand (in figures) R

Rand (in words).....

.....

.....

The amount in words takes precedence over the amount in figures. The award of the tender may be subjected to further price negotiation with the preferred tenderer(s). The negotiated and agreed price will be considered for acceptance as **a firm and final offer**.

This offer may be accepted by the Employer by signing the acceptance part of this form of offer and acceptance and returning one copy of this document to the Tenderer before the end of the period of validity stated in the tender data, whereupon the Tenderer becomes the party named as the Contractor in the conditions of contract identified in the contract data.

THIS OFFER IS MADE BY THE FOLLOWING LEGAL ENTITY: (cross out block which is not applicable)

Company or Close Corporation: And: Whose Registration Number is: And: Whose Income Tax Reference Number is: CSD supplier number:.....	OR	Natural Person or Partnership: Whose Identity Number(s) is/are: Whose Income Tax Reference Number is/are: CSD supplier number:.....

*Any reference to words "Bid" or "Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

**Any reference to the words "payment reduction" herein shall be construed to have the same meaning as the word "retention"

Tender / Quotation no: H25/008 AI

AND WHO IS (if applicable):	
Trading under the name and style of:	
AND WHO IS:	
Represented herein, and who is duly authorised to do so, by: Mr/Mrs/Ms: In his/her capacity as:	Note: A Resolution / Power of Attorney, signed by all the Directors / Members / Partners of the Legal Entity must accompany this Offer, authorising the Representative to make this offer.

SIGNED FOR THE TENDERER:

Name of representative	Signature	Date

WITNESSED BY:

Name of witness	Signature	Date

This Offer is in respect of: (Please indicate with an "X" in the appropriate block)

- The official documents ☐
- The official alternative ☐
- Own alternative (only if documentation makes provision therefore) ☐

(N.B.: Separate Offer and Acceptance forms are to be completed for the main and for each alternative offer)

SECURITY OFFERED:

- (a) the Tenderer accepts that in respect of contracts up to R1 million, a payment reduction** of 5% of the contact value (excluding VAT) will be applicable and will be deducted by the Employer in terms of the applicable conditions of contract
- (b) in respect of contracts above R1 million, the Tenderer offers to provide security as indicated below:
- | | |
|--|--|
| (1) cash deposit of 10 % of the Contract Sum (excluding VAT) | Yes ☐ No ☐ |
| (2) variable construction guarantee of 10 % of the Contract Sum (excluding VAT) | Yes ☐ No ☐ |
| (3) payment reduction of 10% of the value certified in the payment certificate (excluding VAT) | Yes ☐ No ☐ |
| (4) cash deposit of 5% of the Contract Sum (excluding VAT) and a payment reduction of 5% of the value certified in the payment certificate (excluding VAT) | Yes ☐ No ☐ |
| (5) fixed construction guarantee of 5% of the Contract Sum (excluding VAT) and a payment reduction of 5% of the value certified in the payment certificate (excluding VAT) | Yes ☐ No ☐ |

NB. Guarantees submitted must be issued by either an insurance company duly registered in terms of the Insurance Act [Long-Term Insurance Act, 1998 (Act 52 of 1998) or Short-Term Insurance Act, 1998 (Act 35 of 1998)] or by a bank duly registered in terms of the Banks Act, 1990 (Act 94 of 1990) on the pro-forma referred to above. No alterations or amendments of the wording of the pro-forma will be accepted.

*Any reference to words "Bid" or "Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

**Any reference to the words "payment reduction" herein shall be construed to have the same meaning as the word "retention"

For Internal & External Use

Tender / Quotation no: Error! Reference source not found.

The Tenderer elects as its *domicilium citandi et executandi* in the Republic of South Africa, where any and all legal notices may be served, as (physical address):

.....

Other Contact Details of the Tenderer are:

Telephone No..... Cellular Phone No.

Fax No

Postal address

Banker Branch.....

Registration No of Tenderer at Department of Labour

CIDB Registration Number:

ACCEPTANCE

By signing this part of this form of offer and acceptance, the Employer identified below accepts the Tenderer's offer. In consideration thereof, the Employer shall pay the Contractor the amount due in accordance with the conditions of contract identified in the contract data. Acceptance of the Tenderer's offer shall form an agreement between the Employer and the Tenderer upon the terms and conditions contained in this agreement and in the contract that is the subject of this agreement.

The terms of the contract are contained in:

Part C1 Agreement and contract data, (which includes this agreement)

Part C2 Pricing data

Part C3 Scope of work

Part C4 Site information and drawings and documents or parts thereof, which may be incorporated by reference into the above listed Parts.

Deviations from and amendments to the documents listed in the tender data and any addenda thereto as listed in the tender schedules as well as any changes to the terms of the offer agreed by the Tenderer and the Employer during this process of offer and acceptance, are contained in the schedule of deviations attached to and forming part of this agreement. No amendments to or deviations from said documents are valid unless contained in this schedule.

The Tenderer shall within two weeks after receiving a completed copy of this agreement, including the schedule of deviations (if any), contact the Employer's agent (whose details are given in the contract data) to arrange the delivery of any securities, bonds, guarantees, proof of insurance and any other documentation to be provided in terms of the conditions of contract identified in the contract data. Failure to fulfil any of these obligations in accordance with those terms shall constitute a repudiation of this agreement.

Notwithstanding anything contained herein, this agreement comes into effect on the date when the tenderer receives one fully completed original copy of this document, including the schedule of deviations (if any). Unless the tenderer (now contractor) within five (5) working days of the date of such receipt notifies the employer in writing of any reason why he/she cannot accept the contents of this agreement, this agreement shall constitute a binding contract between the parties.

For the Employer:

Name of signatory	Signature	Date

*Any reference to words "Bid" or "Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

**Any reference to the words "payment reduction" herein shall be construed to have the same meaning as the word "retention"
 For Internal & External Use

Tender / Quotation no: Error! Reference source not found.

Name of Organisation:	Department of Public Works and Infrastructure
Address of Organisation:	

WITNESSED BY:

Name of witness	Signature	Date

Schedule of Deviations

1.1.1. Subject:
Detail:
1.1.2. Subject:
Detail:
1.1.3. Subject:
Detail:
1.1.4. Subject:
Detail:
1.1.5. Subject:
Detail:
1.1.6. Subject:
Detail:

By the duly authorised representatives signing this agreement, the Employer and the Tenderer agree to and accept the foregoing schedule of deviations as the only deviations from and amendments to the documents listed in the tender data and addenda thereto as listed in the tender schedules, as well as any confirmation, clarification or changes to the terms of the offer agreed by the Tenderer and the Employer during this process of offer and acceptance.

It is expressly agreed that no other matter whether in writing, oral communication or implied during the period between the issue of the tender documents and the receipt by the Tenderer of a completed signed copy of this Agreement shall have any meaning or effect in the contract between the parties arising from this agreement.

*Any reference to words "Bid" or "Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

**Any reference to the words "payment reduction" herein shall be construed to have the same meaning as the word "retention"
For Internal & External Use

PA-11: BIDDER'S DISCLOSURE

1. PURPOSE OF THE FORM

Any person (natural or juristic) may make an offer or offers in terms of this invitation to bid. In line with the principles of transparency, accountability, impartiality, and ethics as enshrined in the Constitution of the Republic of South Africa and further expressed in various pieces of legislation, it is required for the bidder to make this declaration in respect of the details required hereunder.

Where a person/s are listed in the Register for Tender Defaulters and / or the List of Restricted Suppliers, that person will automatically be disqualified from the bid process.

2. Bidder's declaration

- 2.1 Is the bidder, or any of its directors / trustees / shareholders / members / partners or any person having a controlling interest (1) in the enterprise, employed by the state?

YES / NO

- 2.1.1 If so, furnish particulars of the names, individual identity numbers, and, if applicable, state employee numbers of sole proprietor/ directors / trustees / shareholders / members/ partners or any person having a controlling interest in the enterprise, in table below.

Full Name	Identity Number	Name of State institution

(1) the power, by one person or a group of persons holding the majority of the equity of an enterprise, alternatively, the person/s having the deciding vote or power to influence or to direct the course and decisions of the enterprise.

- 2.2 Do you, or any person connected with the bidder, have a relationship with any person who is employed by the procuring institution?

YES / NO

- 2.2.1 If so, furnish particulars:

.....
.....

- 2.3 Does the bidder or any of its directors / trustees / shareholders / members / partners or any person having a controlling interest in the enterprise have any interest in any other related enterprise whether or not they are bidding for this contract?

YES / NO

- 2.3.1 If so, furnish particulars:

.....
.....

3 DECLARATION

I, the undersigned, (name).....
in submitting the accompanying bid, do hereby make the following statements that I certify to be true and complete in every respect:

- 3.1 I have read and I understand the contents of this disclosure;
- 3.2 I understand that the accompanying bid will be disqualified if this disclosure is found not to be true and complete in every respect;
- 3.3 The bidder has arrived at the accompanying bid independently from, and without consultation, communication, agreement or arrangement with any competitor. However, communication between partners in a joint venture or consortium² will not be construed as collusive bidding.
- 3.4 In addition, there have been no consultations, communications, agreements or arrangements with any competitor regarding the quality, quantity, specifications, prices, including methods, factors or formulas used to calculate prices, market allocation, the intention or decision to submit or not to submit the bid, bidding with the intention not to win the bid and conditions or delivery particulars of the products or services to which this bid invitation relates.
- 3.5 The terms of the accompanying bid have not been, and will not be, disclosed by the bidder, directly or indirectly, to any competitor, prior to the date and time of the official bid opening or of the awarding of the contract.
- 3.6 There have been no consultations, communications, agreements or arrangements made by the bidder with any official of the procuring institution in relation to this procurement process prior to and during the bidding process except to provide clarification on the bid submitted where so required by the institution; and the bidder was not involved in the drafting of the specifications or terms of reference for this bid.

² Joint venture or Consortium means an association of persons for the purpose of combining their expertise, property, capital, efforts, skill and knowledge in an activity for the execution of a contract.

- 3.7 I am aware that, in addition and without prejudice to any other remedy provided to combat any restrictive practices related to bids and contracts, bids that are suspicious will be reported to the Competition Commission for investigation and possible imposition of administrative penalties in terms of section 59 of the Competition Act No 89 of 1998 and or may be reported to the National Prosecuting Authority (NPA) for criminal investigation and or may be restricted from conducting business with the public sector for a period not exceeding ten (10) years in terms of the Prevention and Combating of Corrupt Activities Act No 12 of 2004 or any other applicable legislation.

I CERTIFY THAT THE INFORMATION FURNISHED IN PARAGRAPHS 1, 2 and 3 ABOVE IS CORRECT.

I ACCEPT THAT THE STATE MAY REJECT THE BID OR ACT AGAINST ME IN TERMS OF PARAGRAPH 6 OF PFMA SCM INSTRUCTION 03 OF 2021/22 ON PREVENTING AND COMBATING ABUSE IN THE SUPPLY CHAIN MANAGEMENT SYSTEM SHOULD THIS DECLARATION PROVE TO BE FALSE.

.....
Signature

.....
Date

.....
Position

.....
Name of bidder

This form has been aligned with SBD4

PA-15.1: RESOLUTION OF BOARD OF DIRECTORS

RESOLUTION of a meeting of the Board of *Directors / Members / Partners of:

(Legally correct full name and registration number, if applicable, of the Enterprise)

Held at _____ (place)

on _____ (date)

RESOLVED that:

- The Enterprise submits a Bid / Tender to the Department of Public Works in respect of the following project:

(Project description as per Bid / Tender Document)

Bid / Tender Number: _____ (Bid / Tender Number as per Bid / Tender Document)

- *Mr/Mrs/Ms: _____

in *his/her Capacity as: _____ (Position in the Enterprise)

and who will sign as follows: _____

be, and is hereby, authorised to sign the Bid / Tender, and any and all other documents and/or correspondence in connection with and relating to the Bid / Tender, as well as to sign any Contract, and any and all documentation, resulting from the award of the Bid / Tender to the Enterprise mentioned above.

	Name	Capacity	Signature
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			
16			

17			
18			
19			
20			

The bidding enterprise hereby absolves the Department of Public Works from any liability whatsoever that may arise as a result of this document being signed.

Note:

1. * Delete which is not applicable.
2. **NB:** This resolution must, where possible, be signed by all the Directors / Members / Partners of the Bidding Enterprise.
3. In the event that paragraph 2 cannot be complied with, the resolution must be signed by Directors / Members / Partners holding a majority of the shares / ownership of the Bidding Enterprise (attach proof of shareholding / ownership hereto).
4. Directors / Members / Partners of the Bidding Enterprise may alternatively appoint a person to sign this document on behalf of the Bidding Enterprise, which person must be so authorized by way of a duly completed power of attorney, signed by the Directors / Members / Partners holding a majority of the shares / ownership of the Bidding Enterprise (proof of shareholding / ownership and power of attorney are to be attached hereto).
5. Should the number of Directors / Members / Partners exceed the space available above, additional names and signatures must be supplied on a separate page.

ENTERPRISE STAMP

PA-15.3: SPECIAL RESOLUTION OF CONSORTIA OR JOINT VENTURES

RESOLUTION of a meeting of the duly authorised representatives of the following legal entities who have entered into a consortium/joint venture to jointly bid for the project mentioned below: *(legally correct full names and registration numbers, if applicable, of the Enterprises forming a Consortium/Joint Venture)*

1. _____

2. _____

3. _____

4. _____

5. _____

6. _____

7. _____

8. _____

Held at _____ (place)

on _____ (date)

RESOLVED that:

RESOLVED that:

- A. The above-mentioned Enterprises submit a Bid in Consortium/Joint Venture to the Department of Public Works in respect of the following project:

(Project description as per Bid /Tender Document)

Bid / Tender Number: _____ (Bid / Tender Number as per Bid /Tender Document)

PA-15.3: Special Resolution of Consortia or Joint Ventures

B. *Mr/Mrs/Ms: _____

in *his/her Capacity as: _____ (Position in the Enterprise)

and who will sign as follows: _____

be, and is hereby, authorised to sign the Bid, and any and all other documents and/or correspondence in connection with and relating to the Bid, as well as to sign any Contract, and any and all documentation, resulting from the award of the Bid to the Enterprises in Consortium/Joint Venture mentioned above.

C. The Enterprises constituting the Consortium/Joint Venture, notwithstanding its composition, shall conduct all business under the name and style of:

D. The Enterprises to the Consortium/Joint Venture accept joint and several liability for the due fulfilment of the obligations of the Consortium/Joint Venture deriving from, and in any way connected with, the Contract entered into with the Department in respect of the project described under item A above.

E. Any of the Enterprises to the Consortium/Joint Venture intending to terminate the consortium/joint venture agreement, for whatever reason, shall give the Department 30 days written notice of such intention. Notwithstanding such decision to terminate, the Enterprises shall remain jointly and severally liable to the Department for the due fulfilment of the obligations of the Consortium/Joint Venture as mentioned under item D above.

F. No Enterprise to the Consortium/Joint Venture shall, without the prior written consent of the other Enterprises to the Consortium/Joint Venture and of the Department, cede any of its rights or assign any of its obligations under the consortium/joint venture agreement in relation to the Contract with the Department referred to herein.

G. The Enterprises choose as the *domicilium citandi et executandi* of the Consortium/Joint Venture for all purposes arising from the consortium/joint venture agreement and the Contract with the Department in respect of the project under item A above:

Physical address: _____

_____ (Postal code) _____

Postal Address: _____

_____ (Postal code) _____

Telephone number: _____

Fax number: _____

PA-15.3: Special Resolution of Consortia or Joint Ventures

	Name	Capacity	Signature
1			
2			
3			
4			
5			
6			
7			
8			
9			
10			
11			
12			
13			
14			
15			

The bidding enterprise hereby absolves the Department of Public Works & Infrastructure from any liability whatsoever that may arise as a result of this document being signed.

Note:

1. * Delete which is not applicable.
2. **NB:** This resolution must be signed by all the Duly Authorised Representatives of the Legal Entities to the consortium/joint venture submitting this tender, as named in item 2 of Resolution PA-15.2.
3. Should the number of the Duly Authorised Representatives of the Legal Entities joining forces in this tender exceed the space available above, additional names, capacity and signatures must be supplied on a separate page.
4. Resolution PA-15.2, duly completed and signed, from the separate Enterprises who participate in this consortium/joint venture, must be attached to this Special Resolution (PA-15.3).

PA-16: PREFERENCE POINTS CLAIM FORM IN TERMS OF THE PREFERENTIAL PROCUREMENT REGULATIONS 2022

This preference form must form part of all tenders invited. It contains general information and serves as a claim form for preference points for specific goals.

NB: BEFORE COMPLETING THIS FORM, TENDERERS MUST STUDY THE GENERAL CONDITIONS, DEFINITIONS AND DIRECTIVES APPLICABLE IN RESPECT OF THE TENDER AND PREFERENTIAL PROCUREMENT REGULATIONS, 2022

1. GENERAL CONDITIONS

1.1 The following preference point systems are applicable to invitations to tender:

- the 80/20 system for requirements with a Rand value of up to R50 000 000 (all applicable taxes included); and
- the 90/10 system for requirements with a Rand value above R50 000 000 (all applicable taxes included).

1.2 Preference Points System to be applied

(tick whichever is applicable).

- ☐ The applicable preference point system for this tender is the **80/20** preference point system.
- ☒ The applicable preference point system for this tender is the **90/10** preference point system.
- ☐ Either the **90/10 or 80/20** preference point system will be applicable in this tender. The lowest/ highest acceptable tender will be used to determine the accurate system once tenders are received.

1.3 Points for this tender shall be awarded for:

1.3.1 Price; and

1.3.2 Specific Goals

1.4 The maximum points for this tender are allocated as follows:

CHOOSE APPLICABLE PREFERENCE POINT SCORING SYSTEM	☐ 80/20	☒ 90/10
PRICE	80	90
SPECIFIC GOALS	20	10
Total points for Price and Specific Goals	100	100

1.5 Breakdown Allocation of Specific Goals Points



1.5.1. For procurement transaction with rand value greater than R2 000, 00 and up to R1 Million (Inclusive of all applicable taxes) the specific goals listed in table 1 below are applicable.

Table 1

Serial No	Specific Goals	Preference Points Allocated out of 20	Documentation to be submitted by bidders to validate their claim
1.	An EME or QSE which is at least 51% owned by black people (Mandatory)	10	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be done or services to be rendered in that area (Mandatory)	2	- Official Municipal Rates Statement which is in the name of the bidder. Or - Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder. Or - Lease Agreement which is in the name of the bidder.
3.	An EME or QSE which is at least 51% owned by black women (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
4.	An EME or QSE which is at least 51% owned by black people with disability (Mandatory)	2	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.

			and • Medical Certificate indicating that the disability is permanent. Or • South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or • National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).
5.	An EME or QSE which is at least 51% owned by black youth (Mandatory)	2	• ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.



1.5.2. For procurement transaction with rand value greater than R1 Million and up to R50 Million (Inclusive of all applicable taxes) the specific goals listed in table 2 below are applicable.

Table 2

Serial No	Specific Goals	Preference Points Allocated out of 20	Documentation to be submitted by bidders to validate their claim
1.	An EME or QSE or any entity which is at least 51% owned by black people (Mandatory)	10	• SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
2.	Located in a specific Local Municipality or District Municipality or Metro or Province area for work to be done or services to be rendered in that area (Mandatory)	2	• Official Municipal Rates Statement which is in the name of the bidder. Or

			- Any account or statement which is in the name of the bidder. Or - Permission to Occupy from local chief in case of rural areas (PTO) which is in the name of the bidder. Or - Lease Agreement which is in the name of the bidder.
3.	An EME or QSE or any entity which is at least 51% owned by black women (Mandatory)	4	SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable.
4.	An EME or QSE or any entity which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent. Or - South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).

</

		owned by black women (mandatory)		
	4. ☐	An EME or QSE or any entity which is at least 51% owned by black people with disability (Mandatory)	2	- SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable. and - Medical Certificate indicating that the disability is permanent. Or - South African Social Security Agency (SASSA) Registration indicating that the disability is permanent. Or National Council for Persons with Physical Disability in South Africa registration (NCPDPSA).
	OR			
	5. ☒	An EME or QSE or any entity which is at least 51% owned by black youth (Mandatory)	2	ID Copy and SANAS Accredited BBBEE Certificate or Sworn Affidavit where applicable

Black people mean Africans, Coloureds and Indians, who - (a) are citizens of the Republic of South Africa by birth or descent; or (b) became citizens of the Republic of South Africa by naturalisation - (i) before 27 April 1994; or (ii) on or after 27 April 1994 and who would have been entitled to acquire citizenship by naturalisation prior to that date. (BROAD-BASED BLACK ECONOMIC EMPOWERMENT ACT No 25899, 2003 of 9 JANUARY 2004).

- 1.6 Failure on the part of the tenderer to submit proof or documentation required in terms of this tender to claim points for specific goals, if the service provider/ tenderer did not submit proof or documentation required to claim for specific goals will be interpreted to mean that preference points for specific goals are not claimed.
- 1.7 The organ of state reserves the right to require of a service provider/tenderer, either before a tender is adjudicated or at any time subsequently, to substantiate any claim in regard to preferences, in any manner required by the organ of state.

2. DEFINITIONS

- (a) **“tender”** means a written offer in the form determined by an organ of state in response to an invitation to provide goods or services through price quotations,

competitive tendering process or any other method envisaged in legislation;

- (b) “**price**” means an amount of money tendered for goods or services, and includes all applicable taxes less all unconditional discounts;
- (c) “**rand value**” means the total estimated value of a contract in Rand, calculated at the time of bid invitation, and includes all applicable taxes;
- (d) “**tender for income-generating contracts**” means a written offer in the form determined by an organ of state in response to an invitation for the origination of income-generating contracts through any method envisaged in legislation that will result in a legal agreement between the organ of state and a third party that produces revenue for the organ of state, and includes, but is not limited to, leasing and disposal of assets and concession contracts, excluding direct sales and disposal of assets through public auctions; and
- (e) “**the Act**” means the Preferential Procurement Policy Framework Act, 2000 (Act No. 5 of 2000).

3. FORMULAE FOR PROCUREMENT OF GOODS AND SERVICES

3.1. POINTS AWARDED FOR PRICE

3.1.1. THE 80/20 OR 90/10 PREFERENCE POINT SYSTEMS

A maximum of 80 or 90 points is allocated for price on the following basis:

$$\begin{array}{ccc} \mathbf{80/20} & \mathbf{or} & \mathbf{90/10} \\ \\ \mathbf{Ps = 80 \left(1 - \frac{Pt - P_{min}}{P_{min}} \right)} & \mathbf{or} & \mathbf{Ps = 90 \left(1 - \frac{Pt - P_{min}}{P_{min}} \right)} \end{array}$$

Where

- Ps = Points scored for price of tender under consideration
- Pt = Price of tender under consideration
- Pmin = Price of lowest acceptable tender

3.2. FORMULAE FOR DISPOSAL OR LEASING OF STATE ASSETS AND INCOME GENERATING PROCUREMENT

3.2.1. POINTS AWARDED FOR PRICE

A maximum of 80 or 90 points is allocated for price on the following basis:

$$\begin{array}{ccc} \mathbf{80/20} & \mathbf{or} & \mathbf{90/10} \\ \\ \mathbf{Ps = 80 \left(1 + \frac{Pt - P_{max}}{P_{max}} \right)} & \mathbf{or} & \mathbf{Ps = 90 \left(1 + \frac{Pt - P_{max}}{P_{max}} \right)} \end{array}$$

Where

- Ps = Points scored for price of tender under consideration
- Pt = Price of tender under consideration
- Pmax = Price of highest acceptable tender

4. POINTS AWARDED FOR SPECIFIC GOALS

- 4.1. In terms of Regulation 4(2); 5(2); 6(2) and 7(2) of the Preferential Procurement Regulations, preference points must be awarded for specific goals stated in the tender. For the purposes of this tender the tenderer will be allocated points based on the goals stated in table 1,2 and 3 above as may be supported by proof/ documentation stated in the conditions of this tender:
- 4.2. In cases where organs of state intend to use Regulation 3(2) of the Regulations, which states that, if it is unclear whether the 80/20 or 90/10 preference point system applies, an organ of state must, in the tender documents, stipulate in the case of—
- (a) an invitation for tender for income-generating contracts, that either the 80/20 or 90/10 preference point system will apply and that the highest acceptable tender will be used to determine the applicable preference point system; or
 - (b) any other invitation for tender, that either the 80/20 or 90/10 preference point system will apply and that the lowest acceptable tender will be used to determine the applicable preference point system,
- then the organ of state must indicate the points allocated for specific goals for both the 90/10 and 80/20 preference point system.

Table 4: Specific goals for the tender and points claimed are indicated per the table below.

(Note to organs of state: Where either the 90/10 or 80/20 preference point system is applicable, corresponding points must also be indicated as such.)

Note to tenderers: The tenderer must indicate how they claim points for each preference point system.)

The specific goals allocated points in terms of this tender	Number of points allocated (90/10 system) (To be completed by the organ of state)	Number of points allocated (80/20 system) (To be completed by the organ of state)	Number of points claimed (90/10 system) (To be completed by the tenderer)	Number of points claimed (80/20 system) (To be completed by the tenderer)
1. An EME or QSE (or any entity for procurement transaction with rand value greater than R1 Million) which is at least 51% owned by black people	4	10		
2. Located in a specific Local Municipality or District Municipality or Metro or	2	2		

The specific goals allocated points in terms of this tender	Number of points allocated (90/10 system) (To be completed by the organ of state)	Number of points allocated (80/20 system) (To be completed by the organ of state)	Number of points claimed (90/10 system) (To be completed by the tenderer)	Number of points claimed (80/20 system) (To be completed by the tenderer)
Province area for work to be done or services to be rendered in that area				
3. An EME or QSE (or any entity for procurement transaction with rand value greater than R1 Million) which is at least 51% owned by black women	2	4		
4. An EME or QSE (or any entity for procurement transaction with rand value greater than R1 Million) which is at least 51% owned by black people with disability	0	2		
5. An EME or QSE (or any entity for procurement transaction with rand value greater than R1 Million) which is at least 51% owned by black youth.*	2	2		

DECLARATION WITH REGARD TO COMPANY/FIRM

4.3. Name of company/firm.....

4.4. Company registration number:

4.5. TYPE OF COMPANY/ FIRM

Partnership/Joint Venture / Consortium
One-person business/sole propriety
Close corporation
Public Company
Personal Liability Company
(Pty) Limited
Non-Profit Company

State Owned Company
[TICK APPLICABLE BOX]

- 4.6. I, the undersigned, who is duly authorised to do so on behalf of the company/firm, certify that the points claimed, based on the specific goals as advised in the tender, qualifies the company/ firm for the preference(s) shown and I acknowledge that:
- i) The information furnished is true and correct;
 - ii) The preference points claimed are in accordance with the General Conditions as indicated in paragraph 1 of this form;
 - iii) In the event of a contract being awarded as a result of points claimed as shown in paragraphs 1.4 and 4.2, the contractor may be required to furnish documentary proof to the satisfaction of the organ of state that the claims are correct;
 - iv) If the specific goals have been claimed or obtained on a fraudulent basis or any of the conditions of contract have not been fulfilled, the organ of state may, in addition to any other remedy it may have –
 - (a) disqualify the person from the tendering process;
 - (b) recover costs, losses or damages it has incurred or suffered as a result of that person's conduct;
 - (c) cancel the contract and claim any damages which it has suffered as a result of having to make less favourable arrangements due to such cancellation;
 - (d) recommend that the tenderer or contractor, its shareholders and directors, or only the shareholders and directors who acted on a fraudulent basis, be restricted from obtaining business from any organ of state for a period not exceeding 10 years, after the *audi alteram partem* (hear the other side) rule has been applied; and
 - (e) forward the matter for criminal prosecution, if deemed necessary.

.....	
SIGNATURE(S) OF TENDERER(S)	
SURNAME AND NAME:	
DATE:	
ADDRESS:	
	
	
	

B-BBEE EXEMPTED AFFIDAVIT FOR EXEMPTED MICRO ENTERPRISES (ISSUED IN TERMS OF THE AMENDED CONSTRUCTION SECTOR CODE)

(Gazette Vol. 630 No. 41287)
Issued in terms of paragraph 3.6.2.4.1 (B)

I, the undersigned,

Full name & Surname	
Identity number	

Hereby declare under oath as follows:

- 1) The contents of this statement are to the best of my knowledge a true reflection of the facts.
- 2) I am a Member ☐ / Director ☐ / Owner ☐ **(Select one)** of the following enterprise and am duly authorised to act on its behalf:

Enterprise Name:			
Trading Name (If Applicable):			
Registration Number:			
Enterprise Physical Address:			
Type of Entity (CC, (Pty) Ltd, Sole Prop			
Nature of Construction	BEP (Built Environment Professional)	Contractor	Supplier
Definition of "Black People"	As per the Broad-Based Black Economic Empowerment Act 53 of 2003 as Amended by Act No 46 of 2013 "Black People" is a generic term which means Africans, Coloureds and Indians – who are citizens of the Republic of South Africa by birth or descent; or who became citizens of the Republic of South Africa by naturalization before 27 April 1994; or after 27 April 1994 and who would have been entitled to acquire citizenship by naturalization prior to that date;"		
Definition of "Black Designated Groups"	"Black Designated Groups" means: (a) unemployed black people not attending and not required by law to attend an educational institution and not awaiting admission to an educational institution; (b) Black people who are youth as defined in the National Youth Commission Act of 1996; (c) Black people who are persons with disabilities as defined in the Code of Good Practice on employment of people with disabilities issued under the Employment Equity Act; (d) Black people living in rural and under developed areas; (e) Black military veterans who qualifies to be called a military veteran in terms of the Military Veterans Act 18 of 2011;"		

- 3) I hereby declare under Oath that as per Amended Code Series 100 of the Amended Codes of Good Practice issued under section 9 (1) of B-BBEE Act No 53 of 2003 as Amended by Act No 46 of 2013,
 - The Enterprise is _____ % Black Owned
 - The Enterprise is _____ % Black Female Owned
 - The Enterprise is _____ % Owned by Black Designated Group (provide Black Designated Group Breakdown below as per the definition in the table above)
 - Black Youth % _____ %
 - Black Disabled % _____ %
 - Black Unemployed % _____ %
 - Black People living in Rural areas % _____ %
 - Black Military Veterans % _____ %

Effective date: 21 July 2023

- 4) Based on the ☐ Financial Statements or ☐ Management Accounts and other information available on the latest financial year-end of ____/____/____, (format: day/month/year) the annual Total Revenue was less than the applicable amount confirmed by ticking the applicable box below (Select applicable).

BEP	R1.8 million	
Contractor	R3.0 million	
Supplier	R3.0 million	

If the turnover exceeds the applicable amount in the table above then this affidavit is no longer applicable and an EME certificate must be obtained from a rating agency accredited by SANAS or when applicable a B-BBEE Verification Professional Regulator appointed by the Minister of Trade and Industry.

- Please Confirm on the below table the B-BBEE Level Contributor, **by ticking the applicable box below.**

100% Black Owned	Level One (135% B-BBEE procurement recognition level)	
At least 51% Black Owned	Level Two (125% B-BBEE procurement recognition level)	
At least 30% Black Owned	Level Four (100% B-BBEE procurement recognition level)	
Less than 30% Black Owned	Level Five (80% B-BBEE procurement recognition level)	


- 5) I know and understand the contents of this affidavit and I have no objection to take the prescribed oath and consider the oath binding on my conscience and on the Owners of the Enterprise which I represent in this matter.

- 6) The sworn affidavit will be valid for a period of 12 months from the date signed by commissioner.

Deponent Signature_____

Date: _____

Commissioner of Oaths
Signature & stamp



PA-16.1 (EC)

PA-16.1 (EC): OWNERSHIP PARTICULARS

NB: 1. This form is to be read with the Broad-based Black Economic Empowerment Act, 2003 (Act 53 of 2003), the Preferential Procurement Policy Framework Act, 2000 (Act 5 of 2000), the Preferential Procurement Regulations, 2011, the Notice and Invitation to Tender and the Tender Data pertaining to this Tender, and completed according to the definitions and information contained in said documents.

2. **Failure to complete this form may result in the tender being disqualified.**

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)
Tender no:	H25/008 AI

1. PARTICULARS OF TENDERER

Name of Tendering Entity (the Tenderer):

.....
(must correspond with the Form of Offer and Acceptance DPW-07 (EC) in Section C1.1)

Physical Address:	Postal Address:
Company/CC Registration No:	Tenderer's Income Tax Reference No:
Company VAT Registration No:	

Name of the duly authorized Representative of the Tenderer:

(must correspond with the Resolution PA-15.1, PA-15.2 and/or PA-15.3)

Telephone:	Facsimile:
Is the Tenderer a ☐ public* or ☐ private company?	

(*Preference points may not be awarded to public companies)

2. LIST ALL PROPRIETORS, MEMBERS OR SHAREHOLDERS BY NAME, IDENTITY NUMBER, CITIZENSHIP, PRE 1994 ELECTION FRANCHISE-STATUS AND OWNERSHIP, AS RELEVANT

Name #	Identity/Registration Number	Citizenship ##	HDI-Status ###	Date of Ownership	Percentage Owned	Percentage Voting	Percentage of time devoted to the Tendering Entity
			Qualify as HDI by virtue of not having had any franchise in elections prior to 1983 or 1994				
1.			☐ Yes ☐ No				
2.			☐ Yes ☐ No				
3.			☐ Yes ☐ No				
4.			☐ Yes ☐ No				
5.			☐ Yes ☐ No				
6.			☐ Yes ☐ No				
7.			☐ Yes ☐ No				
8.			☐ Yes ☐ No				
9.			☐ Yes ☐ No				
10.			☐ Yes ☐ No				
11.			☐ Yes ☐ No				
12.			☐ Yes ☐ No				

where Owners are themselves a Company, Close Corporation, Partnership etc, identify the ownership of the Holding Company, together with Registration number

state date of South African citizenship obtained

state "Yes" or "No" (refer to definitions contained in the PPPF Act, 2000 (Act 5 of 2000) and the Preferential Procurement Regulations, 2011)

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

For Internal & External Use

Effective date January 2012

Page 2 of 6

Version: 2.0

3 The following documentation must be included in the tender as part of the Returnable Documents. Failure to provide the said documentation may result in the tender being disqualified.

Legal Status of Tendering Entity: If the Tendering Entity is:	Documentation to be submitted with the tender:
a. A Close Corporation, incorporated under the Close Corporation Act, 1984 (Act 69 of 1984)	Certified copies of the Founding Statement – CK1
b. A private Company having share capital, incorporated under the Companies Act, 1973 (Act 61 of 1973) [including Companies incorporated under Art 53(b)]	Certified copies of: i. Certificate of Incorporation – CM1, and ii. Shareholders Certificates of all Members of the Company, plus a signed statement of the Company's Auditor, certifying each Member's ownership /shareholding percentage relative to the total.
c. A private Company having share capital, incorporated under the Companies Act, 1973 (Act 61 of 1973) in which any, or all, shares are held by another Close Corporation or Company with or without share capital	Certified copies of documents referred to in a. and/or b. above in respect of all such Close Corporation(s) and/or Company(ies).
d. A public Company having share capital, incorporated under the Companies Act, 1973 (Act 61 of 1973) [including Companies incorporated under Art 21]	A signed statement of the Company's Secretary confirming that the Company is a public Company.
e. A natural person or a Partnership	Certified copy of the Identity Document of: i. such natural person, or ii. each of the Partners to the Partnership.
f. A Trust	Deed of Trust.

4. Identify by name, HDI-status and length of service, those individuals (including Owners and non-Owners) responsible for the day-to-day management and business decisions:

	Name	HDI-status ###			Length of service (years)
		Qualify as HDI by virtue of not having had any franchise in elections prior to 1983 or 1994	Qualify as HDI by virtue of being female	Qualify as HDI by virtue of having a disability	
<u>FINANCIAL DECISIONS</u>					
Cheque signing Signing & Co-signing for loans		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Acquisition of lines of credit		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Sureties		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Major purchase or acquisitions		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Signing contracts		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
<u>MANAGEMENT DECISIONS</u>					
Estimating		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Market and sales operations		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Hiring and firing of management personnel		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Supervision of office personnel		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	
Supervision of Field / Production activities		☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	

state "Yes" or "No" (refer to definitions contained in the PPPF Act, 2000 (Act 5 of 2000) and the Preferential Procurement Regulations, 2011)

Any reference to words "Bid" or Bidder" herein and/or in any other documentation shall be construed to have the same meaning as the words "Tender" or "Tenderer".

For Internal & External Use

Effective date January 2012

5. If this tender offer is submitted by a Consortium or Joint Venture, provide the following information regarding the Participation Parameter of each of the Tendering entities relative to the project tendering for:

Name of Consortium / Joint Venture Partner	Participation Parameter expressed as a percentage
1.	%
2.	%
3.	%
4.	%
5.	%

NB: If submitting a tender offer in Consortium or Joint Venture, a copy of the proposed Consortium or Joint Venture Agreement must be submitted together with the Offer for scrutiny purposes during the Evaluation stage. All other requirements for deliverable documents pertaining to Consortium / Joint Ventures, as described in the Tender Data, must, in addition hereto, be adhered to. Information required in Sections 1 to 5 of this form must be provided separately in respect of each Consortium or Joint Venture Partner.

6. List the following personnel or external firms who provide the following services:

Service	Name	Contact Person	Telephone
Accounting			
Legal			
Auditing			
Banking			
Insurance			

7. DECLARATION:

The undersigned, who warrants that he/she is duly authorized to do so on behalf of the Tenderer, hereby confirms that:

- 7.1 The information and particulars contained in this Affidavit are true and correct in all respects;
- 7.2 The Broad-based Black Economic Empowerment Act, 2003 (Act 53 of 2003), Preferential Procurement Policy Framework Act, 2000 (Act 5 of 2000), the Preferential Procurement Regulations, 2011, and all documents pertaining to this Tender were studied and understood and that the above form was completed according to the definitions and information contained in said documents;
- 7.3 The Tenderer understands that any intentional misrepresentation or fraudulent information provided herein shall disqualify the Tenderer's offer herein, as well as any other tender offer(s) of the Tenderer simultaneously being evaluated, or will entitle the Employer to cancel any Contract resulting from the Tenderer's offer herein;
- 7.4 The Tenderer accepts that the Employer may exercise any other remedy it may have in law and in the Contract, including a claim for damages for having to accept a less favourable tender as a result of any such disqualification due to misrepresentation or fraudulent information provided herein;
- 7.5 Any further documentary proof required by the Employer regarding the information provided herein, will be submitted to the Employer within the time period as may be set by the latter;
- 7.6 The Tenderer understands that, once the tender herein has been awarded and it is later detected by the Employer that a preference relating to Ownership in terms of the Act and Regulations has been intentionally misrepresented or fraudulently claimed, the Employer will have recourse against such party as stipulated in Regulation 15 of the Preferential Procurement Regulations, 2011 and/or to impose a penalty amount equal to Y%, of the Offered Total of Prices (inclusive of Value Added Tax), tendered in the Form of Offer and Acceptance (section C1.1), calculated separately for each Ownership category misrepresented or fraudulently claimed; where Y is the maximum number of points allocated for each individual Ownership description provided in the Notice and Invitation to Tender (PA-04 EC), to a combined maximum of 10%. Furthermore: failure to achieve the tendered Contract Participation Goal will be penalized by a penalty amount as described in the Tender and Contract Conditions Pertaining to Contract Participation Goal (Participation of Targeted Enterprises) (PA-16.2 EC).

Signed by the Tenderer

Name of representative	Signature	Date

PA- 40: DECLARATION OF DESIGNATED GROUPS

Tender no: **H25/008 AI**

Name of Tenderer

☐ EME¹ ☐ QSE² ☐ Non EME/QSE (tick applicable box)

1. LIST ALL PROPRIETORS, MEMBERS OR SHAREHOLDERS BY NAME, IDENTITY NUMBER, CITIZENSHIP AND DESIGNATED GROUPS.

Name and Surname #	Identity/ Passport number and Citizenship##	Percentage owned	Black	Indicate if youth	Indicate if woman	Indicate if person with disability	Indicate if living in Rural (R) / Under Developed Area (UD) / Township (T) / Urban (U).	Indicate if military veteran
1.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
2.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
3.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
4.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
5.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
6.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
7.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
8.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
9.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
10.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
11.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No
12.		%	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ Yes ☐ No	☐ R ☐ UD ☐ T ☐ U	☐ Yes ☐ No

Where Owners are themselves a Company, Close Corporation, Partnership etc, identify the ownership of the Holding Company, together with Registration number
 ## State date of South African citizenship obtained (not applicable to persons born in South Africa)

¹ EME: Exempted Micro Enterprise

² QSE: Qualifying Small Business Enterprise

PA- 40: DECLARATION OF DESIGNATED GROUPS

Tender no: **H25/008 AI**

2. DECLARATION:

The undersigned, who warrants that he/she is duly authorized to do so on behalf of the Tenderer, hereby confirms that:

- 1 The information and particulars contained in this Affidavit are true and correct in all respects;
- 2 The Broad-based Black Economic Empowerment Act, 2003 (Act 53 of 2003), Preferential Procurement Policy Framework Act, 2000 (Act 5 of 2000), National Small Business Act 102 of 1996 as amended and all documents pertaining to this Tender were studied and understood and that the above form was completed according to the definitions and information contained in said documents;
- 3 The Tenderer understands that any intentional misrepresentation or fraudulent information provided herein shall disqualify the Tenderer's offer herein, as well as any other tender offer(s) of the Tenderer simultaneously being evaluated, or will entitle the Employer to cancel any Contract resulting from the Tenderer's offer herein;
- 4 The Tenderer accepts that the Employer may exercise any other remedy it may have in law and in the Contract, including a claim for damages for having to accept a less favourable tender as a result of any such disqualification due to misrepresentation or fraudulent information provided herein;
- 5 Any further documentary proof required by the Employer regarding the information provided herein, will be submitted to the Employer within the time period as may be set by the latter;

Signed by the Tenderer

Name of representative	Signature	Date

DPW-09 (EC): PARTICULARS OF TENDERER'S PROJECTS

Project title:	<i>ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)</i>		
Tender / quotation no:	H25/008 AI	Closing date:	15 September 2025
Advertising date:	22 August 2025	Validity period:	84 days

1. PARTICULARS OF THE TENDERER'S CURRENT AND PREVIOUS COMMITMENTS

1.1. Current projects

Projects currently engaged in	Name of Employer or Representative of Employer	Contact tel. no.	Contract sum	Contractual commencement date	Contractual completion date	Current percentage progress
1						
2						
3						
4						
5						
6						
7						
8						

1.2. Completed projects

Projects completed in the previous 5 (five) years	Name of Employer or Representative of Employer	Contact tel. no.	Contract sum	Contractual commencement date	Contractual completion date	Date of Certificate of Practical Completion
1						
2						
3						
4						
5						
6						
7						
8						
9						

Name of Tenderer	Signature	Date

DPW-15 (EC): SCHEDULE OF PROPOSED SUBCONTRACTORS

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender no:	<i>H25/008 AI</i>	Reference no:	<i>WCS 056397</i>

We notify you that it is our intention to employ the following Subcontractors for work in this contract.

We confirm that all subcontractors who are contracted to construct a house are registered as home builders with the National Home Builders Registration Council.

	Name and address of proposed Subcontractor	Nature and extent of work	Previous experience with Subcontractor
1			
2			
3			
4			
5			

Name of representative	Signature	Capacity	Date

Name of organisation:	

ANNEXURE A

(BIDDERS TO PROVIDE EVIDENCE OF INSTRUMENTATIONS, HAND TOOLS, MACHINERY, CLEANING EQUIPMENTS AND UTILITY VEHICLES OWNED OR TO BE HIRED/RENTED IN ORDER TO CARRY OUT THE PROJECT)

NOTE 1: FAILURE TO COMPLETE AND SUBMIT THIS FORM WILL RESULT BIDDERS NOT TO BE SCORED FOR FUNCTIONALITY CRITERIA NO. 9.3

NOTE 2: BIDDERS ARE NOT ALLOWED TO REPLICATE THIS ANNEXURE A

NOTE 3: IF ITEMS MARKED OWNED/RENTED ON ANNEXURE A, PROOF MUST BE PROVIDED

Project

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDING, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS

Description	Quantity	Owned	Outsourced
Instrumentation for testing of drinking water			
Bench top potentiometer, accurate and precise to at least 0,1 pH unit, including reference electrode and glass sensor or combination electrode;	3		
Electrical conducting meter, with error not exceeding 1 % or 0,1 m S/m;	3		
Thermometer covering the range 23 °C < T < 27 °C accurate and capable of being read to the nearest 0,1 °C;	3		
Magnetic stirrer with PTFE (Teflon) stirring bars;	3		
3 x 1 000 millilitre Imhoff cones with wooden rack;	3		
5 x 1 000 millilitre glass bottles with ground stopper;	3		
Turbidity meter	3		

Cleaning Equipment's	Quantity	Owned	Outsourced
Industrial hoover vacuum cleaner	6		
Numatic rotary disk floor scrubber/polisher	6		
Mega mobs (to be continuous supplied and to be sufficient for the duration of the contract period)	30		
Double mopping buckets and wringer 50 litre (to be continuously supplied and to be sufficient for the duration of the contract period)	9		
Platform Broom (to be continuously supplied and to be sufficient for the duration of the contract period)	15		
Multi-purpose cleaner / All-purpose cleaner concentrate or SABS approved General Purpose cleaner to be supplied in 25 litres (to be continuously supplied and to be sufficient for the duration of the contract period)	50		

Utility Vehicles	Quantity	Owned	Outsourced
4x4 LDV's	3		
2500l Fuel Trailer	1		
Machinery	Quantity	Owned	Outsourced
Plate Compacter	1		
Poker drive unit	2		
Concrete Mixer	2		
Hand tools	Quantity	Owned	Outsourced
Wheel barrows	4		
Tool boxes with hammers, Pliers, Screwdrivers, spanners etc.	5		
Step ladders	4		
Grass cutting machines	15		

Chainsaw machines for cutting and trimming trees	3		

NAME OF REPRESENTATIVE:	SIGNATURE:	DATE:

DPW-16 (EC): SITE INSPECTION MEETING CERTIFICATE

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: APPOINTMENT OF A SERVICE PROVIDER/S FOR THE MAINTENANCE AND REPAIRS OF BUILDING, CIVIL, MECHANICAL, ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS FOR A PERIOD OF 36 MONTHS (APPOINTMENT OF A CONTRACTOR)		
Tender / Quotation no:	H25/008 AI	Reference no:	WCS 05397
Closing date:			

This is to certify that I, _____ representing

_____ in the capacity of

_____ visited the site on:

I have made myself familiar with all local conditions likely to influence the work and the cost thereof. I further certify that I am satisfied with the description of the work and explanations given at the site inspection meeting and that I understand perfectly the work to be done, as specified and implied, in the execution of this contract.

Name of Tenderer	Signature	Date

Name of DPW Representative	Signature	Date

DPW-21 (EC): RECORD OF ADDENDA TO TENDER DOCUMENTS

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender no:	<i>H25/008 AI</i>	Reference no:	<i>WCS 056397</i>

1. I / We confirm that the following communications received from the Department of Public Works and Infrastructure before the submission of this tender offer, amending the tender documents, have been taken into account in this tender offer: *(Attach additional pages if more space is required)*

	Date	Title or Details
1.		
2.		
3.		
4.		
5.		
6.		
7.		
8.		
9.		
10.		
11.		
12.		

Name of Tenderer	Signature	Date

2. I / We confirm that no communications were received from the Department of Public Works and Infrastructure before the submission of this tender offer, amending the tender documents.

Name of Tenderer	Signature	Date

DPW-22 (EC): PARTICULARS OF ELECTRICAL CONTRACTOR

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender no:	H25/008 AI	Reference no:	WCS 056397

Name of Electrical Contractor:	
Address:	
Electrical Contractor registration number at the Department of Labour	

Name of Tenderer	Signature	Date

DPW-23 (EC): SCHEDULE FOR IMPORTED MATERIALS AND EQUIPMENT

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender no:	H25/008 AI	Reference no:	WCS 056397

This schedule should be completed by the tenderer. *(Attach additional pages if more space is required)*

Item	Material / Equipment	Rand (R) (Excluding VAT)
1.		R
2.		R
3.		R
4.		R
5.		R
6.		R

Provide additional list if space provided is insufficient.

The Contractor shall list imported items, materials and/or equipment which shall be excluded from the Contract Price Adjustment Provisions (if applicable) and shall be adjusted in terms of currency fluctuations only. Copies of the supplier's quotations for the items, materials or equipment (provided that such costs shall not be higher than the relevant contract rate as listed above) should be lodged with the Principal Agent / Engineer of the Department of Public Works and Infrastructure within 60 (sixty) days from the date of acceptance of the tender. No adjustment of the local VAT amount, nor the contractor's profit, discount, mark-up, handling costs, etc. shall be allowed.

These net amounts will be adjusted as follows:

FORMULA:

The net amount to be added to or deducted from the contract sum:

$$A = V \left(\frac{Z}{Y} - 1 \right)$$

A = the amount (R) of adjustment

V = the net amount (supplier's quotation) (R) of the imported item

Y = exchange rate at the closing date of tender submission

Z = exchange rate on the date of payment.

Name of Tenderer	Signature	Date



public works
& infrastructure

Department:
Public Works and Infrastructure
REPUBLIC OF SOUTH AFRICA

DECLARATION – EPWP PROGRAMME

I _____ from the company

Hereby Undertake To Comply To:

1. LABOUR INTENSIVE CONTRUCTION METHODS (LIC)

- 1.1. Comply To Implementation Of LIC B.O.Q Items Specified Elsewhere in The Tender Documents

~~2. RECRUITMENT AND PLACEMENT OF EPWP NYS PARTICIPANTS (Not Applicable)~~

- ~~2.1. Recruitment, Placement And Exposure Training Of ____ (____) Participants~~
~~2.2. Comply To EPWP B.O.Q, Specifications And Code Of Good Practice~~

3. RECRUITMENT AND PLACEMENT OF LOCAL LABOURERS

- 3.1. Recruitment And Placement Of 15 (Fifteen) Local Labourers
3.2. Comply With Applicable Wage Order/Determination or Agreement, in Terms of Labour Relations Act or Wage Act.

4. COMPLY TO EPWP MONTHLY REPORTING REQUIREMENTS

Monthly, Prepare And Submit Below EPWP Reports Attached To Monthly Payments Certificate:

- 4.1. All Employees and EPWP Participants Contracts
4.2. All Employees and EPWP Participants Certified SA ID Copies
4.3. All Employees and EPWP Participants Attendance Registers
4.4. All Employees and EPWP Participants Proof of Payment
4.5. EPWP Reports Populated on Standard Templates

5. PENALTY FOR NON COMPLIANCE

Acknowledge Non Compliance Penalty of R 3000.00 (Three Thousands Rand) Per Month Per Participants

Signed by : _____
Director of the Company

Company name : _____

Date : _____

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

THE CONTRACT

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

PART C1 AGREEMENT AND CONTRACT DATA

DPW-05: (EC) CONTRACT DATA - GCC 2015: 3RD EDITION

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)				
Tender no:	H25/008 AI	WCS no:	056397	Reference no:	WCS 056397

	The Conditions of Contract applicable to this Contract are clauses 1 to 10 and contract price adjustment schedule of the GENERAL CONDITIONS OF CONTRACT FOR CONSTRUCTION WORKS, THIRD EDITION (2015) prepared by The South African Institution of Civil Engineering Private Bag X200, Halfway House, 1685. Contractors are cautioned to read the GCC Third Edition (2015) and Contract Data [DPW-05 (EC)] together as some clauses in the GCC Third Edition (2015) have been amended in the Contract Data [DPW-05 (EC)] Specific data, which together with these General Conditions of Contract, collectively describe the risks, liabilities and obligations of the contracting Parties and the procedures for the administration of the Contract. Clauses as amended in the Contract Data amends or replaces the corresponding clauses in the GCC Third Edition (2015). Copies of these conditions of contract may be obtained through www.saice.org.za.

	CONTRACT VARIABLES THE SCHEDULE (Contract Data [1.1.1.8]) The schedule is the listed variables in this agreement and contains all variables referred to in this document including specific changes made to GCC Third Edition (2015) documentation. It is divided into part 1: contract data completed by the employer and part 2: contract data completed by the contractor. Part 1 must be completed in full and included in the tender documents. Both the part 1 and part 2 form part of this agreement Spaces requiring information must be filled in, shown as ‘not applicable’ but not left blank. Where choices are offered, the non-applicable items are to be deleted. Where insufficient space is provided the information should be annexed hereto and cross referenced to the applicable clause of the schedule. Key cross reference clauses are italicised in [] brackets

PART 1: CONTRACT DATA COMPLETED BY THE EMPLOYER:

A PROJECT INFORMATION

A 1.0 Works [1.1.1.35]

Works description	Refer to document PG01.1 (EC) – Scope of Works for detailed description
ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)	

Tender / Quotation no: H25/008 AI

A 2.0 Site [1.1.1.29]

Erf / stand number	
Site address	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY
Township / Suburb	
City / Town	Port Nolloth
Province	Northern Cape
Local authority	Namakwa District Municipality
GPS Coordinates	Alexander Bay LPOE: 28.5683° S 16.5058° E Vioolsdrift LPOE: 28.7699° S 17.6254° E Onseepkans LPOE: 28.7345° S 19.3056° E

A 3.0 EMPLOYER AND ITS REPRESENTATIVE

A 3.1 Employer:

Official Name of Organ of State / Public Sector Body	Government of the Republic of South Africa in its Department of Public Works & Infrastructure		
Business registration number	Not applicable	VAT number	Not applicable
E-mail	herman.sagner@dpw.gov.za	Telephone	012 406 1122
Postal address	PRIVATE BAG X65 PRETORIA 0001		
Physical address	256 Madiba Street Pretoria Central Pretorial 0001		

A 3.2 Employer's Representative:

Name	Herman Sagner	Telephone number	012 406 1122
E-mail	herman.sagner@dpw.gov.za	Mobile number	082 908 0577
Postal address	PRIVATE BAG X65 PRETORIA 0001		
Physical address	256 Madiba Street Pretoria Central Pretorial 0001		

Tender / Quotation no: H25/008 AI

A 4.0	Employers Agent/s		
A 4.1	Principal Agent [1.1.1.16]	Discipline	Multi-Disciplinary Consultant (Civil, Electrical, Mechanical Engineering)

Name	Prociv-KNA JV		
Legal entity of above	Prociv-KNA JV	Contact person	Mr. Antony Marunga
Practice number	N/A	Telephone number	011 656 9473
Country	South Africa	Mobile number	083 381 4286
E-mail	amarunga@prociv.co.za		
Postal address	N/A		
Physical address	Unit 6, CMA Office and Conference Park No.1 2 nd Road, Halfway House Estate Midrand 1685		

A 4.2	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

A 4.3	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

Tender / Quotation no: H25/008 AI

A 4.4	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

A 4.5	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

A 4.6	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

Tender / Quotation no: H25/008 AI

A 4.7	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

A 4.8	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

A 4.9	Agent [1.1.1.16]	Discipline	

Name			
Legal entity of above		Contact person	
Practice number		Telephone number	
Country		Mobile number	
E-mail			
Postal address	insert postal address insert suburb insert town insert postal code		
Physical address	insert physical address insert suburb insert town insert postal code		

Tender / Quotation no: H25/008 AI

B CONTRACT INFORMATION

B 1.0 Definitions [1.1.1.2]

Bills of quantities: System / Method of measurement	SANS 1200

B 2.0 Law, regulations and notices [1.3.2]

Law applicable to the works [1.3.2]	Law of the Republic of South Africa

B 3.0 Offer and acceptance [1.1.1.20]

Currency applicable to this agreement [1.1.1.20]	South African Rand

B 4.0 Documents [1.1.1.7]

The original signed agreement is to be held by the principal agent [1.1.1.7], if not, indicate by whom	Employer
Number of copies of construction information issued to the contractor at no cost. (3 Copies of all relevant construction documentation – this to includes 1 priced Bills of Quantities and 2 unpriced Bills of Quantities)	3

Documents comprising the agreement	Page numbers
GCC GENERAL CONDITIONS OF CONTRACT FOR CONSTRUCTION WORKS, THIRD EDITION (2015)	
DPW-05: (EC): GCC 2015: 3RD EDITION	30
The GCC General Preliminaries for use with the GCC 2015: 3RD EDITION	
Contract participation goal documentation as further defined in clause 1.1.1.37 [CD] and B16 [CD]	
Drawings as per drawing register issued with the tender	
Specifications issued with the tender	
Schedules issued with the tender	
Bills of Quantities issued with the tender	
Addenda as issued during tender stage, if applicable	As issued

Tender / Quotation no: H25/008 AI

B 5.0 Employer's agents [3.0]

Authority is delegated to the following agents to issue contract instructions and perform duties for specific aspects of the works [3.0] [3.2.3 [CD]]

Principal Agent
Antony Marunga

Principal agent's and agents' interest or involvement in the works other than a professional interest

B 6.0 Insurances [8.6]

Insurances by contractor

NB: Insurances submitted must be issued by either an insurance company duly registered in terms of the Insurance Act [Long-Term Insurance Act, 1998 (Act 52 of 1998) or Short-Term Insurance Act, 1998 (Act 53 of 1998)] or by a bank duly registered in terms of the Banks Act, 1990 (Act 94 of 1990).
Insured amounts to include VAT.

	The Contract Price [8.6.1.1.1] New Works With a deductible not exceeding 5% of each and every claim [8.6.2]	Contract sum plus 10%	Select
Or	The Contract Price [8.6.1.1.1] Works with alterations and additions (reinstatement value of existing structures / works without or including new works) with a deductible not exceeding 5% of each and every claim [8.6.2]	Contract sum plus 10%	Select
Or	The Contract Price [8.6.1.1.1] Works with practical completion in sections with a deductible not exceeding 5% of each and every claim [8.6.2]	Contract sum plus 10%	Select
	Plant and materials supplied by the Employer [8.6.1.1.2]	R Eng / PQS to determine value	Select
	Professional fees not included in the Contract Price, payable in respect of the repair or reinstatement of damage to the Works or said movables, plus Escalation thereon (if not included above). Minimum R1m unless other amount indicated. [8.6.1.1.3]	R Eng / PQS to determine value	Select
	Direct contractors [8.6.1.1.2] where applicable, to be included in the contract works insurance	R Eng / PQS to determine value	Select
	Special Risks Insurance issued by Sasria [8.6.1.2]	R Eng / PQS to determine value	Select

Tender / Quotation no: H24/XXXX

Public liability insurance [8.6.1.3]	R 5 000 000	Applicable
Ground support insurance [8.6.1.4]	R Eng / PQS to determine value	Select
Subcontractors insurance [8.6.3] where applicable, if not included in works insurance nor by sub-Contractors	R Eng / PQS to determine value	Select
Other insurances [8.6.1.5]		
Free issue where applicable, to be included in the contract works insurance	R Eng / PQS to determine value	Select
Hi Risk Insurance when the project is being executed in a geological area classified as a "High Risk Area" [8.6.8[CD]]	R Eng / PQS to determine value	Select
Other insurances: If applicable, description 1:	R Eng / PQS to determine value	Select
Other insurances; If applicable, description 2:	R Eng / PQS to determine value	Select

B 7.0 Obligations of the employer

Existing premises will be in use and occupied [5.4.1 & 5.4.2]	Applicable
The project will be on a live site. The buildings will be occupied by the End User Clients during the entire duration of the contract	
Restriction of working hours [5.8]	Applicable
As per the operating hours of the border posts	
Natural features and known services to be preserved by the contractor [4.7]	Not Applicable
If applicable, description:	
Restrictions to the site or areas that the contractor may not occupy [5.4.1 & 5.4.2]	Not Applicable
If applicable, description:	

Tender / Quotation no: H25/008 AI

Supply of free issue of material and goods [8.6.1.1.2]	Amount	R	Not Applicable
If applicable, description:			

B 8.0 Subcontractors [4.4]

Not Applicable	If applicable, description of specialisation
Specialisation 1	
Specialisation 2	
Specialisation 3	
Specialisation 4	
Specialisation 5	

B 9.0 Description of different portions of the works, if applicable [5.14.7, B10.3 [CD]]

Not Applicable	If applicable, description of sections
Section 1	
Section 2	
Section 3	
Section 4	
Section 5	
Section 6	
Remainder of the works.	

B 10.0 Contract period [B18: 1.2], Construction period [B18: 1.1], Possession of site [5.4.1], Practical Completion [1.1.1.14, 5.14.1], Completion (Final Approval Certificate) [5.16.1] and Penalties [5.13]

B 10.1 Contract Period

Contract period: Period in **months** as indicated, include the time from the date of award (commencement date [5.2.1]) for submitting contractual obligatory documents, submission of Health & Safety Plan and approval, period for obtaining the Construction Permit (if applicable), the Construction Period and the Defect Liability Period up to and including Final Completion

Tender / Quotation no: H25/008 AI

The contract period is determined as follows (Period/s indicated in months):	
Period to submit contractual obligatory documents including submission and approval of health and safety plan by the appointed Health & Safety Agent	1
Period to obtain Construction Permit from Department of Labour upon approval of the Health & Safety Plan by the appointed Health & Safety Agent	1
Total construction period for the Works as a whole from date of Access to and Possession of the Site up to and including Practical Completion , as indicated below [1.1.1.14, 5.4.1, 5.14.1]	36
Period to achieve Completion [5.14.4]	-
Defect liability period up to and including issuing Final Approval Certificate in months [5.16.1]	12
Total Contract Period	50

B10.2 Construction Period for completion of the Works as a whole

Construction period [B18: 1.2] and Practical Completion for the Works as a whole [5.14.1] The time for achieving Practical Completion of the whole of the Works is measured from the date of Access to and Possession of the site (5.4.1) by the contractor inclusive of all public holidays, special non-working days and builders' holiday shut down periods .	Not Applicable
The date for practical completion for the works as a whole shall be the period in months as indicated, starting from the date of Access to and Possession of the site by the contractor inclusive of all special non-working days and builders' holiday shut down periods [1.1.1.14, 5.4.1, 5.14.1]	Repair Phase = 12 Months Entire Contract = 36 Months
Notification period for inspection in working days by the principal agent.	
Penalty amount per calendar day for late submission of contractual obligatory documents: Ten percent (10%) of the penalty amount per calendar day for late Practical Completion, excluding VAT. [5.13]	R
Penalty amount per calendar day for late Practical Completion , excluding VAT. [5.13].	R
Penalty amount per calendar day for late Completion [5.14.4, 5.13]: Thirty percent (30%) of penalty amount per calendar day for late Practical Completion, excluding VAT.	R
Penalty amount per calendar day for late Final Completion (Issuing of Final Approval Certificate) [5.16, 5.13]: Fifteen percent (15%) of penalty amount per calendar day for late Practical Completion, excluding VAT.	R

Tender / Quotation no: H24/XXXX

B10.3 Construction Period for completion of the Works in portions

Construction period and Practical completion for portions of the Works [5.14.7]		Applicable
Portions of the Works in sections:	1 Repair Phase	2 Maintenance Phase
Notification period for inspection by the principal agent in working days .	2	2
The date for practical completion shall be the period in months as indicated from the date of access and possession of the site by the contractor [1.1.1.14, 5.4.1, 5.14.1]	12	36
The date for practical completion for the whole of the Works, if applicable shall be the period in months as indicated from the date of Access to and Possession of the Site by the contractor inclusive of all public holidays, special non-working days and builders' holiday shut down periods [5.4.1, 12.2.7; 24.1]		36
Penalty for late Practical Completion, if completion in sections is required , excluding VAT [5.13]		
The penalty amount per day for failing to complete Repair Phase of the Works is:		R 1000.00
The penalty amount per day for failing to complete Maintenance Phase of the Works is:		R 500.00
The penalty amount per day for failing to complete section 3 of the Works is:		R N/A
The penalty amount per day for failing to complete section 4 of the Works is:		R N/A
The penalty amount per day for failing to complete section 5 of the Works is:		R N/A
The penalty amount per day for failing to complete section 6 of the Works is:		R N/A
The penalty amount per day for failing to complete the whole of the Works, if applicable, is:		R 1500.00
Penalty amount per calendar day for late submission of contractual obligatory documents: To be calculated at Ten percent (10%) of penalty / calendar day to complete the whole of the Works as indicated above, excluding VAT.		
Penalty amount per calendar day for late Completion [5.14.4, 5.13]: To be calculated at Thirty percent (30%) of penalty / calendar day to complete the whole of the Works , excluding VAT		
Penalty amount per calendar day for late Final Completion (Issuing of Final Approval Certificate) [5.16, 5.13]: To be calculated at Fifteen percent (15%) of penalty / calendar day to complete the whole of the Works , excluding VAT		

B 11.0 Criteria to achieve Practical Completion [1.1.1.14, 5.14.1]

Criteria to achieve Practical Completion not covered in the definition of practical completion	
13.1	All relevant CoCs
13.2	All As-built drawings
13.3	All guarantees and warranties

Tender / Quotation no: H25/008 AI

13.4	Training on electrical, security and mechanical installations if contractually required
13.5	Maintenance / operating manuals
13.6	CPG and cidb BUILD programme achievement certificates submitted with substantiating documentation
13.7	
13.8	
13.9	
13.10	

B 12.0 Defects liability period [5.16]

Defects liability period: Refer B10.1

Applicable	If applicable, description of applicable elements
14.1	All Civil and Structural Engineering Work (Repair and Maintenance)
14.2	All Electrical Engineering Work (Repair and Maintenance)
14.3	All Mechanical Engineering Work (Repair and Maintenance)
14.4	
14.5	
14.6	
14.7	
14.8	
14.9	
14.10	

Tender / Quotation no: H25/008 AI

B 13.0 Payment [6.10]

Date of month for issue of regular payment certificates Refer [6.10.1]	25
Contract price adjustment / cost fluctuations [6.8.2]	Applicable
If yes, method to calculate [6.8.2 [CD]]	Contract price adjustment factor
Employer shall pay the contractor within: Refer [6.10.4 [CD]]	Thirty (30) calendar days

B 14.0 Dispute resolution [10.5 [CD]]

Mediation	YES
Name of nominating body	Association of Arbitrators (Southern Africa)
Appointment of Mediator	State Attorney
Litigation	Court with Jurisdiction

Tender / Quotation no: H25/008 AI

B 15.0 SPECIFIC CHANGES MADE TO GCC 2015: 3RD EDITION

CONTRACT SPECIFIC DATA	
The following contract specific data, referring to the General Conditions of Contract for Construction Works, Third Edition (2015) are applicable to this Contract:	
CLAUSES	COMPULSORY DATA
1.1.1.8	Amend Clause 1.1.1.8 to include the word “rights” to read as follows: “Contract Data” means the specific data which, together with these General Conditions of Contract, collectively describe the rights, risks, liabilities and obligations of the contracting parties and the procedures for the administration of the Contract.
1.1.1.9	Add to Clause 1.1.1.9 the following: “If the Contractor constitutes under the Law of the Republic of South Africa (B2.0) a joint venture, consortium or other unincorporated grouping of two or more persons: (a) these persons shall be deemed to be jointly and severally liable to the Employer for the performance of the Contract; (b) these persons shall notify the Employer of their leader who shall have authority to bind the Contractor and each of these persons; and (c) the Contractor shall not alter its composition or legal status without the prior consent of the Employer.”
1.1.1.13	Amend Clause 1.1.1.13 as follows: “Defects Liability Period” means the period stated in the Contract Data, commencing on the date indicated on the Certificate of Completion for the works as a whole or Certificates of Completion in the event of more than one Certificate of Completion is issued for different parts of the Works, during which the Contractor has both the right and the obligation to make good defects in the materials, Plant and workmanship covered by the Contract. Defects Liability Period is: 12 months . The Defects Liability Period for the works shall commence on the calendar day following the date of the Certificate of Completion for the works as a whole or Certificates of Completion in the event of more than one Certificate of Completion is issued for different parts of the Works and end at midnight (00:00) three hundred and sixty five days (365) calendar days from the date of the Certificate of Completion.
1.1.1.14	Amend Clause 1.1.1.14 as follows: “Due Completion Date” means the date of expiry of the time stated in the Contract Data for achieving Practical Completion of the Works, calculated from the date of Access to and Possession of Site date (5.4.1) and as adjusted by such extensions of time or acceleration as may be allowed in terms of Contract (5.12).
1.1.1.15	The name of the Employer: Refer to A 3.1 [CD]
1.1.1.16	The name of the Employer’s Representative: Refer to A 3.2 [CD]
1.1.1.17	The name of the Employer’s Agent: Refer to A 4.0 and B 5.0 [CD]

Tender / Quotation no: H25/008 AI

1.1.1.20	Amend Clause 1.1.1.20 by inserting the following words at the end of this definition: "If the Acceptance section of the Form of Offer and Acceptance" contains conditional statements or a schedule of deviations is attached to the Form of Offer and Acceptance, then Form of Offer and Acceptance means the Contract Agreement, that shall be substantially in accordance with the form attached to the Scope of Works, and the date of signing the Contract Agreement shall be the date of the Form of Offer and Acceptance"
1.1.1.21.A	Add new Clause 1.1.1.21.A The interest rates applicable on this contract, whether specifically indicated in the relevant clauses or not, will be the rate as determined by the Minister of Finance from time to time, in terms of section 80(1)(b) of the Public Finance Management Act, 1999 (Act No 1 of 1999) as amended, calculated as simple interest, in respect of debts owing to the State, and will be the rate as published by the Minister of Justice and Correctional Services from time to time, in terms of section 1(2) of the Prescribed Rate of Interest Act, 1975 (Act No 55 of 1975) as amended, calculated as simple interest, in respect of debts owing by the State.
1.1.1.27	This Pricing Strategy is a: Re-measurement Contract.
1.1.1.31	Not applicable to this Contract.
1.1.1.35	Insert the definition of "Value of Works" as Clause 1.1.1.35: "Value of Works" means the value of the Works certified by the Employer's Agent as having been satisfactorily executed and shall include the value of the works done, the value of the materials and/or plant and Contract Price Adjustments.
1.1.1.36	Insert the definition of "Latent and Patent Defects" as Clause 1.1.1.36: A 'latent defect' is a material defect, which was not visible after 'reasonable' inspection. The latent defect period commences at the date of Final Approval Certificate and ends 5 years [after that date [5.16.3]. A patent defect is a flaw that is not hidden and ought to be easily identified upon reasonable inspection.
1.1.1.37	Add new Clause 1.1.1.37 Contract participation goals applicable to this Contract are as indicated in B16 [D] and described in the following tender documents: DPW 03 (EC): TENDER DATA, PG 01.1 (EC) SCOPE OF WORK and PG 02.1 (EC) PRICING ASSUMPTIONS.
1.2.3.	Replace Clause 1.2.3. with the following: The Employer's Agent is as indicated in clause B 5.0 and shall have the authority to act on behalf of the employer as indicated in the contract document read with the contract data. [3.2.3].
1.2.6	Add new Clause 1.2.6 The priority of the documents shall be in accordance with the following sequence: (a) The Form of Offer and Acceptance and the signed Schedule of Deviations, (b) Contract Data, (c) These General Conditions of Contract, (e) Scope of Work, and (f) Pricing Data
1.3.4	Not applicable to this Contract.

Tender / Quotation no: H25/008 AI

1.3.5	Replace Clause 1.3.5 with the following: (a) The Employer will become the owner of the information, documents, advice, recommendation and reports collected, furnished and/or compiled by the Contractor during the course of, and for the purposes of executing this Contract, all of which will be handed over to the Employer on request during the contract, but in any event on completion of contract, the termination and/or cancellation of this Contract for whatever reason. The Contractor relinquishes its lien / retention or any other rights thereon to which it may be entitled. (b) The copyright of all documents, recommendations and reports compiled by the Contractor during the course of and for the purposes of finalizing the Works will vest in the Employer, and may not be reproduced or distributed or made available to any person outside the Employer's service, or to any institution in any way, without the prior written consent of the Employer. The Employer shall have the right to use such material for any other purpose without the approval of information or payment to the Contractor. (c) The copyright of all electronic aids, software programmes etc. prepared or developed in terms of the Contract shall vest in the Employer, who shall have the right to use such material for any other purpose without the approval of, information or payment to the Contractor. (d) In case of the Contractor providing documents, electronic aids, software programs or like material to the Employer, the development of which has not been at the expense of the Employer, copyright shall not vest in the Employer. The Contractor shall be required to indicate to which documents, electronic aids, software programs or like material this provision applies. (e) The Contractor hereby indemnifies the Employer against any action, claim, damages or legal cost that may be instituted against the Employer on the grounds of an alleged infringement of any copyright, patents or any other intellectual property right in connection with the Works outlined in this Contract. (f) All information, documents, recommendations, programs and reports collected or compiled must be regarded as confidential and may not be communicated or made available to any person outside the Employer's service and may not be published either during the currency of this Contract or after termination thereof without the prior written consent of the Employer.
1.3.7	Replace Clause 1.3.7 with the following By entering into this contract, the Contractor waives any lien that he may have or acquire, notwithstanding any other condition/s in this contract.
3.2.3	Add to Clause 3.2.3 the following: 1. The Employer's Principal Agent's authority to act and/or to execute functions or duties or to issue instructions are expressly excluded in respect of the following, unless same has been approved by the employer: (a) Appointment of Subcontractors – clause 4.4.4; (b) Granting of an extension of time and/or ruling on claims associated with claims for extension of time – clauses 5.12, 10.1.5; (c) Acceleration of the rate of progress and determination of the cost for payment of such acceleration – clause 5.12.4; (c) Rulings on claims and disputes – clauses 10.1.5, 10.2.3 and 10.3.3; (d) Suspension of the Works – clause 5.11.2; (e) Final Payment Certificate – clause 6.10.9;

Tender / Quotation no: H25/008 AI

	(f) Issuing of <i>mora</i> notices to the Contractor – clauses 9.1.1, 9.1.2.1 and 9.2.1; (g) Cancellation of the contract between the Employer and Contractor – clauses 9.1.1, 9.1.2.1 and 9.2.1. (h) Any variation orders – clause 6.3.1 2. In order to be legally binding and have legal bearing and consequence, any ruling in respect of the above matters (a) to (h) must be on an official document, signed and issued by the Employer to the Contractor. 3. The Contractor must submit claims, demands, notices, notifications, updated particulars and reports in writing, as well as any other supporting documentation pertaining thereto, in respect of any of the above listed matters (a) to (h), to the Employer's Agent within the time periods and in the format(s) as determined in the relevant clauses of the Conditions of Contract. Failing to deliver such to the Employer's Agent and in the correct format will invalidate any claim and the consequences of such failure will <i>mutatis mutandis</i> be as stated in clause 10.1.4. 4. Clauses 6.10.9 and 10.1.5 shall be amended as follows to indicate the limitation on the Employer's Agent authority in respect thereof: Clause 6.10.9 – Amend to read as follows: Within 14 days of the date of final approval as stated in the Final Approval Certificate, the Contractor shall deliver to the Employer's Agent a final statement claiming final settlement of all moneys due to him (save in respect of matters in dispute, in terms of Clauses 10.3 to 10.11, and not yet resolved). The Employer's Agent shall within 14 days issue to the Contractor a Final Payment Certificate the amount of which shall be paid to the Contractor within 30 days of the date of such certificate, after which no further payments shall be due to the Contractor (save in respect of matters in dispute, in terms of Clauses 10.3 to 10.11 and not yet resolved). Clause 10.1.5 – Amend to read as follows: Unless otherwise provided in the Contract, the Employer shall, within 28 days after the Contractor has delivered his claim in terms of Clause 10.1.1 as read with Clause 10.1.2, deliver to the Contractor his written and adequately reasoned ruling on the claim (referring specifically to this Clause). The amount thereof, if any, allowed by the Employer shall be included to the credit of the Contractor in the next payment certificate. If no ruling has been made within the 28 days, as referred to in clause 10.1.5. or any extension thereof as agreed to by the parties, the claim shall be regarded as rejected by the Employer. 5. Insert the following under 3.2.3: Provided that, notwithstanding any provisions to the contrary in the Contract, the Employer shall have the right to reverse and, should it deem it necessary, to amend any certificate, instruction, decision or valuation of the Employer's Agent and to issue a new one, and such certificate instruction, decisions or valuations shall for the purposes of the Contract be deemed to be issued by the Employer's Agent, provided that the Contractor shall be remunerated in the normal manner for work executed in good faith in terms of an instruction issued by the Employer's Agent and which has subsequently been rescinded.
3.3.2.1	Amend Clause 3.3.2.1 to insert the word "plant" to read as follows: Observe how the Works are carried out, examine and test materials, plant and workmanship, and receive from the Contractor such information as he shall reasonably require.

Tender / Quotation no: H25/008 AI

3.3.2.2.3	Add to Clause 3.3.2.2.3 the following: All oral communication must be reduced into writing to be binding on the parties.
3.3.2.2.4	Add to Clause 3.3.2.2.4 the following: All oral communication must be reduced into writing to be binding on the parties.
3.3.3.2	Amend Clause 3.3.3.2 to insert the word “plant” to reads as follows: Notwithstanding any authority assigned to him in terms of Clauses 3.3.2 and 3.3.4, failure by the Employer’s Agent’s Representative to disapprove of any work, workmanship, plant or materials shall not prejudice the power of the Employer’s Agent’s thereafter to disapprove thereof and exercise any of his powers in terms of the Contract in respect of thereof.
4.4.4	Ref Clause 3.2.3.
4.4.6	Not applicable to this Contract.
4.8.2.1	Amend Clause 4.8.2.1 to include the word “person”, as follows: Makes available to the Employer, or to any such contractor, person or authority, any roads or ways for the maintenance of which the Contractor is responsible, or
4.8.2.2	Amend Clause 4.8.2.2 to include “Employer” and “contractors”, as follows: Provides any other facility or service of whatsoever nature to the Employer or to any of the said contractors, persons or authorities,
4.12.3	Add to Clause 4.12.3 the following: All oral communication must be reduced into writing to be binding on the parties.
5.3.1	Add to Clause 5.3.1: The documentation required before commencement with Works execution are: • Health and Safety Plan to be provided within 14 calendar days from award (Ref Clause 4.3) • Initial programme to be provided within 21 calendar days of handing over the site to the contractor (Clause 5.6) • Security (C1.0, Clause 6.2) • Insurance/s (B6, Clause 8.6)
5.3.2	Add to Clause 5.3.2: The time to submit the documentation required before commencement with Works execution is: 21 calendar days.
5.4.2	Add to Clause 5.4.2: The access to, and possession of, the Site referred to in Clause 5.4.1 shall be NOT EXCLUSIVE to the Contractor. In the event of access to, and possession of, the Site is not exclusive to the Contractor, the following limitations apply: N/A

Tender / Quotation no: H25/008 AI

5.6.2.2	Replace Clause 5.6.2.2 with the following: The sequence, timing of activities and resources for carrying out the Works.
5.6.2.7	Add the following to Clause 5.6.2.7: Updated cash flows and construction programme/s to be submitted on a monthly basis to the Employer's Agent and the Employer.
5.8.1	Add the following to Clause 5.8.1: The non-working days are: Saturdays and Sundays The special non-working days are: Public Holidays and the year-end break annually published by the BCCEI (Bargaining Council for the Civil Engineering Industry)
5.9.1	Amend Clause 5.9.1 as follows: On the Commencement Date, the Engineer shall deliver to the Contractor three (3) copies, at no cost to the Contractor, of the drawings and any instructions required for the commencement of the Works. The cost of any additional copies of such drawings and/or instructions, as may be required by the Contractor, will be for the account of the Contractor.
5.11.2	Ref Clause 3.2.3
5.12	Ref Clause 3.2.3
5.12.2.2	Amend Clause 5.12.2.2 as following: "Abnormal climatic conditions, therefore any weather conditions i.e. rain, wind (speed or dust), snow, frost, temperature (cold or heat) that have an adverse effect on the progress of the Works and during which no work is possible on site."
5.13.1	Add the following to Clause 5.13.1: The penalty for failing to complete the Works: Refer to B10 CD
5.14.1	Amend the second paragraph of Clause 5.14.1 as follows: When the Works are about to reach the said stage, the Contractor shall, in writing, request a Certificate of Practical Completion and the Employer's Agent shall, within 14 days after receiving such request, issue to the Contractor a written list setting out the work to be completed to justify Practical Completion. Should the Employer's Agent not issue such a list within the 14 days, the Contractor shall notify the Employer accordingly. Should the Employer not issue such a list within 7 days of receipt of such notice, Practical Completion shall be deemed to have been achieved on the 14th day after the contractor requested the Certificate of Practical Completion.
5.14.4	Add the following to Clause 5.14.4: Penalty for late Completion will be 30% of penalty applicable to late Practical Completion / calendar day. Penalty for late Final Completion will be 15% of penalty applicable to late Practical Completion / calendar day.
5.16.1	Amend Clause 5.16.1 by deleting the provision in the third paragraph of this clause.

Tender / Quotation no: H25/008 AI

5.16.2	Amend Clause 5.16.2 as follows: No certificate other than the Final Approval Certificate referred to in Clause 5.16.1 shall be deemed to constitute approval of the Works or shall be taken as an admission of the due performance of the Contract or any part thereof, nor of the accuracy of any claim made by the Contractor, nor shall any other certificate exclude or prejudice any of the powers of the Employer's Agent and/or the Employer.
5.16.3	The latent defect period for all works is: 5 years
6.2.1	The type of security for the due performance of the Contract, as selected by the Contractor in the Contract Data, must be delivered to the Employer.
6.2.3	Amend Clause 6.2.3 as follows: If the Contractor has selected a performance guarantee as security, he shall ensure that it remains valid and enforceable as required in terms of the Contract.
6.3.1	Amend first paragraph to Clause 6.3.1 as follows: If, at any time before the issue of the Practical Completion, the Employer's Agent shall require any variation of the form, quality or quantity of the Works or any part thereof provided that such Variation Order shall not substantially alter the Scope of Work, he shall have power to order the Contractor to do any of the following subject to obtaining approval from the Employer (3.2.3):
6.5.1.2.3	The percentage allowance to cover overhead charges is 33%, except on material cost where the percentage allowance is 10%.
6.8.2	When Contract Price Adjustment is applicable [B13] the value of payment certificates is to be adjusted by a Contract Price Adjustment Factor (CPAF): The value of the certificates issued shall be adjusted in accordance with the Contract Price Adjustment Factor with the following values: The value of "x" is 0.15. The values of the coefficients are: a = 0.25. (Labour) b = 0.3 (Contractor's equipment) c = 0.3 (Material) d = 0.15 (Fuel) The values of the coefficients for "Repair and Maintenance Project" (RAMP) contracts are: a = 0.35 (Labour) b = 0.20 (Contractor's equipment) c = 0.35 (Material) d = 0.10 (Fuel) The urban area nearest the Site is SPRINGBOK, NORTHERN CAPE. <i>(Select urban area from Statistical News Release, P0141, Table A)</i> The applicable industry for the Construction Material Price Index for materials / plant is Civil Engineering Material. <i>(Select the applicable industry from Statistical News Release, P0151.1, Tables 2,4,5)</i> The area for the Producer Price Index for fuel is SPRINGBOK, NORTHERN CAPE. <i>(Select the area from Statistical News Release, P0142.1, Table 1.)</i> The base month is August 2025. <i>(The month prior to the closing of the tender.)</i>

Tender / Quotation no: H25/008 AI

6.8.3	Price adjustments for variations in the costs of special materials are not allowed.
6.9.1	Replace Clause 6.9.1 with the following: “Plant and materials will only be certified and paid for upon furnishing proof of ownership by the contractor. Once paid, material and goods shall become the property of the Employer and shall not be removed from site without the written authority of the Employers Agent.
6.10.1	Add at end of Clause 6.10.1 The contractor shall provide the Employer’s Agent every month, on dates as agreed between parties / instructed by the Principal Agent, with the following information: (a) Monthly Local content report, (b) EPWP / NYS payment register, labour reports and certified ID document of EPWP/ NYS beneficiaries, Contract between Contractor and EPWP/ NYS beneficiaries, attendance register. (if applicable) (c) Tax Invoice (d) Labour intensive report (e) Contract participation goal reports (f) Updated construction programme (g) Revised cash flows
6.10.1.5	The percentage advance on materials not yet built into the Permanent Works is: 85 % .
6.10.3	The limit of retention money is dependent on the security to be provided by the Contractor in terms of Clause 6.2.1.
6.10.4	Replace “28 days” with “30 days” provided all required documents including an invoice have been submitted and are correct in all respects.
6.10.5	Replace Clause 6.10.5 with the following: <u>In respect of contracts up to R2 million and in respect of contracts above R2 million where the Contractor elects a security by means of a 10% retention, 50% of the retention shall be released to the Contractor when the Employer’s Agent issues the Certificate of Completion in terms of clause 5.14.4. The remaining 50% of the retention shall be released in accordance with the provisions of the conditions of contract and will become due and payable when the Contractor becomes entitled, in terms of Clause 5.16.1, to receive the Final Approval Certificate.</u> <u>In respect of contracts above R2 million, where the Contractor elects a security by means of a cash deposit or fixed guarantee of 5% of the Contract Sum (excl. VAT) and a 5% retention of the Value of the Works (excl. VAT), the cash deposit or fixed guarantee, whichever is applicable, shall be refunded to the Contractor or return to the guarantor, respectively, when the Employer’s Agent issues the Certificate of Completion in terms of Clause 5.14.4. The 5% retention of the Value of the Works (excl. VAT) shall become due and payable when the Contractor becomes entitled, in terms of Clause 5.16.1, to receive the Final Approval Certificate.</u> <u>In respect of contracts above R2 million, where the Contractor elects a security by means of a cash deposit or a variable guarantee of 10% of the Contract Sum (excl. VAT), the cash deposit or the variable guarantee, whichever is applicable, will be reduced to 5% of the Value of the Works (excl. VAT) when the Employer’s Agent issues the Certificate of Completion in terms of Clause 5.14.4. The balance of the cash deposit shall become due and payable or the variable guarantee shall expire when the Contractor becomes entitled in terms of Clause 5.16.1 to receive the Final Approval Certificate.</u>

Tender / Quotation no: H25/008 AI

6.10.6.2	Replace Clause 6.10.6.2 with the following: “In the event of failure by the Employer to make the payment by the due date, he shall pay to the Contractor interest, at the rate as published by the Minister of Justice and Correctional Services from time to time, in terms of section 1(2) of the Prescribed Rate of Interest Act, 1975 (Act No 55 of 1975) as amended, calculated as simple interest, in respect of debts owing by the State”. (1.1.1.21.A).
6.10.9	Ref Clause 3.2.3.
7.2.1	The last sentence to read “Failing requirements or instructions, the Plant, workmanship and materials of the respective kinds shall be suitable for the intended purpose provided that materials procured for the works are from South African manufactures and suppliers. Imported materials shall only be considered under exceptional circumstances, based on compelling technical justifications, and subject to the approval by the DPWI. Failing to comply, unless specified or approval granted will result in a ten percent (10%) penalty of the value of imported material used without approval.
7.5.3	Add the following to Clause 7.5.3 “Should the work inspected by the Employer’s Agent be rejected, all consultant’s fees / costs pertaining to the unsuccessful inspection shall be recovered from the contractor”.
7.9.1	Insert the following at the end of Clause 7.9.1: Provided that, should the Contractor on demand not pay the amount of such costs to the Employer, such amount may be determined and deducted by the Employer from any amount due to or that may become due to the Contractor under this or any other previous or subsequent contract between the Contractor and the Employer.
8.2.2.1	Insert the following as a second paragraph to Clause 8.2.2.1: The Contractor shall at all times proceed immediately to remove or dispose of any debris arising from damage to or destruction of the Works and to rebuild, restore, replace and/or repair the Works, failing which the Employer may cause same to be done and recover the reasonable costs associated therewith from the Contractor.
8.3.1.10	Replace Clause 8.3.1.10 with the following: “Ionising, radiation, or contamination by radioactivity from any nuclear fuel, or from any nuclear waste from the combustion of nuclear fuels, excluding leakages of any radioactive material / gases / corrosive liquids/chemicals, which are harmful to the environment and biological life, brought on to site for installation or used in the Works prior to final approval”.
8.4.3	Add the following as Clause 8.4.3: Where the Contractor has caused damage to property (moveable and immovable), of any person, the Employer or third parties, the Contractor shall on receiving a written instruction from the Employer’s Agent immediately proceed at his own cost to remove or dispose of any debris and to rebuild, restore, replace and/or repair such property and to execute the Works.
8.6.1	Replace Clause 8.6.1 with the following: Except if provided otherwise in the Contract Data, the Contractor, without limiting his obligations in terms of the Contract, shall effect and keep the respective insurances [CD] in force, in favour of the employer as beneficiary, from the date of possession of the site until the issue of the certificate of practical completion and with an extension to cover the contractors obligations after the date of practical completion [8.2.1]
8.6.1.1.1	Ref B6.0 CD for value of insurance.
8.6.1.1.2	Ref B6.0 CD for value of insurance.

Tender / Quotation no: H25/008 AI

8.6.1.1.3	Ref B6.0 CD for value of insurance.
8.6.1.3	Amend Clause 8.6.1.3 as follows: Liability insurance that covers the Contractor against liability for the death of, or injury to any person, or loss of, or damage to any property (other than property while it is insured in terms of Clause 8.6.1.1) arising from or in the course of the fulfilment of the Contract, from the Commencement Date to the date of the end of the Defects Liability Period, if applicable, or otherwise to the issue of the Certificate of Completion.
8.6.4	Not applicable to this Contract.
8.6.6	Replace Clause 8.6.6 with the following: Without limiting the contractor's obligations in terms of the contract, the contractor shall, within twenty-one (21) calendar days of the date of letter of acceptance, but before commencement of the works, submit to the employer all the policies by which the insurances are effected and due proof of upfront payment of all premiums thereunder to keep the policies effective from the Commencement Date to the date of the end of the Defects Liability Period, if applicable, or otherwise to the issue of the Certificate of Completion.
8.6.7	Replace Clause 8.6.7 with the following: If the Contractor fails to effect and keep in force any of the insurances referred to in Clause 8.6.1, the Employer may cancel the Contract in terms of Clause 9.2.
8.6.8	Add new Clause 8.6.8. HIGH RISK INSURANCE In the event of the project being executed in a geological area classified as a "High Risk Area", that is an area which is subject to highly unstable subsurface conditions that might result in catastrophic ground movement evident by sinkhole or doline formation the following will apply: (1) Damage to the Works The Contractor shall, from the date of Commencement of the Works until the date of the Certificate of Completion, bear the full risk of and hereby indemnifies and holds harmless the Employer against any damage to and/or destruction of the Works consequent upon a catastrophic ground movement as mentioned above. The Contractor shall take such precautions and security measures and other steps for the protection of the Works as he may deem necessary. When so instructed to do so by the Employer's Agent, the Contractor shall proceed immediately to remove and/or dispose of any debris arising from damage to or destruction of the Works and to rebuild, restore, replace and/or repair the Works, at the Contractor's own costs. (2) Injury to Persons or Loss of or damage to Properties The Contractor shall be liable for and hereby indemnifies and holds harmless the Employer against any liability, loss, claim or proceeding arising during the Contract Period whether arising in common law or by Statute, consequent upon personal injuries to or the death of any person whomsoever resulting from, arising out of or caused by a catastrophic ground movement as mentioned above. The Contractor shall be liable for and hereby indemnifies the Employer against any and all liability, loss, claim or proceeding consequent upon loss of or damage to any moveable, or

Tender / Quotation no: H25/008 AI

	immovable or personal property or property contiguous to the Site, whether belonging to or under the control of the Employer or any other body or person whomsoever arising out of or caused by a catastrophic ground movement, as mentioned above, which occurred during the Contract Period. (3) It is the responsibility of the Contractor to ensure that he has adequate insurance to cover his risk and liability as mentioned in Clauses 8.6.8(1) and 8.6.8 (2) above. Without limiting his obligations in terms of the Contract, the Contractor shall, within 21 days of the Commencement Date and before Commencement of the Works, submit to the Employer proof of such insurance policy, if requested to do so. (4) The Employer shall be entitled to recover any and all losses and/or damages of whatever nature suffered or incurred consequent upon the Contractor's default of his obligations as set out in Clauses 8.6.8 (1), 8.6.8 (2) and 8.6.8 (3). Provided that, should the Contractor on demand not pay the amount of such costs to the Employer, such amount may be determined and deducted by the Employer from any amount due to or that may become due to the Contractor under this or any other existing or subsequent contract between the Contractor and the Employer.
9.1.1	Ref Clause 3.2.3
9.1.2.1	Ref Clause 3.2.3
9.1.4	Replace the first paragraph of Clause 9.1.4 with the following: "In the circumstances referred to in Clauses 9.1.1, 9.1.2 or 9.1.3 (provided that the circumstances in 9.1.3 is not due to the fault of the Contractor, his employees, contractors or agents), and whether or not the Contract is terminated under the provisions of this Clause, the Contractor shall be entitled on proof of payment of any increased cost of or incidental to the execution of the Works which is specifically attributable to, or consequent upon the circumstances defined in Clauses 9.1.1, 9.1.2 or 9.1.3; necessary changes"
9.1.5	Replace the first paragraph of Clause 9.1.5 with the following: If the Contract is terminated on any account in terms of this Clause (provided that the circumstances in 9.1.3 is not due to the fault of the Contractor, his employees, contractors or agents) , the Contractor shall be paid by the Employer (insofar as such amounts or items have not already been covered by payments on account made to the Contractor) for all measured work executed prior to the date of termination, the amount (without retention), payable in terms of the Contract and, in addition: "
9.1.5.5	Not applicable to this Contract.
9.1.6	Not applicable to this Contract.
9.2.1	Ref Clause 3.2.3
9.2.1.3.9	Add new Clause 9.2.1.3.9: Has failed to effect and keep in force any of the insurances referred to in Clause 8.6.1.
9.2.4	Add the following as Clause 9.2.4: In the case where a contract is terminated by the Employer by no fault by any party, the contractor shall be entitled to no other compensation than for work done and materials on site as certified by the Principal Agent at the date of termination.

Tender / Quotation no: H25/008 AI

9.3.2.2	Replace Clause 9.3.2.2 with the following: All Plant and Construction Equipment, Temporary Works and unused materials brought onto the Site by the Contractor, and where ownership has not been transferred to the Employer (see Clause 6.9.1), shall be removed from the Site on termination of the contract by any party.
9.3.2.3	Not applicable to this Contract.
9.3.3	Add the following at the end of Clause 9.3.3 After cancellation of the Contract by the Contractor, the Contractor, when requested by the Employer to do so, shall not be entitled to refuse to withdraw from the Works on the grounds of any lien or a right of retention or on the grounds of any other right whatsoever. Nothing in this Clause shall prejudice the right of the Contractor to exercise, either in lieu of or in addition to the Contractor rights and remedies specified in this Clause, any other rights or remedies to which the Contractor may be entitled under the Contract or common law.
10.1.3.1	Replace Clause 10.1.3.1 with the following: All facts and circumstances relating to the claims shall be investigated as and when they occur or arise. For this purpose, the Contractor shall deliver to the Employer's Agent, records in a form approved by the Employer's Agent, of all the facts and circumstances which the Contractor considers relevant and wishes to rely upon in support of his claims, including details of all construction equipment, plant, labour, and materials relevant to each claim. Such records shall be submitted promptly after the occurrence of the event giving rise to the claim.
10.1.3.6	Replace Clause 10.1.3.6 with the following: The Employer, the Employer's Agent and the Contractor shall in any proceedings in accordance with Clauses 10.3 and 10.11 be entitled to give or lead evidence of or rely on any fact or circumstance not recorded in terms of this Clause, if other party to the dispute is prejudiced by such non-recording of the facts.
10.1.4	Ref Clause 3.2.3.
10.1.5	Ref Clause 3.2.3.
10.1.6	Add new Clause 10.1.6: If the Employer fails to give his ruling within the period referred to in Clause 10.1.5 he shall be deemed to have given a ruling dismissing the claim.
10.1.3.6	Replace Clause 10.1.3.6 with the following: The employer, the Employer's Agent and the Contractor shall in any proceedings in accordance with Clauses 10.3 and 10.11 be entitled to give or lead evidence oof or rely on any fact or circumstance not recorded in terms of the Clause, if the other party to the dispute in prejudiced by such nor-recording of the facts.
10.2.1	Replace Clause 10.2.1 with the following: In respect of any matter arising out of or in connection with the Contract, which is not required to be dealt with in terms of Clause 10.1 or which does not require the decision or ruling of the Employer, the Contractor or the Employer shall have the right to deliver a written dissatisfaction claim to the Employer's Agent. This written claim shall be supported by particulars and substantiated.

Tender / Quotation no: H25/008 AI

10.2.2	Replace Clause 10.2.2 with the following: If, in respect of any matter arising out of or in connection with the Contract, which is not required to be dealt with in terms of Clause 10.1 or which does not require the decision or ruling of the Employer, the Contractor or the Employer fails to submit a claim within 28 days after the cause of dissatisfaction, he shall have no further right to raise any dissatisfaction on such matter.
10.2.3	Ref clause 3.2.3.
10.3.2	Replace Clause 10.3.2 with the following: If either party shall have given notice in compliance with Clause 10.3.1, the dispute shall be referred immediately to mediation under Clause 10.5, unless amicable settlement is contemplated.
10.3.3	Replace Clause 10.3.3 with the following:: In respect of a ruling given by the Employer (Ref clause 3.2.3), and although the parties may have delivered a Dispute Notice, the ruling shall be in full force and carried into effect unless and until otherwise agreed by both parties, or in terms of a mediation decision or court judgement.
10.4.2	Replace Clause 10.4.2 with the following: If the other party rejects the invitation to amicable settlement in writing, or does not respond in writing to the invitation within 14 days, or amicable settlement is unsuccessful, referral to mediation shall follow immediately. Should mediation be unsuccessful, the dispute shall be resolved by Litigation.
10.4.4	Replace Clause 10.4.4 with the following: Save for reference to any portion of any settlement, or decision which has been agreed to be final and binding on the parties, no reference shall be made by or on behalf of either party in any subsequent court proceedings, to any outcome of an amicable settlement, or to the fact that any particular evidence was given, or to any submission, statement or admission made in the course of the amicable settlement.
10.5	Replace Clause 10.5 with the following: The parties may, by agreement and at any time before Litigation, refer a dispute to mediation, in which event: 10.5.1 The appointment of a mediator, the procedure, and the status of the outcome shall be agreed between the parties. 10.5.2 Regardless of the outcome of a mediation the parties shall bear their own costs concerning the Mediation and equally share the costs of the mediator and related expenses.
10.6	Not applicable to this Contract.
10.7	Not applicable to this Contract.
10.10.3	Replace Clause 10.10.3 with the following: The court shall have full power to open up, review and revise any ruling, decision, order, instruction, certificate or valuation of the Employer's Agent and Employer and neither party shall be limited in such proceedings before such court to the evidence or arguments put before the Employer's Agent or Employer for the purpose of obtaining his ruling.

Tender / Quotation no: H25/008 AI

B 16.0 CONTRACT PARTICIPATION GOAL TARGETS AND CIDB B.U.I.L.D. PROGRAMME

The contractor shall achieve in the performance of the contract the following Contract Participation Goals (CPGs) as described in PG-01.2 (EC): Scope of Work and PG-02.2 (EC): Pricing Assumptions and in accordance with the feasibility study, which forms part of the specifications in the CPG Section of the Specification of this contract.

(a)	Minimum Targeted Local Manufacturers of Material Contract Participation Goal, in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	<i>Applicable</i>
(b)	Minimum Targeted Local Building Material Suppliers Contract Participation Goal in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	<i>Applicable</i>
(c)	Minimum Targeted Local Labour Skills Development Contract Participation Goal in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	<i>Applicable</i>
(d)	cidb BUILD Programme: Minimum Targeted Enterprise Development Contract Participation Goal in accordance with the cidb Standard for Indirect Targeting for Enterprise Development through Construction Works Contracts, No 36190 Government Gazette, 25 February 2013, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	<i>Applicable</i>
(e)	cidb BUILD Programme: Minimum Targeted Contract Skills Development Goal in accordance with the cidb Standard for Developing Skills through Infrastructure Contracts as published in the Government Gazette Notice No. 48491 of 28 April 2023. and the cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.	<i>Applicable</i>
(f)	DPWI National Youth Service training and development programme (NYS) – Condition of Contract.	<i>Not applicable</i>
(g)	Labour Intensive Works – Condition of Contract. (Applicable to all CE projects and all GB projects ≥ R 30 million where feasible.)	<i>Applicable</i>
(h)		<i>Select</i>
(i)		<i>Select</i>

Tender / Quotation no: H25/008 AI

PART 2: CONTRACT DATA COMPLETED BY THE TENDERER:

C TENDERER'S SELECTIONS

C 1.0 Securities [11.0]

In respect of contracts with a contract sum up to R1 million, the security to be provided by the contractor to the employer will be a payment reduction of five per cent (5%) of the value certified in the payment certificate (excluding VAT).

In respect of contracts with a contract sum more than R1 million, the security to be provided by the contractor to the employer will be selected by the Contractor as indicated below:

Guarantee for construction: Select Option A, B, C, D or E

Option A	cash deposit of 10 % of the contract sum (excluding VAT)
Option B	variable construction guarantee of 10 % of the contract sum (excluding VAT) (DPW-10.3 EC)
Option C	payment reduction of 10% of the value certified in the payment certificate (excluding VAT)
Option D	cash deposit of 5% of the contract sum (excluding. VAT) and a payment reduction of 5% of the value certified in the payment certificate (excluding. VAT)
Option E	fixed construction guarantee of 5% of the contract sum (excluding VAT) and a payment reduction of 5% of the value certified in the payment certificate (excluding VAT) (DPW-10.1 EC)]

NB: Insurances submitted must be issued by either an insurance company duly registered in terms of the Insurance Act [Long-Term Insurance Act, 1998 (Act 52 of 1998) or Short-Term Insurance Act, 1998 (Act 53 of 1998)] or by a bank duly registered in terms of the Banks Act, 1990 (Act 94 of 1990) on the pro-forma referred to above. No alterations or amendments of the wording of the pro-forma will be accepted.

Guarantee for payment by employer [11.5.1; 11.10]	Not applicable
Advance payment, subject to a guarantee for advance payment [11.2.2; 11.3]	Not applicable

Tender / Quotation no: H25/008 AI

C 2.0 Payment of preliminaries [25.0]

Contractor's selection

Select Option A or B

☐

Where the **contractor** does not select an option, Option A shall apply

Payment methods

Option A	The preliminaries shall be paid in accordance with an amount prorated to the value of the works executed in the same ratio as the amount of the preliminaries to the contract sum , which contract sum shall exclude the amount of preliminaries . Contingency sum(s) and any provision for cost fluctuations shall be excluded for the calculation of the aforesaid ratio
Option B	The preliminaries shall be paid in accordance with an amount agreed by the principal agent and the contractor in terms of the priced document to identify an initial establishment charge, a time-related charge and a final dis-establishment charge. Payment of the time-related charge shall be assessed by the principal agent and adjusted from time to time as may be necessary to take into account the rate of progress of the works

Lump sum contract

Where the amount of **preliminaries** is not provided it shall be taken as 7.5% (seven and a half per cent) of the **contract sum**, excluding contingency sum(s) and any provision for cost fluctuations.

C 3.0 Adjustment of preliminaries [26.9.4]

Lump sum contract

Where the amount of **preliminaries** is not provided it shall be taken as 7.5% (seven and a half per cent) of the **contract sum**, excluding contingency sum(s) and any provision for cost fluctuations.

Contractor's selection

Select Option A or B

☐

Where the **contractor** does not select an option, Option A shall apply.

Provision of particulars

The **contractor** shall provide the particulars for the purpose of the adjustment of **preliminaries** in terms of his selection. Where completion in **sections** is required, the **contractor** shall provide an apportionment of **preliminaries** per **section**.

Option A	An allocation of the preliminaries amounts into Fixed, Value-related and Time-related amounts as defined for adjustment method Option A below, within fifteen (15) working days of the date of acceptance of the tender
Option B	A detailed breakdown of the preliminaries amounts within fifteen (15) working days of possession of the site . Such breakdown shall include, inter alia, the administrative and supervisory staff, the use of construction equipment , establishment and dis-establishment charges, insurances and guarantees, all in terms of the programme

Tender / Quotation no: H25/008 AI

Adjustment methods

The amount of **preliminaries** shall be adjusted to take account of the effect which changes in time and/or value have on **preliminaries**. Such adjustment shall be based on the particulars provided by the **contractor** for this purpose in terms of Options A or B, shall preclude any further adjustment of the amount of **preliminaries** and shall apply notwithstanding the actual employment of resources by the **contractor** in the execution of the **works**.

Option A	The preliminaries shall be adjusted in accordance with the allocation of preliminaries amounts provided by the contractor, apportioned to sections where completion in sections is required Fixed - An amount which shall not be varied. Value-related - An amount varied in proportion to the contract value as compared to the contract sum. Both the contract sum and the contract value shall exclude the amount of preliminaries, contingency sum(s) and any provision for cost fluctuations. Time-related - An amount varied in proportion to the number of calendar days extension to the date of practical completion to which the contractor is entitled with an adjustment of the contract value [23.2; 23.3] as compared to the number of calendar days in the initial construction period [26.9.4].
Option B	The adjustment of preliminaries shall be based on the number of calendar days extension to the date of practical completion to which the contractor is entitled with an adjustment of the contract value [23.2; 23.3] as compared to the number of calendar days in the initial construction period [26.9.4]. The adjustment shall take into account the resources as set out in the detailed breakdown of the preliminaries for the period of construction during which the delay occurred.

Failure to provide particulars within the period stated

Option A	Where the allocation of preliminaries amounts for Option A is not provided, the following allocation of preliminaries amounts shall apply: Fixed - Ten per cent (10%) Value-related - Fifteen per cent (15%) Time-related - Seventy-five per cent (75%) Where the apportionment of the preliminaries per section is not provided, the categorised amounts shall be prorated to the cost of each section within the contract sum as determined by the principal agent
Option B	Where the detailed breakdown of preliminaries amounts for Option B is not provided, Option A shall apply

DPW-10.2 (EC): VARIABLE CONSTRUCTION GUARANTEE GCC 3rd Edition (2015)

Director-General
Department of Public Works and Infrastructure
Government of the Republic of South Africa

FOR ATTENTION

To: Department of Public Works and Infrastructure
Private Bag X 65
PRETORIA
0001

Sir,

VARIABLE CONSTRUCTION GUARANTEE FOR THE EXECUTION OF A CONTRACT IN TERMS OF GCC 3rd Edition (2015)

1. With reference to the contract between _____
_____ (hereinafter referred to as the “**contractor**”) and the Government of the Republic of South Africa in its Department of Public Works and Infrastructure (hereinafter referred to as the “**employer**”), Contract/Tender No: **H25/008 AI**, for the **ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)** (hereinafter referred to as the “**contract**”) for the sum of
R _____, (*In words*) _____

_____, (hereinafter referred to as the “**contract sum**”).

I / We, _____
in my/our capacity as _____ and hereby
representing _____ (hereinafter referred to as the “**guarantor**”) advise that the **guarantor** holds at the **employer**’s disposal the sum of
R _____, (*In words*) _____

_____ being 10% of the **contract sum** (excluding VAT), for the due fulfilment of the **contract**.

2. I / We advise that the **guarantor**’s liability in terms of this guarantee shall be as follows:

- (a) From and including the date on which this guarantee is issued and up to and including the day before the date on which the last **certificate of completion** of works is issued, the **guarantor** will

Tender no: H25/008 AI

GCC (2015) 3rd Edition 2015

be liable in terms of this guarantee to the maximum amount of 10% of the **contract sum** (excluding VAT);

(b) The **guarantor's** liability shall reduce to 5 % of the **value of the works** (excluding VAT) as determined at the date of the last **certificate of completion** of works, subject to such amount not exceeding 10% of the **contract sum** (excluding VAT);

(c) This guarantee shall expire on the date of the last **final approval certificate**.

3. The **guarantor** hereby renounces the benefits of the exceptions *non numeratae pecunia; non causa debiti; excussionis et divisionis*; and *de duobus vel pluribus reis debendi* which could be pleaded against the enforcement of this guarantee, with the meaning and effect whereof I/we declare myself/ourselves to be conversant, and undertake to pay the **employer** the amount guaranteed on receipt of a written demand from the **employer** to do so, stating that (in the **employer's** opinion and sole discretion):

(a) the **contractor** has failed or neglected to comply with the terms and/or conditions of the **contract**; or

(b) the **contractor's** estate is sequestrated, liquidated or surrendered in terms of the insolvency laws in force within the Republic of South Africa.

4. Subject to the above, but without in any way detracting from the **employer's** rights to adopt any of the procedures provided for in the **contract**, the said demand can be made by the **employer** at any stage prior to the expiry of this guarantee.

5. The amount paid by the **guarantor** in terms of this guarantee may be retained by the **employer** on condition that upon issue of the last **final approval certificate**, the **employer** shall account to the **guarantor** showing how this amount has been expended and refund any balance due to the **guarantor**.

6. The **employer** shall have the absolute right to arrange his affairs with the **contractor** in any manner which the **employer** deems fit and the **guarantor** shall not have the right to claim his release on account of any conduct alleged to be prejudicial to the **guarantor**. Without derogating from the foregoing, any compromise, extension of the construction period, indulgence, release or variation of the **contractor's** obligation shall not affect the validity of this guarantee.

7. The **guarantor** reserves the right to withdraw from this guarantee at any time by depositing the guaranteed amount with the **employer**, whereupon the **guarantor's** liability ceases.

8. This guarantee is neither negotiable nor transferable, and

(a) must be surrendered to the **guarantor** at the time when the **employer** accounts to the **guarantor** in terms of clause 5 above, or

(b) shall lapse in accordance with clause 2 (c) above.

9. This guarantee shall not be interpreted as extending the **guarantor's** liability to anything more than payment of the amount guaranteed.

SIGNED AT _____ ON THIS _____ DAY OF _____ 20____

AS WITNESS

1. _____

2. _____

Tender no: H25/008 AI

DPW-10.2 (EC): Variable Construction Guarantee - GCC

GCC (2015) 3rd Edition 2015

By and on behalf of:

(insert the name and physical address of the guarantor)

NAME: _____

CAPACITY: _____
(duly authorised thereto by resolution attached marked
Annexure A)

DATE: _____

- A. No alterations and/or additions of the wording of this form will be accepted.
- B. The physical address of the guarantor must be clearly indicated and will be regarded as the guarantor's *domicilium citandi et executandi*, for all purposes arising from this guarantee.
- C. This GUARANTEE must be returned to: _____

DPW-10.4 (EC): FIXED CONSTRUCTION GUARANTEE GCC 3rd Edition (2015)

Director-General
Department of Public Works and Infrastructure
Government of the Republic of South Africa

FOR ATTENTION

To: Department of Public Works and Infrastructure
Private Bag X 65
Pretoria
0001

Sir,

FIXED CONSTRUCTION GUARANTEE FOR THE EXECUTION OF A CONTRACT IN TERMS OF GCC 3rd Edition (2015)

- With reference to the contract between _____
_____ (hereinafter referred to as the “**contractor**”) and the Government of the Republic of South Africa in its Department of Public Works and Infrastructure (hereinafter referred to as the “**employer**”), Contract/Tender No: **H25/008 AI**, for the **ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)** (hereinafter referred to as the “**contract**”), for the sum of R _____, (*In words*) _____,
_____, (hereinafter referred to as the “**contract sum**”).

I / We, _____
in my/our capacity as _____ and hereby
representing _____ (hereinafter referred to as the “**guarantor**”) advise that the **guarantor** holds at the **employer**’s disposal the sum of R _____,
_____, (*In words*) _____,
_____,
being 5% of the **contract sum** (excluding VAT), for the due fulfillment of the **contract**.
- The **guarantor** hereby renounces the benefits of the exceptions *non numeratae pecunia; non causa debiti; excussionis et divisionis*; and *de duobus vel pluribus reis debendi* which could be pleaded against the enforcement of this guarantee, with the meaning and effect whereof I/we declare myself/ourselves

Contract/Tender No: **H25/008 AI**

to be conversant, and undertake to pay the **employer** the amount guaranteed on receipt of a written demand from the **employer** to do so, stating that (in the **employer's** opinion and sole discretion):

- (a) the **contractor** has failed or neglected to comply with the terms and/or conditions of the **contract**;
or
 - (b) the **contractor's** estate is sequestrated; liquidated or surrendered in terms of the insolvency laws in force within the Republic of South Africa.
3. Subject to the above, but without in any way detracting from the **employer's** rights to adopt any of the procedures provided for in the **contract**, the said demand can be made by the **employer** at any stage prior to the expiry of this guarantee.
4. The amount paid by the **guarantor** in terms of this guarantee may be retained by the **employer** on condition that upon the issue of the last **final approval certificate**, the **employer** shall account to the **guarantor** showing how this amount has been expended and refund any balance due to the **guarantor**.
5. The **employer** shall have the absolute right to arrange his affairs with the **contractor** in any manner which the **employer** deems fit and the **guarantor** shall not have the right to claim his release on account of any conduct alleged to be prejudicial to the **guarantor**. Without derogating from the foregoing, any compromise, extension of the construction period, indulgence, release or variation of the **contractor's** obligation shall not affect the validity of this guarantee.
6. The **guarantor** reserves the right to withdraw from this guarantee at any time by depositing the guaranteed amount with the **employer**, whereupon the **guarantor's** liability ceases.
7. This guarantee is neither negotiable nor transferable, and
- (a) must be surrendered to the **guarantor** at the time when the **employer** accounts to the **guarantor** in terms of clause 4 above, or
 - (b) shall lapse on the date of the last **certificate of completion** of works.
8. This guarantee shall not be interpreted as extending the **guarantor's** liability to anything more than the payment of the amount guaranteed.

SIGNED AT _____ ON THIS _____ DAY OF _____ 20____.

AS WITNESS

1. _____

2. _____

Contract/Tender No: **H25/008 AI**

By and on behalf of:

(insert the name and physical address of the guarantor)

NAME: _____

CAPACITY: _____
(duly authorised thereto by resolution attached marked Annexure A)

DATE: _____

- A.** No alterations and/or additions of the wording of this form will be accepted.
- B.** The physical address of the guarantor must be clearly indicated and will be regarded as the guarantor's *domicilium citandi et executandi*, for all purposes arising from this guarantee.
- C.** This GUARANTEE must be returned to: _____

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

PART C2 PRICING DATA

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

C2.1 PRICING INSTRUCTIONS

PG-02.1 (EC) PRICING ASSUMPTIONS – GCC 3rd Edition (2015)

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender / Quotation no:	H25/008 AI	Reference no:	WCS 056397

C2.1 Pricing Assumptions

C2.1.1 GENERAL

The Bill of Quantities forms part of the Contract Documents and must be read and priced in conjunction with all the other documents comprising the Contract Documents, which include the Conditions of Tender, Conditions of Contract, the Specifications (including the Project Specification) and the Drawings.

C2.1.2 DESCRIPTION OF ITEMS IN THE SCHEDULE

The Bill of Quantities has been drawn up generally in accordance with Civil Engineering Quantities 1990 issued by the SA Institution of Civil Engineers.

The short descriptions of the items in the Bill of Quantities are for identification purposes only and the measurement and payment clause of the Standardized Specifications and the Particular Specifications, read together with the relevant clauses of the Project Specification and directives on the drawings, set out what ancillary or associated work and activities are included in the rates for the operations specified.

C2.1.3 QUANTITIES REFLECTED IN THE SCHEDULE

The quantities given in the Bill of Quantities are estimates only, and subject to remeasuring during the execution of the work. The Contractor shall obtain the Engineer's detailed instructions for all work before ordering any materials or executing work or making arrangements for it.

The Works as finally completed in accordance with the Contract shall be measured and paid for as specified in the Bill of Quantities and in accordance with the General and Special Conditions of Contract, the Specifications and Project Specifications and the Drawings. Unless otherwise stated, items are measured net in accordance with the Drawings, and no allowance has been made for waste.

The validity of the contract will in no way be affected by differences between the quantities in the Bill of Quantities and the quantities finally certified for payment.

C2.1.4 PROVISIONAL SUMS

Where Provisional sums or Prime Cost sums are provided for items in the Bill of Quantities, payment for the work done under such items will be made in accordance with Clause 45 of the General Conditions of Contract 2004. The Employer reserves the right, during the execution of the works, to adjust the stated amounts upwards or downwards according to the work actually done under the item, or the item may be omitted altogether, without affecting the validity of the Contract.

The Tenderer shall not under any circumstances whatsoever delete or amend any of the sums inserted in the "Amount" column of the Bill of Quantities and in the Summary of the Bill of Quantities unless ordered or authorized in writing by the Employer before closure of tenders. Unauthorized changes made by the Tenderer to provisional items in the Bill of Quantities, or to the provisional percentages and sums in the Summary of the Bill of Quantities will lead to the disqualification of the Tenderer.

C2.1.5 PRICING OF THE BILL OF QUANTITIES

The **bills of quantities / lump sum document** forms part of and must be read and priced in conjunction with all the other documents forming part of the **contract documents**, the Standard Conditions of Tender, Conditions of Contract, Specifications, Drawings and all other relevant documentation.

The prices and rates to be inserted by the Tenderer in the Bill of Quantities shall be the full inclusive prices to be paid by the Employer for the work described under the several items, and shall include full compensation for all cost and expenses that may be required in and for the completion and maintenance during the defects liability period of all the work described and as shown on the drawings as well as all overheads, profits, incidentals and the cost of all general risks, liabilities and obligations set forth or implied in the documents on which the Tender is based.

Each item shall be priced and extended to the "Total" column by the Tenderer, with the exception of the items for which only rates are required, or items which already have Prime Cost or Provisional Sums affixed thereto. If the Contractor omits to price any items in the Bill of Quantities, then these items will be considered to have a nil rate or price.

The Tenderer is required to check the Bills of Quantities and the numbers of the pages and should any be found to be missing or in duplicate, or should any of the typing be indistinct, or any doubt of obscurity arise as to the meaning of any description or particulars of any item, or if this Tender Enquiry contains any obvious errors, then the Tenderer must immediately inform the Principal Agent and have them rectified or explained in writing as the case may be. No liability whatsoever will be admitted by reason of the Contractor having failed to comply with the foregoing instruction.

No alterations, erasures, omissions or additions is to be made in the text and/or conditions of these Bills of Quantities. Should any such alterations, amendments, note/s or addition be made, the same will not be recognized, but reading of these Bills of Quantities as originally prepared by the Quantity Surveyor will be adhered to.

The contractor is cautioned that the use of any quantities appearing in these Bills of Quantities for the purpose of ordering material, it is done at own risk and no liability whatsoever will be admitted by the Employer or Quantity Surveyor for the correctness of such Quantities. Unless otherwise stated, items are measured net in accordance with the drawings, and no allowance is made for waste.

The prices and rates to be inserted by the Tenderer in the Bills of Quantities shall be the full inclusive prices to be paid by the Employer for the work described. Such prices and rates shall cover all costs and expenses that may be required in and for the execution of the work described, and shall cover the cost of all general risks, liabilities, and obligations set forth or implied in the documents on which the tender is based, as well as overhead charges and profit. Market related prices shall be inserted as these will be used as a basis for assessment of payment for additional work that may have to be carried out. The Employer reserves the right to balance the Bill rates where deemed necessary within the Tendered Amount.

A price or rate is to be entered against each item in the Bills of Quantities, whether the quantities are stated or not. An item against which no rate is/are entered, or if anything other than a rate or a nil rate (for example, a zero, a dash or the word "included" or abbreviations thereof) is entered against an item, it will also be regarded as a nil rate having been entered against that item, i.e. that there is no charge for that item. The Tenderer may be requested to clarify nil rates, or items regarded as having nil rates; and the Employer may also perform a risk analysis with regard to the reasonableness of such rates.

Should the full intent and meaning of any description not be clear, the bidder shall, before submission of his tender, call for a written directive from the principal agent, failing which it shall be assumed that the contractor has allowed in his pricing for materials and workmanship in terms of National Best Practice.

All items for which terminology such as "inclusive" or "not applicable" have been added by the Tenderer will be regarded as having a nil rate which shall be valid irrespective of any change in quantities during the execution of the Contract.

The Tenderer shall fill in rates for all items where the words "rate only" appear in the "Total" column. "Rate Only" items have been included where:

- (a) variations of specified components in the make-up of a pay item may be expected; and
- (b) no work under the item is foreseen at tender stage but the possibility that such work may be required is not excluded.

For 'Rate Only' items no quantities are given in the "Quantity" column but the quoted rate shall apply in the event of work under this item being required. The Tenderer shall however note that in terms of the Tender Data the Tenderer may be asked to reconsider any such rates which the Employer may regard as unbalanced.

Descriptions in the Bills of Quantities are abbreviated and comply generally with those in the "PW 371" and the principles contained in the latest version of the SANS 1200 in South Africa. It is the intention that the abbreviated descriptions be fully described when read with the applicable measuring system and the relevant preambles and/or specifications. However, should the full intent and meaning of any description not be clear, the bidder shall, before submission of his tender, call for a written directive from the principal agent, failing which it shall be assumed that the contractor has allowed in his pricing for materials and workmanship in terms of National Best Practice.

The price quoted against each item of this Bills of Quantities shall cover the full inclusive cost of the complete work to which it refers, as described in the Conditions of Contract and Specifications and as shown on the Drawings and shall allow for labour, material, transporting, loading, storage, supervision, commissioning, wastage, as well as the builders profit and attendance.

The Tenderer must ensure that he fully completes all columns of the Bill of Quantities including the Final Summary. The fully priced bill of quantities must be submitted with the tender or The Final Summary and the Section Summary pages MUST be returned with the tender document as indicated the PA-03 Notice and Invitation to Tender / PA-04 Notice and Invitation for quotation.

The tenderers are to ensure that they have read and understood the project specifications included in C3: Scope of Work. All the information provided in the Scope of Works form part of the work and must be included in the rates.

"The Contractor shall be deemed to have inspected and examined the Site and its surroundings and information available in connection therewith and to have satisfied himself before submitting his tender (as far as is practicable) as to:

- (a) the form and nature of the Site and its surroundings, including subsurface conditions,
- (b) the hydrological and climatic conditions,
- (c) the extent and nature of work and materials necessary for the execution and completion of the Works,
- (d) the means of access to the Site and the accommodation he may require

and, in general, shall be deemed to have obtained all information (as far as is practicable) as to risks, contingencies and all other circumstances which may influence or affect his Tender"

C2.1.6 VALUE ADDED TAX

The **contract sum** must include for Value Added Tax (VAT). All rates, provisional sums, etc. in the **bills of quantities / lump sum document** shall be in Rands and cents and shall include all levies and taxes (other than VAT). VAT will be added in the summary of the Bill of Quantities. The rates must however be net (exclusive of VAT) with VAT calculated and added to the total value thereof in the Final Summary. All rates and amounts quoted in the Bill of Quantities

C2.1.7 CORRECTION OF ENTRIES

Incorrect entries shall not be erased or obliterated with correction fluid but must be crossed out neatly. The correct figures must be entered above or adjacent to the deleted entry, and the alteration must be initialled by the Tenderer.

C2.1.8 ARITHMETICAL ERRORS

Arithmetical errors found in the Bill of Quantities as a result of faulty multiplication or addition, will be corrected by the Engineer at the tender evaluation stage, as set out in the Tender Data.

C2.1.9 CONTRACT DOCUMENTS

The Tenderers are advised to examine the bills of quantities, drawings and specifications including all other contract documents and make themselves thoroughly acquainted with the nature and requirements of the work, as no claim for extra payment in this regard will be entertained. Should any parts of the drawings not be clearly intelligible to the Tender, he must, before submitting his tender, obtain clarification from the Principal Agent.

C2.1.10 UNITS OF MEASUREMENT

The units of measurement described in the Bill of Quantities are metric units for which the standard international abbreviations are used. Non-standard abbreviations which may appear in the Bill of Quantities are as follows:

No.	=	Number
%	=	Percent
Sum	=	Lump sum
PCsum	=	Prime cost sum
Prov sum	=	Provisional sum
m ³ .km	=	Cubic metre - kilometre
Km-pas	=	kilometre - pass
m ² .pass	=	square metre – pass

C2.1.11 TRADE NAMES

Tenderers attention is drawn to the fact that wherever trade names or references to any catalogue have been made in these Bills of Quantities, it is purely to establish a standard for the required material. If use is made of any other equally approved material in lieu of the prescribed trade name or catalogue, the necessary price adjustments will be made.

C2.1.12 CONTRACT DOCUMENTS

The Tenderers are advised to examine the bills of quantities, drawings and specifications including all other contract documents and make themselves thoroughly acquainted with the nature and requirements of the work, as no claim for extra payment in this regard will be entertained. Should any parts of the drawings not be clearly intelligible to the Tender, he must, before submitting his tender, obtain clarification from the Principal Agent.

C2.1.13 PAYMENTS

Interim valuations and payments will be prepared on a monthly basis, all in terms of the conditions of contract.

The contractor is to note that no payment will be made for materials stored off site and in the case of materials being stored on site, payment will only be made for such materials on condition that they have not been delivered to the site prematurely, a tax invoice and proof of payment (ownership) is submitted by the Contractor.

C2.1.14 ACCOMMODATION ON SITE

It is imperative to note that no living quarters for construction workers on site will not be permitted for the full duration of the contract unless otherwise stated in the contract data or permission be granted by the Employer.

C2.1.15 LOCAL MATERIAL UTILISATION REPORT (LOCAL CONTENT)

Submission of Local Material Utilisation Reports is *applicable* to this project.

Bidders to note that materials procured for the works should be from South African manufactures and suppliers. Imported materials shall only be considered under exceptional circumstances, based on compelling technical justifications, and subject to the approval by the NDPWI.

The contractor shall be responsible for record keeping, documenting and submission of monthly local material utilization report with supporting documentation to the Employer's representative within 7 working days of the beginning of the successive month, indicating the percentage targets achieved in terms of DTI&C designated industry/sector/sub-sector schedule as per the PA36 and Annexures C attached to the tender document. The final percentage achievement to be reconciled upon completion of the project and form part of the final account. Allowance must be made for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

C2.1.16 CONTRACT PARTICIPATION GOALS

The contractor shall achieve in the performance of this contract the following Contract Participation Goals (CPGs) as indicated below:

Provision for pricing of compliance with the achieving the CPGs is made in the Contract Participation Goal Section of the Bills of Quantities and it is explicitly pointed out that all requirements in respect of the aforementioned are deemed to be priced thereunder and no additional claims in this regard shall be entertained

Monthly progressive reports to be submitted to the Employer's representative indicating the percentage targets achieved which must be reconciled upon completion of the project and to form part of the final account.

C2.1.16.1 MINIMUM TARGETED LOCAL BUILDING MATERIAL MANUFACTURERS CONTRACT PARTICIPATION GOAL

The Minimum Targeted Local Building Material Manufacturers CPG is *applicable* to this project.

Provision is made within the Contract Participation Goal section in the Bill of Quantities for the Minimum Targeted Local Building Material Manufacturers CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.1. Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

C2.1.16.2 MINIMUM TARGETED LOCAL BUILDING MATERIAL SUPPLIERS CONTRACT PARTICIPATION GOAL

The Minimum Targeted Local Building Material Suppliers CPG is *applicable* to this project.

Provision is made within the Contract Participation Goal section in the Bill of Quantities for the Minimum Targeted Local Building Material Suppliers CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.2. Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

C2.1.16.3 MINIMUM TARGETED LOCAL LABOUR CONTRACT PARTICIPATION GOAL

The Minimum Targeted Local Labour Skills Development CPG is *applicable* to this project.

Provision is made within the Contract Participation Goal section in the Bill of Quantities for the Minimum Targeted Local Labour CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.3. The Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

C2.1.16.4 MINIMUM TARGETED ENTERPRISE DEVELOPMENT: CONTRACT PARTICIPATION GOALS (CPG)

The Minimum Targeted Enterprise Development Contract Participation Goal is *applicable* to this project.

A provisional amount has been allowed for within the Contract Participation Goal section in the Bill of Quantities for the Minimum Targeted Enterprise Development CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.4. The provisional amount allowed is for the appointment of training coordinator, mentor, training service providers and training of the beneficiary enterprises. The provisional amount will be adjusted in accordance with the actual Contract Amount (Awarded tender amount excluding allowance, provisional amounts and VAT) of the awarded bid.

Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

The contractor shall complete a separate bill of quantities upon the award of the project and identification of the respective beneficiaries and the appointment of the training coordinator, mentor, training service providers of which the cost will be offset against the provisional amount allowed in the Bills of Quantities.

C2.1.16.5 MINIMUM TARGETED TARGETED CONTRACT SKILLS DEVELOPMENT GOALS (CSDG)

The Minimum Targeted Contract Skills Development CPG is *applicable* to this project.

A provisional amount has been allowed for within the Contract Participation Goal section in the Bill of Quantities for the Minimum Targeted Skills Development CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.5. The provisional amount allowed is for:

- stipends payable to the beneficiaries
- appointment of training coordinator
- appointment of mentor (where applicable)
- appointment of training service providers
- other additional costs as per Table 3 of the Standard

The provisional amount will be adjusted in accordance with the actual Contract Amount (Awarded tender amount excluding allowance, provisional amounts and VAT) of the awarded bid.

Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative

on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

The contractor shall complete a separate bill of quantities upon the award of the project and identification of the respective beneficiaries. The CPG value to be achieved will be based on the actual contract amount which will be offset against the provisional amount allowed for within the Contract Participation Goal section in the Bill of Quantities.

Payment

The contractor shall upon the appointment of beneficiaries, provide a breakdown of all the associated costs. The contractor shall provide a payment schedule as to how the CPG costs will be claimed against for inclusion in the monthly payment certificates.

(a) Payment to the contractor to accommodate Part/Full Occupational qualification and Trade qualifications;

Should the contractor select Part/Full Occupational qualification and Trade qualifications learners, then the employer shall make provision for payment to the contractor as indicated in Table 3 of the Standard.

The contract skills participation goal, expressed in Rand, shall not be less than the contract amount multiplied by a percentage (%) factor given in Table 2 in the Standard for the applicable class of construction works. Should the contractor select Part/Full Occupational qualification and Trade qualifications learners, then the employer shall make provision for payment to the contractor as indicated in Table 3 of the Standard.

Table 1: Contracting skills development goals for different classes of engineering and construction works contracts

Source: cidb Standard for Developing Skills through Infrastructure Contracts as published in the Government Gazette Notice No 48491 Government Gazette, 23 April 2023 (Table 2, Page 7)

Class of construction works as identified in terms of Regulation 25 (3) of the Construction Industry Regulations 2004		Construction skills development goal (CSDG) (%)
Designation	Description	
CE	Civil Engineering	0.25
CE and GB	Civil engineering and General Building	0.375
EE	Electrical Engineering works (buildings)	0.25
EP	Electrical Engineering works (infrastructure)	0.25
GB	General Building	0.5
ME	Mechanical Engineering works	0.25
SB	Specialist	0.25

No provision for an additional payment item for the payment of the supervisor and/or mentors for the provision of training as provided for in the Contract Participation Goal section in the Bill of Quantities for the training of part/full time occupational learners and/or trade qualification learners. The associated cost is deemed to be included in general supervision on site.

The contractor shall complete a separate bill of quantities upon award, indicating the type and number of beneficiaries as well as the associated Notional Cost of Training to be provided, on which payment will be based.

(b) Payment to the contractor to accommodate Work Integrated Learners and Candidates for professional registration;

Provisional amounts have been included in the Contract Participation Goal section in the Bill of Quantities for the training of Work Integrated Learners and Candidates for professional registration. The contractor shall price his Profit and Attendance (all inclusive of associated costs to the contractor for implementation and reporting), based on the provisional amount in the Contract Participation Goal section in the Bill of Quantities.

The CPG value to be achieved will be based on the contract amount as defined by the Standard, which will be offset against the provisional amount allowed for within the Contract Participation Goal section in the Bill of Quantities.

The contractor shall apportion the cost of accommodating work integrated learners (P1 and P2 learners) and candidates for professional registration by using Table 3 in the Standard and this cost will be used to determine the Rand value and will be used in determining the contract participation goal in the Bills of Quantities.

Source: cidb Standard for Developing Skills through Infrastructure Contracts as published in the Government Gazette Notice No. 48491 Government Gazette, 23 April 2023 (table 3, Page 9)

Type of Training Opportunity	Provision for stipends (Unemployed learners only)	Provisions for mentorship	Provisions for additional costs*	Total costs	
				Unemployed learners	Employed learners
Method 1					
Occupational qualification	R7 000	R0	R9 000	R16 000	R9 000
Method 2					
TVET College graduates	R14 000	R0	R9 000	R23 000	N/A
Apprenticeship	R14 000	R0	R12 000	R26 000	R12 000
Method 3					
P1 and P2 learners	R24 000	R20 000	R4 500	R48 500	N/A
Method 4					
Candidates with a 3 year diploma	R37 000	R20 000	R4 500	R61 500	R20 000
Candidates with 4 year qualification	R47 000	R20 000	R4 500	R71 500	R20 000

Note: The notional cost of providing training opportunities will increase by CPI on an annual basis based on April CPI. Should the rates increase after bid award or during construction the rates will be adjusted as a provisional item.

Example: Training Target Calculation for a R65,7m GB contract

Contract amount	R65 700 000
Contract duration	12 Months
CSDG	0,50%
Minimum CSDG target	0,50% x R65 700 000 = R328 500 (Minimum requirement)

Skills Types	Number of learners	Notional Cost / Learner / Quarter	Notional cost/learner/year	Total Notional Cost over 12 months Contract
Method 2: Workplace learning opportunities, with unemployed TVET graduates	1	R23 000	R92 000	R92 000
Method 3: Candidacy for an unemployed learner with a 3-year qualification	1	R61 500	R246 000	R246 000
Total	2			R338 000

C2.1.16.6 NATIONAL YOUTH SERVICE TRAINING AND DEVELOPMENT PROGRAMME

The National Youth Service Training and Development Programme is *not applicable* to this project.

The programme shall be implemented in terms of the Implementation of the National Youth Service Programme under the Expanded Public Works (EPWP) and shall be priced in the CPG section of the Bills of Quantities.

Provision has been made within the Contract Participation Goal section in the Bill of Quantities for the National Youth Service Training and Development Programme CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.6.

Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

C2.1.16.7 LABOUR-INTENSIVE WORKS

Labour Intensive Works is *applicable* to this project.

Where labour intensive work is specified in the Bill of Qualities and indicated by "LI" the contractor must price for and include in rates. Contractors are expected to use their initiative to identify additional activities that can be done labour-intensively to comply with the set minimum labour intensity target. Provision has been made within the Contract Participation Goal section in the Bill of Quantities for the monthly reporting illustrating the value of the works executed under Labour Intensive Works CPG in the execution of this project as described in PG-01.1 (EC) SCOPE OF WORKS C3.7.7 and any other supplementary specifications.

Prescribed Profit and Attendance percentages have been stipulated, all inclusive of associated costs to the contractor for implementation and allowance for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

C2.2 Submission of Accrual Reports

The Contractor shall submit accrual reports to the client representative at the end of March and September each year for the duration of the Service Contract period from the date of appointment up to and including project closeout. This is to ensure that PMTE complies with the accounting framework GRAP, which requires that PMTE disclose all its accruals as at the end of each reporting date. Allowance must be made for submitting reports to the Employer's Representative on a monthly basis in terms of monthly and accumulative targets achieved with audited supporting documentation.

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

C2.2 BILL OF QUANTITIES

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS
REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND
INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

CALCULATION OF TENDER SUMMARY

	TENDER AMOUNT
TOTAL: CIVIL REPAIR WORK	
TOTAL: ELECTRICAL REPAIR WORK	
TOTAL: MECHANICAL REPAIR WORK	
TOTAL: CIVIL MAINTENANCE WORK	
TOTAL:ELECTRICAL MAINTENANCE WORK	
TOTAL: MECHANICAL MAINTENANCE WORK	

TOTAL OF SCHEDULE OF QUANTITIES

15 % VALUE-ADDED TAX (VAT)

TENDER SUM CARRIED TO THE TENDER FORM

SIGNED ON BEHALF OF TENDERER:

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SUMMARY OF BILL OF QUANTITIES: CIVIL REPAIR WORK

CIVIL REPAIR WORK

SCHEDULE NO 1: PRELIMINARY AND GENERAL	
SCHEDULE NO 2: INSTALLATION C1: STRUCTURAL AND BUILDING	
SCHEDULE NO 3: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES	
SCHEDULE NO 4: INSTALLATION C3: FENCING, CLEANING, SITE KEEPING AND PEST CONTROL	
SCHEDULE NO 5: INSTALLATION C4: BULK WATER SUPPLY SYSTEM AND EXTERNAL	
SCHEDULE NO 6: INSTALLATION C5: WASTEWATER TREATMENT WORKS AND SEWER NETWORKS	
SCHEDULE NO 7: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE	

TOTAL OF BILL OF QUANTITIES - CIVIL REPAIR WORK
CARRIED TO CALCULATION OF TENDER SUM

.....

SIGNED ON BEHALF OF TENDERER:

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QAUNTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	100.00	GENERAL				
	100.01	Scheduled fixed-charge and value related items				
		0.01 Fixed preliminary and general charges for all four (04) Border Posts	Sum	1.00		
	100.02	Scheduled time related items				
		0.01 Alexander Bay LPoE	Month	36.00		
		0.02 Vioolsdrift LPoE	Month	36.00		
		0.03 Onseepkans LPoE	Month	36.00		
	101.00	TEMPORARY WORKS				
	101.01	Location and Protection of existing				
		0.01 Water and sewer pipes	Sum	1.00		
		0.02 Electrical and other cables	Sum	1.00		
	101.02	Hand execution necessary for locating and exposing existing services in all material:				
		0.01 in roadways	m ³	45.00		
		0.02 in all other areas	m ³	25.00		
	101.03	Additional tests				
		0.01 Additional tests required by the Engineer	PC sum	1.00	R50,000.00	R 50,000.00
		0.02 Attendance and profit	%	R 50,000.00		
	Carried forward					

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	101.04	Call Centre:				
		0.01 Call centre for breakdown calls logged	PC sum	1.00	R 360,000.00	R 360,000.00
		0.02 Charge required by Contrator on subitem 0.1 above	%	R 360,000.00		
		Updating of existing Ports of Entry Key Plans				
	101.05	.01 Supply a complete Updated site plan for Alexander Bay LPoE	Sum	1.00		
	101.06	.02 Supply a complete Updated site plan for Vioolsdrift LPoE	Sum	1.00		
	101.07	.03 Supply a complete Updated site plan for Onseepkans LPoE	Sum	1.00		
		Maintenance Control Plan				
		Compile complete maintenance control plan as specified in SA 04.20 including monthly maintenance control sheets and recordings				
		.01 Alexander Bay Port of Entry	Site	1.00		
		.02 Vioolsdrift Drift Port of Entry	Site	1.00		
		.03 Onseepkans Port of Entry	Site	1.00		
		Site Maintenece Record Keeping (monthly maintenance report for all schedules checklists, reports, etc as detailed specification SA 03.10 maintenance control plan)				
		.01 Alexander LPoE	month	1.00		
		.02 Vioolsdrift LPoE	month	1.00		
		.03 Onseepkans LPoE	month	1.00		
	102.00	PRIME COST SUMS				
		0.01 Housing for the Engineer's representative	PC Sum	1.00	R260,000.00	R 260,000.00
		0.02 Charge required by Contractor on subitem 0.1 above	%	R 260,000.00		
		.03 Survey assistants and materials	PC Sum	1.00	R 396,000.00	R 396,000.00
		.04 Charge required by Contractor on sub item	%	R 396,000.00		
	Carried forward					

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	102.00	OCCUPATIONAL HEALTH AND SAFETY				
		0.01 Preparation of Health and Safety file	Sum	1.00		
		0.02 Compliance with OHS Act and Construction Regulations 2014	Month	36.00		
	104.00	HIV/AIDS AWARENESS				
		It is required of the Contractor to thoroughly study the additional specification SH: HIV/AIDS Requirements (PW 1544) of the Department that must be read together with and is deemed to be incorporated under this Section of the Bills of Quantities. Provision for pricing of HIV/AIDS awareness is made under the items hereafter and it is explicitly pointed out that all requirements of the aforementioned specification are deemed to be priced hereunder, as the said items represent the only method of measurement and no additional items or extras to the contract in this regard. The Contractor must take note that compliance with the HIV/AIDS specification is compulsory. In the event of partial or total non-compliance, the Representative/agent, notwithstanding the provisions of Clause 52 of the General Conditions of Contract for Works of civil engineering Construction or any other clause to the contrary, reserves the right to delay issuing any progress payment certificate until the contractor provides satisfactory proof of compliance. the contractor shall not be entitled to any compensation of whatsoever nature, including interest due to such delay of				
		0.01 Awareness Champion	Sum	36.00	R 2,500.00	R 90,000.00
		Selection, appointment, briefing and making available of an awareness Champion including provision of all relevant services				
		0.02 Awareness Workshop	Sum	36.00		
		Selection and appointment of a competent service Provider Workshop Plan and suitable venue, conducting of awareness workshops by means of traditional and for modern multi-media techniques, including follow-up courses, making available all tuition material and performing assessment procedures				
	Carried forward					

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
SN	104.00	0.03 Posters, Booklets, Videos, etc. Provision, displaying, maintaining and replacing when necessary of four plastic laminated posters, booklets and educational videos, etc for the duration of the construction period.	Sum	36.00		
		0.04 access to Condoms Provision and maintenance of condom dispensers fixed in position, including male and female condoms, replenishing male and female condoms on daily basis as required for the duration of the construction period	Sum	36.00		
		0.05 Monitoring Monitoring HIV/AIDS awareness of workers, providing the Representative/Agent with access to information including making available all reports, thoroughly completed and reflecting the information, for the	Sum	36.00		
	105.00	BMA CONTINGENCY INFRASTRUCTURE				
		.01 Alexander Bay LPoE	PC Sum	1.00	R 95,000.00	R 95,000.00
		.02 Vioolsdrift LPoE	PC Sum	1.00	R 215,000.00	R 215,000.00
		.03 Onseepkans LPoE	PC Sum	1.00	R 45,000.00	R 45,000.00
		0.02 Charge required by Contractor on sub-item 0.01, 0.02 & 0.03 above	%	R 355,000.00		
		EPWP: LABOUR-INTENSIVE (LIC)				
	1.11	Training of EPWP Workers (Target: 10 EPWP Maintenance Workers) Orientation, Life Skills Development and Technincal Skills Training				
SN 10.01.01		.01 Orientation and Life Skills development training for EPWP workers for an average of 10 days per EPWP worker.	PC sum	1.00	R 30,000.00	R 30,000.00
SN 10.01.02		.02 Techical skills training for EPWP workers for an average of 20 days per EPWP worker.	PC sum	1.00	R 120,000.00	R 120,000.00
		.03 Profit and attendance for administration of items .01, and.02 above	%	R 150,000.00		
SN10.02.01		.04 Penalty due to not meeting the target as in SN 10.01.02	worker/day	-	-R 2,700.00	Rate Only
	Carried forward					R 505,000.00

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					R 505,000.00
SN10.01.03		.05 First Aid Level 1 training for EPWP workers for an average 5 of days per EPWP worker (ref. SN 10.01.03)	PC Sum	1	R 20,000.00	R 20,000.00
SN 10.03		EMPLOYEMENT OF EPWP WORKERS				
SN 10.03.01		Employment of EPWP workers				
		The unit of measuerement shall be the number of EPWP workers at the labour rate of comparable unskilled worker in the local area alternatively a minimum R 2425.60 per month as the amount indicated in the Ministerial Determinanation 4: EPWP, dated on 01 March 2025, Cluase 14.2: Minimum of R 126.64 per day multiplied by the period employed in months and the rate tendere shall include full compensation for all costs associated with the employment of EPWP workers and for complying with conditions of contract. The cost for the training shall be excluded from this item. This item is based on a 24 months appointment for EPWP workers.Plus 5% Annual Escalation (it Ministerial determination)				
		.01 Employment of EPWP workers: 10 workers x 24 months	PC sum	1.00	R 1,005,480.00	R 1,005,480.00
		.02 Profit and attendance for administration of items .01	%	R1,005,480.00		
SN 10.03		<u>PROVISION OF EPWP DESIGNED OVERALLS AND HARD HATS AND SAFETY BOOTS (PPE) TO EPWP WORKERS</u>				
SN 10.04.01		.01 Supply 2 x EPWP branded overalls to each EPWP worker	PC sum	1.00	R 12,000.00	R 12,000.00
SN 10.04.02		.02 Supply 1 x EPWP branded hard hat to EPWP worker	PC sum	1.00	R 1,000.00	R 1,000.00
SN 10.04.03		.03 Supply 1 x pair of safety boots to each EPWP worker	PC sum	1.00	R 10,000.00	R 10,000.00
SN 10.04.04		Profit and attendance for administartion of items 1,2 and 3 above.	%	R 23,000.00		
	Carried forward					

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
SN 10.02.01	1.12	EPWP: LABOUR-INTENSIVE (LIC) ,01 Traveling to Alexander Bay Port of Entry from the nearest local township (based on a 50 km return trip/EPWP worker) (5 workers x 2 years x 250 work days per Year	PC sum	1.00	R 100,000.00	R 100,000.00
SN 10.02.01	1.13	,02 Traveling to Onseepkans Port of Entry from the nearest local township (based on a 20 km return trip/EPWP worker) (2 workers x 2 years x 250 work days per Year	PC sum	1.00	R 75,000.00	R 75,000.00
SN 10.02.01	1.14	,03 Traveling to Vioolsift Port of Entry from the nearest local township (based on a 100km return trip/EPWP worker) (8 workers x 2 years x 250 work days per Year	PC sum	1.00	R 170,000.00	R 170,000.00
PG01,1 (EC)		.04 Charge required by Contractor on sub item.01,02 and 03 above	%	R 345,000.00		
		CONTRACT PARTICIPATION GOALS (CPG) - FOR THE CALCULATION OF THESE GOALS, REFER ALSO TO DOCUMENT IN PART C7: NDPWI CONTRACT PARTICIPATION GOALS AND CIDB BUILD PROGRAMME IMPLEMENTATION GUIDE				
	100.25	MINIMUM TARGETED LOCAL BUILDING MATERIAL SUPPLIERS				
	1	Provision is made for the Minimum Targeted Local Building Material Suppliers CPG in the execution of this project as described in PG-01.1 (EC) / PG-01.2 (EC) SCOPE OF WORKS C3.7.2. Material to the value of R 1 150,000.00 should be purchased from local suppliers as defined in the CPG specifications in terms of locality, based on determination by PQS taking into account specific project variables.	PC Sum			
	2	Allowance for monitoring and monthly reporting on material purchased from Local Building Material Suppliers by main contractor and subcontractors.	%	R1,150,000.00	5%	R 57,500.00
	3	Allowance for profit all inclusive of associated costs to the contractor for implementation.	%	R 115,000.00	10%	R 11,500.00
	4	Allowance for attendance all inclusive of associated costs to the contractor for implementation.	%	R 115,000.00	10%	R 11,500.00
	Carried forward					

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	100.26	MINIMUM TARGETED LOCAL LABOUR SKILLS DEVELOPMENT				
	1	Provision is made for the Minimum Targeted Local Labour Skills Development CPG in the execution of this project as described in PG-01.1 (EC) / PG-01.2 (EC) SCOPE OF WORKS C3.7.3.	PC Sum	1.00	R 300,000.00	R 300,000.00
	2	Allowance for monitoring and monthly reporting on training provided by main contractor and subcontractors.	%	R 300,000.00	5%	R 15,000.00
	3	Allowance for profit all inclusive of associated costs to the contractor for implementation.	%	R 300,000.00	5%	R 15,000.00
	4	Allowance for attendance all inclusive of associated costs to the contractor for implementation.	%	R 300,000.00	5%	R 15,000.00
		MINIMUM TARGETED ENTERPRISE DEVELOPMENT				
	1	Provision is made for 5 % compulsory subcontracting to SMMEs in the execution of this project as described in PG-01.1 (EC) / PG-01.2 (EC) SCOPE OF WORKS C3.7.4.	PC Sum	1.00	R192,000.00	R 192,000.00
	2	A provisional amount has been allowed for in the execution of this project as described in PG-01.1 (EC) / PG-01.2 (EC) SCOPE OF WORKS C3.7.5.	PC Sum	1.00	R2,004,000.00	R 2,004,000.00
	3	Allowance for monitoring and monthly reporting on SMME subcontracting by main contractor and subcontractors including training provided.	%	R2,196,000.00	5%	R 109,800.00
	4	Allowance for profit all inclusive of associated costs to the contractor for implementation.	%	R2,196,000.00	5%	R 109,800.00
	5	Allowance for attendance all inclusive of associated costs to the contractor for implementation.	%	R2,196,000.00	5%	R 109,800.00
	Carried forward					

SCHEDULE NO 1: PRELIMINARY AND GENERAL

SCHEDULE NO 1: PRELIMINARY AND GENERAL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		MINIMUM TARGETED SKILLS DEVELOPMENT GOALS				
	1	A provisional amount has been allowed for the Minimum Targeted Development CPG in the execution of this project as described in PG-01.1 (EC) / PG-01.2 (EC) SCOPE OF WORKS C3.7.5. • stipends payable to the beneficiaries • appointment of training coordinator • appointment of mentor (where applicable) • appointment of training service providers • other additional costs as per table 3 of the Standard	PC Sum	1.00	R532,500.00	R 532,500.00
	2	Allowance for monitoring and monthly reporting on skills development by main contractor and subcontractors.	%	R 532,500.00	5%	R 26,625.00
	3	Allowance for attendance all inclusive of associated costs to the contractor for implementation.	%	R 532,500.00	5%	R 26,625.00
100.24	4	Allowance for attendance all inclusive of associated costs to the contractor for implementation.	%	R 532,500.00	5%	R 26,625.00
		COMMUNITY LIASON OFFICER (CLO)				
		Provide the sum of R216 000,00 for the community liaison officer for the construction period of 18 months for each port of entry				
	1	Alexander Bay, Vioolsdrift and Onseepkans Ports of Entry	PC Sum	1.00	R 216,000.00	R 216,000.00
100.30	2	Profit and attendance for administration of items 0,01	%	R 216,000.00		
		Enterprise Development				
		Enterprise Development of Targeted Enterprise or JV partners				
	1	Appointment of training co-ordinator (As determined by the PQS)	Per Quarter	12.00		
	2	Appointment of Mentor /Training Service provider (As determined by the PQS)	Per Quarter	12.00		
	3	Needs Analysis and Enterprise Development Plan per Targeted Enterprise (As determined by the PQS)	Per Quarter	6.00		
	4	Monitoring and Interim reporting per targeted enterprise (As determined by the PQS)	Per Quarter	12.00		
	5	Project Completion report per Targeted Enterprise (As determined by the PQS)	No.	6.00		
TOTAL SCHEDULE NO 1: PRELIMINARY AND GENERAL - CARRIED TO SUMMARY						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	200.00	BA : ROOFS CARPENTRY AND JOINERY FOR ROOFS				
	200.01	Remove existing joinery items by length				
		.01 Roof timbers	m	20.00		
		.02 Fascias and barge boards	m	25.00		
	200.02	Supply and install new items measured by				
		.01 225 x 10 mm Thick pressed fibre cement fascia, including painting, etc.	m	20.00		
		.02 225 x 10 mm Thick pressed fibre cement barge board, including painting, etc.	m	25.00		
		.03 75 x 50 mm SAP purlins.	m	320.00		
		.04 38 x 114 mm Wrought sloping SAP rafters	m	150.00		
	200.03	CLADDING AND SHEETING				
	200.04	Replace, supply and install cladding and sheeting.				
		0,6mm Thick galvanised IBR or equivalent approved sheeting with CHROMADEK silicone polyester finish on one side and CHROMADEK finish on the other side in:				
		.01 Roof covering with pitches exceeding 15°, fixed to timber or steel purlins	m ²	600.00		
		.02 10 mm Thick corrugated fibre cement or equivalent approved sheeting	m ²	436.00		
		.03 Ridge Covering, 06 mm	m ²	20.00		
	200.05	Carefully remove existing cladding and sheeting				
		.10 Existing galvanised sheet metal roof covering removed from timber or steel purlins or girts	m ²	750.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	200.05	Supply and install sundry items, etc: 0,8mm Thick galvanised sheet iron flashings with CHROMADEK Silicone polyester finish to one side of sundry items to IBR or concealed fixing roof sheeting complete as detailed in BA 03.01				
		.01 Ridge flashing	m	100.00		
		.02 Side wall flashing	m	100.00		
	200.06	Supply and Install rainwater goods: 0.8 mm Thick galvanised sheeting with CHROMADEK silicone polyester finish to one side in:				
		.01 125 x 100 mm self-supporting box gutter	m	250.00		
		.0.2 125 x 100 mm Down pipe	m	52.00		
	200.07	Carefully remove existing rainwater goods				
		.01 Eaves gutters	m	326.00		
		.02 Down pipes	m	52.00		
	200.08	Rehabilitation:				
		.01 Rehabilitation of existing roof sheeting, seal joints and replace loose screws or re-fix sheets	m ²	1,600.00		
		.02 Supply and install additional fixing crew etc	No	1,100.00		
		.03 Prepare existing galvanised or previously painted roof sheeting and paint with a polyurethane coating system as per technical specification BA 03.02	m ²	2,000.00		
		.04 Replace missing or broken roof tiles similar to existing	No	50.00		
		.05 Re-align existing down pipes and gutters, including sealing joints	m	92.00		
	200.08	Supply and install roof insulation				
		.01 White Bubble Foil insulation 4mm thick fixed on white sealing wires:				
		.01 Roofs	m ²	128.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	200.09	Miscellaneous items:				
		0.01 Items measured by square metre:				
		.01 Pure acrylic emulsion waterproofing paint with polyester membrane or glass fibre tissue waterproofing sealing system.	m ²	20.00		
	200.10	Timber				
		.01 Wrought SA pine: Removal of existing and supply and install new for rehabilitation:				
		.01 38 mm x 38 mm Wrougght timber bandering	m	44.00		
		.02 76 mm x 52 mm Wroufgh timber bandering	m	32.00		
	201.00	BB CARPENTRY				
	201.01	Ceillings:				
		0.01 Gypsum board with metal H-profile jointing strips				
		.01 6,4 mm ceilings	m ²	200.00		
		0.02 Fibre cement with metal H-profile jointing strips:				
		.01 6mm ceilings	m ²	10.00		
		.02 Extra over 6,4 mm ceiling for trap door with framing	m ²	8.00		
	201.02	0.03 Gypsum cornices.				
		.01 76 mm gypsum coved cornices including silicone sealant in contact joint with plastered brickwork	m	90.00		
	202.00	ALTERATION WORK				
	202.01	Alterations and repairs to existing Structures:				
		0.01 Remove:				
		.01 Softboard, plaster board or fibre cement ceiling boards including cornices cover and jointing strips	m ²	100.00		
		.02 76 mm gypsum coved cornices	m	90.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	203.00	BD: WALLS				
	203.00	NEW WORK				
	203.01	EARTHWORKS (SMALL WORKS)				
		SCHEDULED ITEMS				
		.01 Excavate for restricted foundation, footings and trenches in all materials and for backfill or embankment or dispose.	m ³	10.00		
		.02 Break up, hack of and remove existing concrete	m ³	2.00		
		.03 Importing, placing and compacting approved G6 material from commercial sources or from borrow pits to 95% MOD AASTHO.	m ³	42.00		
	203.02	CONCRETE (STRUCTURAL)				
		SCHEDULED CONCRETE ITEMS				
		Strength Concrete:				
		.01 Class 20 Mpa Concrete	m ³	1.00		
		.02 Class 25 Mpa concrete to scheduled items including ramps	m ³	5.00		
	203.03	SCHEDULED REINFORCEMENT				
		High-tensile steel welded mesh and steel bars				
		.01 Ref No 193 mesh in Concrete	m ²	6.00		
		.02 Ref No 245 mesh in concrete	m ²	6.00		
		.03 Y12 high tensile steel bars	m	100.00		
	203.04	Sandblasting				
		Sandblasting tio steel surfaces exposing steel for paint surfaces preparation	m ²	50.00		
	203.05	0.03 Break out/hack up/demolish and remove				
		.01 Half brick walls	m ²	20.00		
		.02 One brick walls	m ²	240.00		
		,03 External plaster to walls	m ²	45.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.04 External cement plaster to walls	m ²	30.00		
		.05 6mm clear float laminated	m ²	10.00		
	203.06	0.05 Clean existing surfaces:				
		.01 tiles to walls and floors including cleaning and refilling of joints	m ²	1,000.00		
		.02 Face bricks with calcium build up and residue	m ²	800.00		
	203.06	0.06 Repair and seal:				
		.01 Crack in plastered wall	m	30.00		
		.02 Crack in face brick wall	m	30.00		
	203.06	BUILDING WORK				
		Doors and windows:				
		.01 Wooden doors:				
		.01 Solid hardwood core flush panel door, 40 mm thick x 813 mm wide x 2032 mm high. All doors shall comply with the requirements of SANA specifications 545 and bear the "MARK"	No	20.00		
		.02 Hollow core door, 40 mm thick x 813 mm wide x 2032 mm high. All doors shall comply with the requirements of SANA specifications 545 and bear the "MARK"	No	10.00		
		.02 Aluminium windows/doors and frames (Natural anodised)				
		.01 Aluminium 2-panel single slider sliding door 1500 mm wide and 2100 mm high	No	2.00		
		.02 Aluminium 2-panel single slider sliding door 2100 mm wide and 2100 mm high	No	2.00		
	203.07	0 01 Steel door frames				
		.01 1,6 mm thick pressed steel door frame for door size 813 mm x 2032 mm high suitable for 115 mm wall	No	2.00		
		.02 1,6 mm thick pressed steel door frame for door size 813 mm x 2032 mm high suitable for 230 mm wall	No	2.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	203.08	0.02 Steel garage doors and frames				
		0.01 CHROMADEK steel roll up door withh frame and locking device for 2400 mm x 2135 mm high opening in 230 mm walls	No	5.00		
	203.09	Joinery:				
		Items measured by number				
		.01 Solid laminated door, 40 mm thick x 813 mm wide x 2032 mm high with meranti veneer both sides	No	10.00		
		.02 Semi-solid core flushpanel door, 40 mm thick x 813 mm wide x 2032 mm high with meranti veneer both sides	No	3.00		
		.03 Framed, ledged and braced batten hardwood door, 40 mm thick x 813 mm wide x 2032 mm high with splayed wehther board	No	8.00		
	204.00	METAL WORK				
		Replace hydraulic overhead door closer "dorma TS91B" or similar approved as existing	No	6.00		
		Replace natural aluminium patio door roller system with heavy duty double roller unit	No	10.00		
		Replace natural aluminium patio door roller guides	No	30.00		
		Supply and fit natural anodised aluminium tri panel sliding shower door 950 mm x 1850 mm with clear safety glass	No	2.00		
		Supply and fit aluminium 50x50x4mm equal angles screwed to brick walls	m	25.00		
	204.01	Ironmongery, Steelwork, glass, wall finishings, etc				
		.01 Supply, install and removal of existing:				
		.01 Cupboard pull handles	No	75.00		
		.02 Standard brass peg and stay to residential steel windows	No	15.00		
		.03 Standard brass sliding stay to residential steel windows	No	10.00		
		.04 Residential type steel window handle	No	15.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.05 100 mm brass barrel bolt	No	6.00		
		.06 cupboard door lockset	No	23.00		
		.07 Four lever mortice lockset with one pair handles chrome type B2088, two keys, back plates and striking plate	No	30.00		
		.08 Four lever mortice lockset with one pair anodised aluminium handles type B2085, two keys, back plates and striking plate	No	30.00		
		.09 Four lever mortice lockset with one pair anodised aluminium handles and back plate type B2086, two keys, back plates and striking plate	No	16.00		
		.10 Cylinder lever lockset with one pair handles chrome type B2088, two keys, back plates and striking plate	No	14.00		
		.11 Indicator bolt with one pair anodised aluminium handles type B2085, display back plates and striking plate	No	9.00		
		.12 facility indicator bolt for disabled facilities with one pair anodised aluminium handles type B2581, display back plates and striking Plate	No	6.00		
		.13 Anodised aluminium door handles type B2085	No	3.00		
		.14 Striking plate for single door	No	10.00		
		.15 6 mm thick mirror glass 450mm x 300 mm wide	No	3.00		
		.17 Vertical fabric blinds as approved by Engineer fit to existing windows smaller than 1m2	m2	20.00		
		.18 Vertical fabric blinds as approved by Engineer fit to existing windows larger than 1m2	m2	20.00		
		.19 washing line with 2 fully galvanised posts and stays, 5m apart and 4 plastic coated washing lines complete with straining bolts concrete base, etc	No	1.00		
		.20 Stainless steel toilet paper dispensing units, capable of holding two toilet paper rolls (Similar to existing)	No	10.00		
		.21 Aluminium weather strips 813 to 915 wide door	No	12.00		
		Carried forward				

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.22 Rubber door stops 35mm dia by 30mm high	No	12.00		
		.23 150 mm Natural Anodised Aluminium disabled sign type B2312 or similar approved	No	10.00		
		.24 150 mm Natural Anodised Aluminium male sign type B2312 or similar approved	No	10.00		
		.25 150 mm Natural Anodised Aluminium female sign type B2314 or similar approved	No	10.00		
		.27 150mm Natural Anodised Aluminium no entry or exit sign type B2315 or similar approved	No	10.00		
		.28 175 mm high Aluminium number signage to be securely fitted to external walls at residential buildings	No	23.00		
		.29 standard arm door closer, with adjustable closing speed speed, adjustable hydraulic latch action, suitable for doors up 1100 mm	No	2.00		
		.30 Aluminium sliding shower door "TRI-SLIDER" with range of up to 1550mm wide x 1900mm high	No	4.00		
		.31 19 mm diameter chromium plated towel or hanging rail 650 mm long including end brackets	No	3.00		
		.32 19 mm diameter chromium plated towel or hanging rail 1200 mm long including end brackets	No	3.00		
		0.33 380 mm x 610 high bathroom cabinet(white) with mirror, two doors, handles and one shelf	No	3.00		
		.34 6 mm polished edge mirror size 300mm wide 450 mm high fixed with chrome plugged screws	No	3.00		
		.35 Custom made Aluminium Fly screen for opening smaller than 1m2 including gauze	m ²	3.00		
		.36 Custom made Aluminium Fly screen for opening larger than 1m2 including gauze	m ²	3.00		
		.37 Kick Plate 800x300x1,2mm Stainless Steel fixed to bottom of doors	No	6.00		
		.38 Supply and install security gate for single door constructed of 25x25mm steel tubing frame and ledge with 16mm dia steel rod inserts at 70mm c/c incl. pin lock mechanism.	No	2.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		,39 Powder coated key cabinet (480 mm x 350 mm x 60 mm) with key capacity	No	1.00		
		,40 Double Cylinder Lockset, two keys, back plate and striking plate	No	20.00		
		,41 3 mm thick Perspex signage for general information	m ²	20.00		
		,42 Stainless steel sanitizer (similar to existing)	No	2.00		
		,43 Stainless steel air freshener (Similar to existing)	No	2.00		
		,44 Stainless steel she bins (Similar to existing)	No	2.00		
		,45 Stainless steel soap dispenser (Similar to existing)	No	2.00		
		,46 Hand dryer unit with blower output of 450 watt @ 20 000 rpm	No	2.00		
		,47 Galvanised heavy duty 2.8m diameter rotating washing line with upright dia of 48mm complete with concrete base, 30m plastic coated line, as approved by engineer	No	1.00		
		,48 Plastic coated washing line	m	250.00		
		,49 Aluminium framed pivot shower door natural anodised 850mm to 1150mm wide	No	3.00		
	204.02	Burglar bars consisting of 12 mm thick steel rods, burglar bar type BB25 or similar approved, welded into one window opening on site per frame as stated below				
		.01 Window size 949 mm high x 1511 mm wide	No	10.00		
		.02 Window size 949mm high x 533 mm wide	No	10.00		
	204.03	Items measured by linear metre				
		.01 Silicone sealant in 6 mm contact joint between sanitary fittings and wall finishes	m	27.00		
		.02 Polyurethane/Polysuphide sealant in 12 mm expansion joint in face brick walls	m	30.00		
		.03 Putty in patchwork to steel sashes	m	42.00		
		.04 Regular duty double curtain track including gliders, hangers, brackets, stopped ends, etc	m	20.00		
		Carried forward				

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.05 230 mm wide face brick roller course Horizon Satin - FBS or similar approved	m	12.00		
		Service of existing equipment and refix:				
		.01 Hand dryer blowing unit	No	14.00		
		.02 Stainless steel sanitizers including replacement of cartridge and batteries	No	24.00		
		.03 Stainless steel air freshener including replacement of cartridge and batteries	No	10.00		
		.04 Stainless steel soap dispenser	No	19.00		
		.05 Aluminium sliding or pivot shower door	No	170.00		
		.06 Roll up garage door including servicing opening mechanisms, locks, etc	No	37.00		
		.07 Single Aluminium door and frame	No	6.00		
		.08 Aluminium sliding door and frame	No	12.00		
		Supply, fit and remove existing:				
	204.04	Items measured by area:				
		.01 4 mm clear float glass to steel sashes with putty	m ²	10.00		
		.02 4 mm obscure glass to steel sashes with putty	m ²	10.00		
		.03 115 mm thick brick walls	m ²	20.00		
		.04 230 mm thick brick walls	m ²	50.00		
		.05 230 mm thick face brick walls Buff Satin- FBS or similar approved	m ²	15.00		
		.06 Internal cement plaster to walls	m ²	200.00		
		.07 External cement plaster to walls	m ²	100.00		
		.08 6mm clear float laminated glass	m ²	5.00		
		.09 High tensile welded steel wire brick reinforcement 75 mm wide built horizontally into brickwork, including all laps , bending, cutting, notching etc.	m	180.00		
		.10 High tensile welded steel wire brick reinforcement 150 mm wide built horizontally into brickwork, including all laps , bending, cutting, notching etc.	m	120.00		
		Carried forward				

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		,11 White glazed wall tiles (150mm x 150mm) to painted or plastered walls	m ²	20.00		
		,12 Ceramic wall tiles (200mm x 200mm) to painted or plastered walls colour as approved by engineer	m ²	20.00		
		,13 Extra over for Corobrick Corn Gold face brickwork with recessed vertical and horizontal joints in stretcher bond	m ²	15.00		
		,01 Regrout existing tiles	m ²	200.00		
	205.00	WATER PROOFING				
		"Derbigum" or similar approved torch-on bitumous membrane to all concrete flat roofs including 100 mm turn-ups as per manufacturers specification	m2	100.00		
	205.01	ALTERATION WORK				
		Alterations and repairs to existing structures:				
	205.02	0.01 Repair and refix:				
		0.01 Single doors	No	23.00		
		0.02 Double doors	No	10.00		
		0.03 Window frames	No	13.00		
		0.04 Door frames	No	16.00		
		0.05 Aluminium or steel flyscreen door	No	4.00		
		0.06 Tip up single garage door including servicing opening mechanisms, locks, etc	No	6.00		
		0.07 Aluminium sliding Shower door	No	6.00		
	205.03	0.02 Remove				
		0.01 Timber single door	No	10.00		
		0.02 Timber double door	No	6.00		
		0.03 Cupboard lockset	No	12.00		
		0.04 Mortice lockset with handles	No	20.00		
		0.05 Peg and stay to residential steel	No	16.00		
		Carried forward				

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		0.06 Sliding stay to residential steel window	No	16.00		
		0.07 Residential type steel window handle	No	16.00		
	206.00	BE: FLOORS				
	206.01	EARTHWORKS (SMALL WORKS)				
		SCHEDULED ITEMS				
		Restricted excavation:				
		.01 Excavate for trenches, footings and foundations in all materials and use for backfill or embankment or dispose	m ³	50.00		
	206.02	BUILDING WORK				
		Floor screeds:				
		.01 35 mm thick granolithic screed finish	m ²	230.00		
	206.03	Joinery:				
		Items measured by linear metre:				
		.01 19 mm x 76 mm hardwood skirting with quadrant bead	m	100.00		
		.02 75mm x 10 mm Ceramic floor tiles in skirtings	m	100.00		
		.01 19 mm x 19 mm hardwood skirting with quadrant bead	m	100.00		
	206.04	Floor tiling and finishes. etc:				
		Items measured by area:				
		.01 250 micron damp proofing under solid floors	m ²	450.00		
		.02 White glazed wall tiles 200 mm x 200mm x 6mm as approved by engineer including removal of old, preparation, tile adhesive and waterproof grouting.	m ²	150.00		
		.02 2,5 mm thick semi-flexible vinyl floor tiles	m ²	100.00		
		.03 40 mm x 40 mm x 4 mm thick Mosaic floor tiles on paper backing bedded in waterproofing 3:1 cement screed and flushing-up joints with waterproof white grout as approved by engineer	m ²	150.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.04 410 mm x 410 mm x 6 mm Ceramic floor tiles	m ²	100.00		
		.05 350 mm x 350 mm x 8mm Ceramic floor tiles as approved by engineer including removal of old, preparation, tile adhesive and waterproof grouting.	m ²	30.00		
		.06 350 mm x 350 mm x 8 mm Ceramic floor tiles	m ²	8.00		
		.07 Pavelite or equal approved skim coat to receive vinyl floor tiles	m ²	600.00		
	206.05	Clean and remove stains marks:				
		.01 Carpet floor covering by steam cleaning or dry-powder cleaning	m ²	38.00		
	207.00	ALTERATION WORK				
		Alterations and repairs to existing structures:				
	207.01	.01 Remove and clean				
		.01 Vinyl floor tiles	m ²	240.00		
	207.02	.02 Break out/hack and clean				
		.01 Cement plaster screed on floors	m ²	400.00		
		.02 Ceramic tiles to floors in patches	m ²	600.00		
	207.03	Refix, sand down to smooth and even surface and seal with approved sealer as described in Item BE 03.01.11 of the Project Specification				
		0.01 Wood block flooring	m ²	30.00		
	207.03	Cleaning and sealing of floor surfaces				
		01 Vinyl floor tiles as per technical specification BE 06.01.01 for cleaning	m ²	300.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	207.04	FITTINGS				
		Steelwork and joinery:				
		Items measured by number:				
	207.05	.01 Standard approved hardwood veneered particle board				
		.01 Kitchen cupboard door	No	15.00		
		.02 Kitchen cupboard drawer	No	18.00		
	207.06	.02 Cupboard ironmongery 0.8mm thick steel baked enamel with 32mm Formica tops				
		.01 Hinge for kitchen cupboard door	No	15.00		
		.02 Kitchen cupboard pull handles	No	30.00		
		.03 Wall unit size 1 500 mm x 300 mm x 580 mm high with three doors and one shelf	No	2.00		
		.04 Wall unit size 1 800 mm x 300 mm x 580 mm high with four doors and one shelf	No	2.00		
		.05 Base unit size 1 500 mm x 533 mm x 865 mm high with three doors, three drawers and one shelf	No	2.00		
		.06 Base unit size 1 800 mm x 533 mm x 865 mm high with four doors, four drawers and one shelf	No	2.00		
		.07 Base double bowl sink unit size 1500 mm x 533 mm x 865 mm high with three doors, and one shelf	No	2.00		
		.08 Base double bowl sink unit size 1300 mm x 533 mm x 865 mm high with three doors, and one shelf	No	2.00		
	207.07	Items measured by linear metre:				
		.01 32 mm chipboard with "Formica" laminated finish on one side and profiled edges where so described	m	21.00		
		.02 Work top 600 mm wide with profiled front edge and fitted on top of kitchen cupboard floor unit 32 mm x 1,2 mm "Formica" veneered edge strips	m	15.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.04 32 mm Meranti counter and profiled edges where so described:				
		.01 Work top 600 mm wide with profiled front edge				
	208.00	ALTERATION WORK				
		Alterations and repairs to existing fittings:				
	208.01	1 Service, repair and refix kitchen cupboards as per Project Specification BH 03.01.02				
		.01 Kitchen cupboard door	No	25.00		
		.02 Kitchen cupboard drawer including	No	42.00		
	208.02	.02 Removal of existing steel or wooden kitchen cupboards				
		0.01 Sink unit up to 2000mm long	No	50.00		
		.02 Base unit up to 2000mm long	No	50.00		
		.03 Wall unit up to 2000mm long	No	50.00		
	209.00	PREVIOUSLY PAINTED SURFACES				
		Paint to previously painted surfaces:				
	209.01	Concrete surfaces:				
		.02 Alkali resistant solvent based (modified alkyd) stoep paint,				
		.01 Floors	m ²	500.00		
		.02 Window sills, etc	m ²	500.00		
	209.02	Plaster surfaces:				
		.01 Interior quality acrylic emulsion paint with smooth sheen appearance				
		.01 Walls residential areas	m ²	4,500.00		
		.02 Walls operational areas	m ²	4,500.00		
	209.03	Exterior quality pure acrylic emulsion paint with Teflon				
		.01 Walls and piers residential areas	m ²	2,700.00		
		.02 Walls and piers operational areas	m ²	2,700.00		
		Carried forward				

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	209.04	Ceiling				
		.01 Buildings in residential areas	m ²	2,400.00		
		.02 Buildings in operational areas	m ²	650.00		
	209.04	Roofs (Clean and prepare surface and apply 2 coats of quality acrylic emulsion on existing ceiling)				
		.01 Buildings in residential areas - GI sheeting	m ²	1,800.00		
		.02 Buildings in residential areas - Concrete tiles	m ²	1,800.00		
		.03 Buildings in operational areas - GI sheeting	m ²	640.00		
		.04 Buildings in operational areas - Concrete tiles	m ²	640.00		
	209.05	Protective and decorative solvent based polyurethane alkyd semi gloss non-drip enamel paint:				
		.01 Walls	m ²	2,000.00		
		.02 Ceilings	m ²	610.00		
	209.06	Quarry tile surfaces:				
		.01 Alkali resistant solvent based (modified alkyd) stoep paint:				
		.01 Window sills	m ²	20.00		
	209.07	Fibre cement Surfaces:				
		.01 Protective and decorative solvent based polyurethane alkyd semi gloss non-drip enamel paint				
		.01 Walls	m ²	250.00		
	209.08	Exterior quality super acrylic copolymer PVA paint:				
		.01 Ceilings and cornices	m ²	600.00		
		.02 Walls	m ²	600.00		
	209.09	Super universal high gloss enamel paint				
		.01 Fascias and barge boards	m ²	200.00		
	209.10	Interior quality super acrylic copolymer PVA paint	m ²	5,000.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	209.11	Softboard surfaces				
		.01 Interior quality super acrylic copolymer PVA paint				
		01 Ceilings and cornices	m ²	90.00		
	209.12	02 Protective and decorative solvent based polyurethane alkyd semi- gloss non-drip enamel paint				
		.01 Ceilings and cornices	m ²	55.00		
	209.13	Galvanised steel surfaces.				
		.01 Super universal high gloss enamel paint.				
		.01 Gutters	m ²	50.00		
		.02 Rainwater down pipes	m ²	50.00		
	209.13	Steel surfaces:				
		01 Super universal high gloss enamel paint				
		.01 Residential type glazed windows	m ²	50.00		
		02 Window burglar proofing or mentis expanded metal grid to steel frame in burglar proofing	m ²	12.00		
		.03 Doors	m ²	16.00		
		04 Door frames	m ²	20.00		
		.05 Garage doors and frame	m ²	6.00		
		0.06 Security gates	m ²	10.00		
		0.07 Rails, pipes, etc not exceeding 50mm diameter	m	15.00		
		0.08 Pipes exceeding 50 mm dia not exceeding 100 mm dia	m	10.00		
		0.09 Steel structures	m ²	100.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	209.14	Wood surfaces:				
		.02 Protective and decorative solvent based polyurethane alkyd semi gloss non-drip enamel paint:				
		.01 Doors	m ²	150.00		
		02 Skirtings and quadrant beads not exceeding 150 mm girth	m	20.00		
	209.15	.03 Protective and decorative solvent based polyurethane alkyd semi- gloss non-drip enamel paint in dark colours:				
		01 Skirtings and quadrant beads not exceeding 150 mm girth	m	25.00		
	209.16	.04 Water resistant polyurethane clear matt varnish:				
		01 Doors	m ²	230.00		
		02 Cupboard doors	m ²	300.00		
		.03 Cupboards, counters, shelving, etc	m ²	300.00		
		.04 Skirtings and quadrant beads not exceeding 150 mm girth	m	15.00		
	209.17	05 Ultra violet light resistant exterior solvent based varnish:				
		01 Doors	m ²	25.00		
	209.18	.06 Rust converter application				
		01 Strips not exceeding 300 mm girth to steel surfaces of carports	m	12.00		
	209.19	.01 Super universal high gloss enamel	m ²	500.00		
	209.20	Painting of existing members in overhangs:				
		.01 Members with creosote	m	1,800.00		
		.02 Members with paint	m	1,300.00		
		RAMPS FOR DISABLED				
		.01 Construct ramps for the disabled at ALEXANDER BAY to allow exit through the back side for emergency evacuation	Sum	1.00		
	Carried forward					

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		JOINERY The following cupboard fittings have been measured as complete units i.e. the components of the units have not been separately measured. The descriptions, therefore, of such units shall be deemed to include all components, assembling, housing, notching, gluing, blocking, planting on and screwing with countersunk screws, edge strips, decorative plastic laminate of approved colour and pattern, glass, ironmongery, metalwork, etc Cupboard, etc of 16mm low-pressure decorative board with self-edging including spring-loaded hinges, plastic pull handles, etc where applicable .01 Replace single cupboard door, doors 580 x 750mm high. .02 Replace double cupboard door, doors 1056 x 750mm high .03 Replace double cupboard door, doors 1400 x 750mm high .04 Replace double cupboard door, doors 1600 x 750mm high .05 Replace double cupboard door, doors 1600 x 750mm high .06 Replace 900 x 1400mm Long worktop formed of 32mm thick stocklam, fixed to 50 x 50 x 5mm equal angle (angle measured elsewhere) MARRIED QUARTERS CUPBOARDS The following cupboard fittings have been measured as complete units i.e. the components of the units have not been separately measured. The descriptions, therefore, of such units shall be deemed to include all components, assembling, housing, notching, gluing, blocking, planting on and screwing with countersunk screws, edge strips, decorative plastic laminate of approved colour and pattern, glass, ironmongery, metalwork, etc ,01 Replace sink cupboard complete 915mm high x 600mm deep x 1460mm long with bottom, back sides and one division, hinged double door approximately 1000 x 800mm high, single door approximately 500 x 800mm high with solid oak 25mm edges				
			No	1.00		
			No	1.00		
			No	1.00		
			No	1.00		
			No	1.00		
			m	1.00		
			No	1.00		
		Carried forward				

SCHEDULE NO 2.1: INSTALLATION C1: STRUCTURAL AND BUILDING

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.02 Replace sink cupboard complete 915mm high x 530mm deep x 2084mm long with bottom, back sides and one division, two hinged double doors approximately 1000 x 800mm high with solid oak 25mm edges	No	1.00		
		.03 Replace three hinged double doors 900 x 2450mm high with solid oak 25mm edges	No	1.00		
		.04 Replace two hinged double doors one average 1500mm high and the other 2100mm high with solid oak 25mm edges	No	1.00		
		.05 Replace three hinged double doors 1050 x 2450mm high with solid oak 25mm edges	No	1.00		
		.06 Replace two hinged double doors 1400 x 2450mm high with solid oak 25mm edges	No	1.00		
		.07 Replace single door 650 x 2000mm high with solid oak 25mm edges	No	1.00		
		.08 32mm Interior type particle board with 1.2mm decorative plastic laminate of approved colour and pattern on exposed faces and balancing oak veneer on both side as existing	m	2.00		
		.09 Replace floor mounted tall unit for brooms, hinged single door 550 x 2000mm high with balancing oak edging including hinges etc.	No	1.00		
		.10 Replace hinged double door 1000 x 800mm high with solid oak 25mm edges	No	1.00		
		.11 Replace cupboard drawers, 210mm high with solid oak 25mm edges	No	1.00		
		.12 Replace cupboard drawer 420mm high with solid oak 25mm edges	No	1.00		
		.13 Replace hinged door 1000 x 600mm high with solid oak 25mm edges	No	1.00		
		.14 Replace hinged single door approximately 500 x 600mm with solid oak 25mm edges	No	1.00		
		.15 Replace two hinged double doors 1000 x 800mm high with solid oak 25mm edges	No	1.00		
		.16 Supply and fit crash resin moulded dado rails 70x18mm glued to walls	m	10.00		
		.17 Supply and fit 42mm solid maranti framed and ledged batten stable doors 2032x813mm with rebated meeting stiles	No	1.00		
	TOTAL	SCHEDULE 2.1 : INSTALLATION C1: STRUCTURAL AND BUILDING - CARRIED TO SUMMARY:				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES**CIVIL REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		DETAIL WORK				
		Isolation, stripping, dismantling and removal of existing brassware, sanitary ware and piping installations:				
		.01 Water closets.				
		.01 Vitreous china WC pan (cistern type)	No	5.00		
		.02 Vitreous china WC cistern	No	6.00		
	206.00 BB:	.03 Tail pipe connections to WC, including shut of valve	No	7.00		
	206.01	.04 100mm dia pan connector	No	5.00		
		.05 Toilet seat and cover	No	10.00		
		.02 Washhand basins				
	206.02	01 Vitreous china wall-mounted wash hand basin	No	10.00		
		.02 15 mm 121 pillar taps	No	8.00		
		03 15 mm 121 pipe connections to pillar taps	No	8.00		
		.04 Rubber flexi p-trap or CP bottle trap	No	8.00		
		.05 15 mm CP sink mixer	No	12.00		
		.06 15 mm CP paraplegic pillar elbow action tap	No	2.00		
		03 Urinals				
	206.03	.01 Build in or wall hung urinal	No	6.00		
		.02 Junior flush valve	No	6.00		
		03 Rubber flexi p-trap or CP bottle trap	No	7.00		
	Carried forward					

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	207.00	4.00 Sinks				
		1.00 20mm wall mounted taps	No	6.00		
	208.00	.02 15mm sink mixer	No	6.00		
		03 Rubber flexi P-trap or combination trap	No	6.00		
		.05 Showers:				
		.01 CP Shower heads	No	12.00		
		.02 Undertile stop cocks	No	16.00		
	2010.00	.03 Shower gratings	No	8.00		
		.04 15 mm CP shower arm with fascia plate and male iron connection - SABS approved	No	6.00		
		.06 Baths				
		.01 Bath mixer complete with shower head attachment.		6.00		
		.02 20mm wall mounted taps				
	300.00					
		.07 External				
	300.00					
		.01 20mm dia RB hose bip tap	No	25.00		
	300.01	Isolation, stripping, dismantling and removal of existing geyser installations:				
		.01 Isolate strip and remove domestic geyser (100 to 250 litres - electric)	No	10.00		
		Supply and installation of sanitary ware and brassware:				
		.01 Water closets:				
		01 Vitreous china WC washdown pan with enlarged pedestal	No	8.00		
		0.02 Vitreous china WC cistern - white 9 liters complete with lid and fitments	No	7.00		
		03 100 mm dia PVC pan connector	No	8.00		
		.04 15 mm dia CP ball-o-stop valve with CP flexi tail pipe to WC cistern	No	8.00		
	Carried forward					

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.05 Heavy duty white buckalite type toilet seat and cover with CP hinge and spindle	No	45.00		
		0.02 Washhand basins:				
		.01 Vitreous china 520 x 415mm rounded wall mounted wash hand basin - white	No	5.00		
		.02 Flexi rubber P-trap or S-trap	No	14.00		
		.03 CP Bottle trap with 75mm deep re-seal and adjustable telescopic pipe	No	5.00		
		.04 15 mm dia CP pillar taps SANS 226 Type 1 (BS 5412), JASWIC Listed	No	14.00		
		.05 15 mm dia flexi pipe tailpipe connections to pillar taps including 15mm CP ball-o-stop valve	No	5.00		
		.06 15 mm ø CP paraplegic pillar elbow action tap	No	2.00		
		.03 Sinks				
		.01 CP wall-mounted sink mixer 15 mm "-SANS 226 Type 1 (BS 5412), JASWIC Listed	No	12.00		
		.02 20mm CP wall-mounted hose bip tap -SANS 226 Type 1 (BS 5412), JASWIC Listed	No	12.00		
		.03 Flexi rubber combination trap for double bowl sink	No	12.00		
		.04 Urinal				
		.01 Vitreous chine wall hung urinal with top inlet including fittings.	No	12.00		
		.02 3/4" 'Flushmaster Junior' Urinal Flush valve,CP, exposed type with integral ballstop valve and wall plate	No	12.00		
		.03 CP Bottle trap with 75mm deep re-seal and adjustable telescopic pipe.	No	12.00		
		.04 CP urinal spreader and tail piece	No	14.00		
		05 Showers.				
		.01 15mm CP Shower rose 50mm dia with ball joint connector	No	35.00		
		.02 15 mm dia under-tile stop-cocks -SANS 226 Type 1 (BS 5412), JASWIC Listed	No	35.00		
	300.01					
		Carried forward				

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	300.02	.03 CP shower grating	No	35.00		
		.04 15mm CP shower arm with fascia plate and male iron connection	No	15.00		
		.06 Baths				
	300.03	01 Rubber flexi bath-trap	No	25.00		
		.02 20 mm dia CP wall mounted taps SANS 226 Type 1 (BS 5412), JASWIC Listed	No	25.00		
		.03 20 mm dia CP pillar taps SANS 226 Type 1 (BS 5412), JASWIC Listed	No	25.00		
		.04 3/4 Bath mixer. CP, wall type with concealed connections adjustable from 138mm to 218mm.	No	12.00		
		.05 3/4" CP Handshower attachment	No	12.00		
		.06 20mm ø CP bath mixer with cascade hand shower and attachments	No	12.00		
		07 External				
		.01 20mm Hose biptap, rough brass, with BSP hose union - SANS 26 Type 2	No	16.00		
		Installation of above ground sanitary drainage piping systems				
		.01 uPVC soil and waste pipes:				
	300.03	01 50 mm dia pipe fixed to walls and soffits	m	100.00		
		02 110mm dia soil pipe fixed to walls and soffits	m	100.00		
		.02 uPVC soil and waste pipe fittings				
		.01 50 mm dia access bend 87.5°	No	5.00		
		.02 50mm dia plain bend 135°	No	5.00		
		.03 50mm junction access heel 87.5°	No	5.00		
		.04 110mm dia plain bend 135°	No	5.00		
		02 .05 110mm dia access bend 87.5°	No	5.00		
		.06 110mm dia plain bend 90°	No	5.00		
		07 110mm vent horn bend access heel 95°	No	5.00		
	Carried forward					

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		Supply and installation of underground sanitary drainage pipes:				
		.01 Pipe trench excavations, bedding and backfilling:				
		01 Excavate in all materials for pipe trenches to depth of 1100 mm x 600 mmwide	m³	20.00		
		0.02 Supply and installation of river sand pipe bedding	m³	20.00		
		03 Backfilling and compacting to 93% modified AASHTO density with selected material	m³	20.00		
		.02 PVC-U Solid wall sewer pipes Class 3.4 - 300 KPA to SANS 791 specifications				
		01 110 mm dia	m	36.00		
		03 uPYC soil and waste pipe fittings				
		.01 110 mm dia plain bend 87.5°	No	5.00		
		.02 110 mm dia plain bend 135°	No	5.00		
		03 110 mm dia square junction	No	5.00		
		.04 110 mm dia 45° junction plain	No	5.00		
		.05 110 mm dia 45° Junction access	No	5.00		
		.06 160 mm dia plain bend 87,5°	No	5.00		
		.07 160 mm dia plain bend 135°	No	5.00		
		.08 160 mm dia square junction	No	5.00		
		0.09 160 mm dia 45° junction plain	No	5.00		
		.10 160 mm dia 45° junction access	No	5.00		
160 mm dia 45° reducing function plain	No	5.00				
	Carried forward					

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.04 Cleaning eyes:				
		.01 100 mm dia inline cleaning eye, constructed complete with Square inspection eye cast iron cover and frame Type 14A (SANS 558) daylight opening size 265 x 265mm and concrete encasement				
		Supply and installation of domestic water piping installation:				
		Copper Tubing class 2 in walls and ducts				
		0,.1 15 mm dia Class 2 copper tubing	m	100.00		
		0.2 22 mm dia Class 2 copper tubing	m	80.00		
		0.3 28 mm dia Class 2 copper tubing	m	15.00		
		0.4 Extra over for 15 mm connex fittings	No	80.00		
		0.4 Extra over for 22 mm connex fittings	No	90.00		
		0.4 Extra over for 28 mm connex fittings	No	24.00		
		.01 Copper piping Class 0 SANS 460 with capillary soldered type joints for cold-water piping installed in voids inclusive of bracketing				
		.01 22 mm dia including fittings	m	50.00		
		.02 15 mm dia including fittings	m	20.00		
		.02 Copper piping Class 0 SANS 460 with capillary soldered type joints for hot-water piping installed in voids including bracketing, lagging and cladding.				
	300.04	01 22 mm including fittings	m	50.00		
		.02 15 mm dia including fittings	m	20.00		
		Copper piping Class 0 SANS 460 with capillary soldered type Joints for hot and cold-water piping chased in walls including wrapping of pipes with builders paper, chasing and reinstatement of chased Surfaces:				
	300.05	.01 22 mm dia including fittings	m	50.00		
		Carried forward				

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.02 15 mm dia including fittings	m	10.00		
		.04 Supply and installation of Class 6 pressure HDPE piping, including fittings, jointing and testing				
		01 20 mm dia HDPE pipe,including fittings	m	10.00		
		02 32 mm dia HDPE pipe, including fittings	m	10.00		
		05 Replace additional geyser accessories				
		.01 20 mm dia pressure-reducing valve, including two gate vales and non-return valve set at 400 kPa	No	70.00		
		.02 Brass vacuum breaker	No	9.00		
		.03 Safety valve	No	9.00		
		,04 15 mm ball stop valve	No	24.00		
		06 Water meter stations installed including strainer and one ball-o-stop shut-off valve with galvanised mild steel medium guage pipe connection 600mm above ground including 500 x 500 concrete 20Mpa base.				
		.01 22 mm Dia water meter	No	10.00		
		.02 50 mm dia water meter	No	2.00		
		.01 110 mm dia water meter	No	1.00		
		.07 Replace 20 mm dia shut-off ball-o-stop valve	No	150.00		
		Supply and installation of domestic geyser installations including two shut-off strainer, galvanised mild steel drip valves tray if, necessary, non-return valve, expansion relief valve, safety valve, drain piping and electrical connection:				
		.01 SANS151 dual 150 liter. 3 kW 600kPA approved geyser	No	9.00		
		0.02 Kwikot Econoflo (or similar approved), 100 litre, 2 kW	No	9.00		
		Carried forward				

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		Supply and installation of domestic solar geyser installations close coupled thermosiphon system with pitch roof support including two shut-off valves, solar mixing valve , non-return valve, expansion relief valve, safety valve, drain piping and electrical connection:				
		.01 Solar system jndirect (200lt) close coupled thermosiphon system with roof (or similar approved)	No	5.00		
		.02 Solar system jndirect (187lt) close coupled thermosiphon system with roof (or similar approved)	No	3.00		
		Servicing, cleaning and repair of sanitary were				
		.01 Water closets				
		01 Destaining of WC pan	No	290.00		
		02 Service WC cistern flushing mechanism with repair kit	No	30.00		
		.02 Wash hand basins				
		01 Destaining of WHB	No	300.00		
		.03 Urinals				
		.01 Destaining of Urinal	No	12.00		
		.02 Service flush valve	No	12.00		
		.03 Sink				
		.01 Destaining of Sink	No	50.00		
		.04 Showers				
		.01 Clean shower trap and grating	No	200.00		
		Servicing, overhauling and cleaning of brassware.				
		.01 Replace washers on brassware with washer kits				
		0.01 15 mm dia CP pillar taps	No	35.00		
		.02 20 mm dia CP pillar taps	No	35.00		
	300.06					
		Carried forward				

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		03 15 mm dia CP wall-mounted taps	No	30.00		
		.04 20 mm dia CP wall-mounted taps	No	100.00		
		.05 20 mm dia brass hose bib taps	No	30.00		
		.06 20mm under wall stop taps	No	100.00		
		.07 15 mm CP sink mixers	No	100.00		
		08 25mm Junior flush master, including replacing flush master kits	No	2.00		
		.09 15 mm dia shut-off gate valve	No	20.00		
		.010 20 mm dia shut-off gate valve	No	10.00		
		.11 32 mm dia shut-off gate valve	No	6.00		
		.12 50 mm dia shut-off gate valve	No	4.00		
		Servicing and repair of water, drainage and fire water pipe installations				
		.01 20 mm dia stop-cocks	No	24.00		
	300.06 04	.01 Servicing and repair of drainage installations				
		.01 Unblock and clean pipework including fittings, 50 mm dia pipe	No	10.00		
		.02 Unblock and clean pipework including fittings, 100 mm dia pipe	No	25.00		
		.03 Unblock and clean gullies	No	15.00		
		.04 Replace damaged gully with pre-cast concrete gully	No	15.00		
		.05 Replace broken or damaged Gully P-traps	No	15.00		
		.06 Replace missing or broken round cast iron gully gratings 100mm - 300mm diameter	No	10.00		
	300.07	.07 Replace missing or broken square cast iron gully gratings 250mm x 250mm wide	No	10.00		
	Carried forward					

SCHEDULE NO 2.2: INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.08 Replace missing or broken vent valve for air vent	No	15.00		
		.09 Replace missing or broken cast iron inspection eye cover and frame only SANS 558 Type 14A in 500 x 500m concrete encasement	No	15.00		
		Servicing, cleaning and repair of domestic geysers:				
		01 100-200 litre electric geyser	No	10.00		
		Servicing and cleaning of domestic solar geysers as per specification SA and manufacturers specification by approved service provider:				
		.01 100-200 litre electric geyser	No	150.00		
		.02 Solar system indirect close coupled (or similar approved:				
		.01 Thermostat	No	150.00		
		.02 2kw Element	No	80.00		
		.03 3kw Element	No	25.00		
		.04 Female TP Safety Valve	No	10.00		
		.05 Male TP Safety Valve	No	20.00		
		.06 Vacuum Breaker	No	25.00		
		.07 Expansion Bottle pump (5litre)	No	2.00		
		.08 Expansion Bottle pump (8litre)	No	4.00		
		.09 Brass DC Circulator Pump	No	2.00		
		.10 Photo Voltaic Solar Module 10Watt	No	6.00		
		.11 Photo Voltaic Solar Module 20Watt	No	10.00		
		.12 Insulation	No	20.00		
	TOTAL	SCHEDULE 2.2 : INSTALLATION C2: PLUMBING, DRAINAGE AND WET SERVICES - CARRIED TO SUMMARY:				

[illegible]

SCHEDULE NO 2.3: INSTALLATION C3:FENCING, CLEANING, SITE KEEPING AND PEST CONTROL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.05 Panels - 358 Double Line Wire Single .01 Heavy high security welded panel fence, with rectangular mesh Inner Apertures: 72.2mm x 8.7mm Wire diameter 4mm vertical wires are welded on both sides of the horizontal wires Width of panel: 3050mm Height of panel 1969m Tensile Strenght. 600 - 900N/mm2 Weld strenght 60 - 80% Weight: 9.34kg/m2 Coating Galfan Class A Coated in accordance with SANS 10244-2:2003 1.8m PERIMETER FENCE - DIAMOND MESH. TUBULAR STEEL POSTS Redress, treating and painting of 01 Gates: 01 Single gate of height 1,8 m or less .02 Double gate of height 1,8 m or less .02 Tubular posts .01 1,8 m high fence 03 Diamond mesh. .01 1,8 m diamond mesh Supply and erection of new fencing material to replace old material: .01 Diamond mesh 301.04 .01 1,8 m 2.5mm 50x50mm High diamond mesh .02 1,8 m 3.15mm 25x25mm High diamond mesh 02 Tubular posts: 304.01 01 75mm tubular post with concrete footing for 1.8 m high fence .02 110mm tubular post with concrete footing for 1.8m high fence	No	15.00		
			No	5.00		
			No	3.00		
			No	15.00		
			m	150.00		
	301.03	Supply and erection of new fencing material to replace old material:				
	301.04	.01 1,8 m 2.5mm 50x50mm High diamond mesh	m	150.00		
		.02 1,8 m 3.15mm 25x25mm High diamond mesh	m	150.00		
	304.01	01 75mm tubular post with concrete footing for 1.8 m high fence	No	10.00		
		.02 110mm tubular post with concrete footing for 1.8m high fence	No	10.00		
		Carried forward				

SCHEDULE NO 2.3: INSTALLATION C3:FENCING, CLEANING, SITE KEEPING AND PEST CONTROL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
	500.01	.03 75 mm tubular posts with additional 450 mm overhang at 450 and with concrete footing for 1.8m high fence	No	10.00		
		.04 110 mm tubular posts with additional 450 mm overhang at 450 and with concrete footing for 1.8m high fence	No	10.00		
		.03 65mm dia Stay for 1.8 m post	No	4.00		
		.04 Y-standards for 1,8 m high fence	No	2.00		
		.05 Straining wire	m	50.00		
		06 Barbed wire	m	600.00		
		.07 Barbed tape "Hatwrap", 700 mm dia.	m	50.00		
		.08 Anti-climb spikes	m	100.00		
		08 Gates in 1,8 m high fences				
		02 Double gate between 3.0 m and 10.0m wide	No	1.00		
		New Pedestrian (Single) Gates - 1.8m fence with 450mm additional overhang at 45°	No	4.00		
		RESIDENTIAL FENCE -1,2 m DIAMOND MESH, TUBULAR STEEL POSTS AND				
	500.01	Clearing of growth along fence route	m	500.00		
		Redress, treating and painting of:				
	501.00	.01 Gates				
	501.01	.01 Single gate of height 1,2 m or less	No	5.00		
		02 Double gate of height 1,2 m or less	No	5.00		
		02 Tubular posts and standards				
		.01 1,2 m high fence	No	20.00		
		03 Diamond mesh.				
		.01 1,2 m diamond mesh	m	95.00		
		Carried forward				

SCHEDULE NO 2.3: INSTALLATION C3:FENCING, CLEANING, SITE KEEPING AND PEST CONTROL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		Supply and erection of new fencing material to replace old material: .01 Diamond mesh: .01 1,2 m diamond mesh .02 Tubular posts for 1,2 m high fence 03 65mm dia Stay for 1.2 m post .04 V-standards for 1,2 m high fence 05 Straining wire .06 Gates .01 In 1,2 m high fences 1 single and double gates less than 1.5m wide 0.2 single and double gates between 1.5m and 5,0 m wide PERIMETER FENCE -2.4 m CONCRETE PALISADE, TUBULAR STEEL POSTS Redress, treating and painting of: .01 Gates .01 Single gate of height 2,4 m or less 02 Double gate of height 2.4 m or less 02 Tubular posts and standards .01 Posts 2400 mm x 100 mm x 2mm fully galvanized including concrete 03 Concrete Palisade .01 Secure, tighten nuts and install missing bolts and nuts for heavy duty concrete palisade fence including replacement of broken concrete slats: .01 2.4m high, 10 Pole at 2.0 m h/h with 450 mm overhang	m No No No m No No No m	150.00 15.00 15.00 15.00 150.00 2.00 2.00 10.00 5.00 10.00 1000.00		
	Carried forward					

SCHEDULE NO 2.3: INSTALLATION C3:FENCING, CLEANING, SITE KEEPING AND PEST CONTROL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	500.01	Supply and erection of new fencing material to replace old material:				
		01 Concrete Palisade				
		.01 2.4m high, 10 Pole at 2.0 m h/h with 450 mm overhang, fully installed	m	8.00		
		.02 Posts 2400 mm x 100 mm x 2mm fully galvanized including concrete	No	9.00		
		.03 Stays for 2400 mm fence	No	9.00		
		.04 Barbed wire	m	9.00		
		PERIMETER FENCE -3,0 m DIAMOND MESH, TUBULAR STEEL POSTS AND				
		Redress, treating and painting of:				
		01 Gates				
		501.00	.01 Single gate of height 3,0 m or less	No	18.00	
	501.01		02 Double gate of height 3,0 m or less	No	14.00	
		02 Tubular posts and standards		10.00		
	.01 3,0 m high fence	No				
	03 Diamond mesh.					
	.01 3,0 m diamond mesh	m	2610.00			
	Supply and erection of new fencing material to replace old material:					
	01 Diamond mesh:					
	.01 3.0 m diamond mesh	m	100.00			
	.02 Tubular posts for 3.0 m high fence	No	20.00			
	03 65mm dia Stay for 3.0 m post	No	20.00			
.04 Y-standards for 3.0 m high fence	No	80.00				
.05 Straining wire	m	10.00				
New Vehicle (Double) Gate - 3m fence with 450mm additional overhang at 45°	No	1.00				
	Carried forward					

SCHEDULE NO 2.3: INSTALLATION C3:FENCING, CLEANING, SITE KEEPING AND PEST CONTROL						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		REPAIR WORK TO FENCES				
		.01 Repair of wire and mesh fences less than 1,3m high	m	120.00		
		.02 Repair of wire and mesh fences between 1,3m and 2,0m high	m	200.00		
		SUPPLY OF WASTE BINS				
		.01 All Areas (180 litre waste bins including wheels)		10.00		
		PEST CONTROL				
		Pest Control Plan for Alexander Bay Port of Entry	site	1.00		
		Pest Control Plan for Vioolsdrift Port of Entry	site	1.00		
		Pest Control Plan for Onseepkans Port of Entry	site	1.00		
		Refilling of rodent bait stations with approved rodenticidal bait, including inspection, removal of expired bait, and replenishment to maintain effective pest control measures.	sum	1.00		
		<u>FLAGPOLE</u>				
		Outdoor 9m Aluminium Flagpole supported by a swivel based consisting of 2 x bases tubes of 78 mm dia, 1 meter high welded based to a palte 400mm x 350mm with gussets and internal halyard" Price	number	2.00		
	TOTAL	SCHEDULE NO 2.3: INSTALLATION C3:FENCING, CLEANING, SITE KEEPING AND PEST CONTROL - CARRIED TO SUMMARY:				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS

						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	400.00	BULK WATER AND BOREHOLE EQUIPMENT				
	401.00	Supply and place pipes, valves, fittings and specials				
		01 25mm dia Polycop pipe for measuring equipment strapped to HDPE pipe in borehole	m	120.00		
		.02 50mm dia GMS distance piece 300mm long flanged both ends	No	2.00		
		03 50mm dia GMS Special T 300 x 640mm flanged ends	No	2.00		
		.04 50mm - 25mm dia GMS Special reducer 300mm long for air release valve	No	2.00		
		.05 50mm dia GMS Flanged 900 bend	No	2.00		
		.06 50mm dia GMS pipe 2000mm long flanged	No	2.00		
		.07 Purpose made housing for bore holes as per detail A on drawing	No	2.00		
		.08 Corrosion resistant Pressure gauges for scale 0 - 800 Kpa	No	2.00		
		09 50mm to 22mm dia Adaptor for pressure gauges	No	2.00		
		.10 22mm Ball-o-stop valves for pressure gauges	No	4.00		
		.11 22mm GMS BSP T-crece, with GMS BSP nipples at two ends for connection of	No	4.00		
		.12 25mm dia air release valves	No	2.00		
		.13 25mm dia shut off ball-o-stop valve	No	4.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS
CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.14 50mm dia flanged butterfly non-return valve	No	2.00		
		.15 50mm dia flanged CI diaphragm valve	No	2.00		
		.16 50mm dia flanged water meter	No	4.00		
	402.00	17 Supply, install and commission rising main pipelines complete with straight coupling				
		.01 50 mm dia. HDPE Class 12	m	50.00		
		.02 63 mm dia. HDPE Class 12	m	50.00		
		03 75 mm dia. HDPE Class 12	m	50.00		
	403.00	.01 Supply, delivery, installation, testing and commissioning of new isolating valves (existing pipeline and valve size to be verified on site before ordering of material).				
		.01 22 mm dia	No	4.00		
		.01 50 mm dia	No	2.00		
		.02 80 mm	No	2.00		
		.03 110 mm dia.	No	1.00		
	404.00	.02 Supply, delivery, installation, testing and commissioning new non-return valves				
		.01 50 mm	No	1.00		
		.02 80 mm dia	No	1.00		
		.03 110 mm dia.	No	1.00		
	405.00	03 Supply, delivery, installation, testing and commissioning new water meters				
		.01 22 mm dia	No	4.00		
		.02 50 mm dia	No	2.00		
		.03 80 mm dia.	No	1.00		
		.04 110 mm dia	No	1.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS
CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	406.00	Servicing of Valves				
	406.01	01 Isolating valves (existing pipeline and valve size to be verified on site before ordering of material).				
		.01 50 mm dia	No	3.00		
		.02 80 mm dia	No	3.00		
		.03 Ø 110mm to Ø 250mm Class 16 Isolating Valve	No	2.00		
	406.02	.02 Non-return valves				
		.01 80 mm dia.	No	3.00		
		.02 110 mm dia	No	2.00		
		Service Motor Control Centres	No	3.00		
	407.00	WATER DISTRIBUTION NETWORKS				
		Water distribution pipelines				
	407.01	Repair of existing pipelines:				
		01 Distribution pipes not exceeding deep	m	30.00		
		.02 House connections not exceeding 800mm deep	m	10.00		
		.02 Provision of materials for repair	m	10.00		
	407.02	uPVC class 12 pressure pipes to SANS 966 with integral "LYNG" mechanical rubber ring joints:				
		.01 75 mm dia.	m	25.00		
		.02 110 mm dia.	m	13.00		
		03 160 mm dia.	m	9.00		
	407.03	Galvanised mild steel (GMS) medium duty duality pipes to SASS 62 with flanged couplings. Normalised pipes:				
		01 50 mm dia.	m	25.00		
		.02 80 mm dia.	m	15.00		
		.03 100 mm dia.	m	8.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS
CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	407.04	.04 150 mm dia. HDPE - 100 Class 10 pressure pipes, ISO:	m	3.00		
		.01 50 mm dia	m	35.00		
		.02 80 mm dia	m	15.00		
	407.05	Saddles with standard drilling and 25 mm SSP tapping for connections to supply lines:				
		.01 110 mm dia.	No	5.00		
		.02 160 mm dia.	No	2.00		
	407.06	Standard bends of all degrees and all types completely fitted in pipes of all types with Inside diameters of				
		.01 between 39 mm and 55 mm	No	3.00		
		.02 between 55 mm and 76 mm	No	2.00		
		.03 between 76 mm and 99 mm	No	1.00		
		.04 between 99 mm and 130 mm	No	2.00		
		.05 between 130 mm and 180 mm	No	2.00		
	407.07	Standard equal tees, reducing tees (largest connection pipe determine payment classification) and cross peaces of all types completely fitted in pipes of all types with inside diameters of:				
		.01 between 39 mm and 55 mm	No	3.00		
		.02 between 55 mm and 76 mm	No	2.00		
		.03 between 76 mm and 99 mm	No	1.00		
		.04 between 99 mm and 130 mm	No	1.00		
	407.08	Standard reducers (largest connection pipe determine payment classification)of all types completely fitted in pipes of all types with inside diameters of:				
		.01 between 55 mm and 76 mm	No	2.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS
CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.02 between 76 mm and 99 mm	No	1.00		
		03 between 99 mm and 130 mm	No	1.00		
	407.09	Standard couplings, repair couplings, flange adapters and other adapters (to connect different types of pipes and fittings) of all types completely fitted in pipes of all types with inside diameters of:				
		.01 between 76 mm and 99 mm	No	2.00		
		08 02 between 99 mm and 130 mm	No	2.00		
		03 between 130 mm and 180 mm	No	1.00		
	407.10	Supply and Installation of Stainless Steel Cascade clamps for any types of pipes				
		.01 full clamps between 50 and 100mm dia pipes	No	1.00		
		02 full clamps between 110 and 150mm dia pipes	No	1.00		
	407.11	Cleaning of pipeline				
		.01 Scouring of pipeline	m	820.00		
		.02 Cleaning of manholes, chambers and other structures	No	32.00		
	407.12	Manholes				
		.01 Manholes and inspection chambers				
		New pre-cast concrete manhole up to 1.2m deep, including pre-cast cover and frame	No	1.00		
	407.13	Replacement of manhole covers, grid inlets, etc				
		.01 SANS 558 Type 8A - Medium duty class size 600 x 450mm rectangular manhole cover and frame, double sealed type	No	2.00		
		.02 SANS 558 Type 8B - Medium duty class size 600 x 600mm square manhole cover and frame, double sealed type.	No	2.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS
CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.03 SANS 558 Type 9A - Light duty class size 600 x 600mm square manhole cover and frame, single sealed type	No	2.00		
		.04 SANS 558 Type 9E - Light duty class size 900 x 600mm rectangular manhole cover and frame, single sealed type	No	2.00		
	408.00	WATER RESERVIORS:				
		.01 Sterilization of storage tanks	No	2.00		
		.02 Clean area around storage tanks (30m x 30 m) of vegetation and growth	No	3.00		
	409.00	WATER TREATMENT PLANT				
		.01 Full service of water treatment plant as per manufacturers specification, O&M manuals etc. Servicing of plant to be performed by specialist contractor	No	3.00		
		.02 Ensure continuous manual and automatic operation of plant and associated equipment	No	36.00		
	409.01	Compile and supply a complete set of operating and Maintenance Manuals for all installations specified				
		.01 Water treatment works	No	2.00		
	409.02	Decommisioning and removal, servicing, installation, testing and commusioning of raw water pumps filter pumps				
		.01 5.5 kw 3,5m3/h pressure pump	No	1.00		
		.02 Mono 7.5kw motor water purification pump	No	1.00		
		.04 Mono 5.5kw motor water purification pump	No	1.00		
		.05 1.1 kw fiter pumps	No	1.00		
		.06 2120aBB Filtration pumps	No	1.00		
		.07 flocculent dosing pump	No	1.00		
		.08 pH corection dosing pump	No	1.00		
		.09 De-sludging pump	No	1.00		
		.10 Product feed pump	No	2.00		
		.11 Sand filtration units inclusive of filter pumps, incl 923 x2107 mm round 400kPA fibre glass pressure vessels	No	2.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS

CIVIL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.12 Pressure pump 0.7 km motor 20-90l/sec fire pressure pump	No	6.00		
		.13 Existing water high lift pump 1.5Kw, 220V with max pressure of 1.8bar and 33,000l/h	1	1.00		
		.14 Water feed pump 1.5kW, 220V with max pressure of 1.8 bar and 33,000l/h	1	1.00		
		Service motor control centres	No	6.00		
		Replace a float level switch	No	8.00		
		Replace filtration media to 923 x 2107mm round 400kPA fibre glass pressure vessels as per manufacturers specification				
		.01 Climabrite sand	kg	2000.00		
		.02 Activated carbon media	kg	400.00		
		.03 Birm metal removal	kg	600.00		
		.04 Anthracite coal	kg	600.00		
		Supply of portable drinking water of port of Entry from commercial sources including transport				
		.01 Alexander Bay Port of Entry	kl	120.00		
		.02 Vioolsdrift Drift Port of Entry	kl	300.00		
		.03 Onseepkans Port of Entry	kl	400.00		
	Carried forward					

SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL WATER NETWORKS						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		TELEMETRY .01 Provide the sum of R 100, 000 for the repair and/or servicing and commissioning of the existing Tele-Flex Telemetry equipment .02 Attendance and profit	Pc Sum %	1.00 R 100,000.00	R 100,000.00	R 100,000.00
		WATER PURIFICATION PLANT Service and repair Endress & Hauser electromagnetic flowmeter as per specification from supplier Replace electronic shut off float valves with 5 m floater including liquid level controller	No No	3.00 2.00		
		Servicing, Reconditioning and filter replacement - domestic water filter .01 Domestic 5-stage reverse-osmosis water purification system (including new filter)	No	6.00		
		Supply and installation of new domestic water purification system .01 Domestic 5-stage reverse-osmosis water purification system (including filter).	No	3.00		
		Procurement and delivery of bottled water (500 ml) .01 Supply and deliver sealed, commercially branded bottled drinking water in 500 ml containers for site personnel use.	No	500.00		
	SCHEDULE NO 2.4: INSTALLATION C4: BULK WATER SUPPLY SYSTEMS AND EXTERNAL TOTAL WATER NETWORKS - CARRIED TO SUMMARY:					

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 2.5: INSTALLATION C5: WASTEWATER AND SEWER NETWORKS

CIVIL REPAIR
WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		SEWER NETWORK				
		.01 Repair/Replace existing pipeline (pipe material measured below)				
		.01 Sewarge pipes	m	32.00		
		Excavation				
		01. Hard rock excavation	m ²	24.00		
		Provision of materials for repair:				
		.01 Upvc 400Kpa structured wwall pipe to SABS type I with smooth inner and outer wall				
		.01 110 mm dia Upvc pipe and sockest	m	50.00		
		.02 160mm dia	m	5.00		
		.04 PVC-U Solid wall sewer fittings to SANS 791 specifications				
		.05 110mm dia single sockets	No	5.00		
		06 160mm dia single sockets	No	5.00		
		07 110mm dia plain 45° bends	No	5.00		
		.08 110mm dia plain 90° bends	No	5.00		
		.09 110mm dia plain junctions	No	5.00		
		10 160 mm dia plain junctions	No	5.00		
		.11 110 mm dia fabricated long radius bends	No	5.00		
		.12 160 mm dia fabricated long radius bends	No	5.00		
	Carried forward					

SCHEDULE NO 2.5: INSTALLATION C5: WASTEWATER AND SEWER NETWORKS

CIVIL REPAIR
WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	703.07	MATURATION PONDS AND REED BED				
		.01 Remove vegetation from pond walls	m ²	800.00		
		.02 Remove vegetation from reed bed walls and undesirable vegetation between reeds on the outskirts of the reed bed	m ²	600.00		
		.03 Remove sand which was washed in by storm water from the reed bed	m ³	100.00		
		Cleaning eyes:				
		.01 110 mmm dia inline cleaning eye costructed complete with ABC CI cover and frame and conctrcte encasement	No	12.00		
		Removal, supply, delivery and replacement of drying bed filter media	m ³	50.00		
		Replacement of manhole covers, grid inlets and the;				
		.01 SANS 558 Type 8B - Medium duty class size 600 x 600mm square manhole cover and frame, double sealed type.	No	2.00		
		.02 SANS 558 Type 8A - Medium duty class size 600 x 450mm rectangular manhole cover and frame, double sealed type	No	2.00		
		.03 SANS 558 Type 4 - Cover size 550 mm dia	No	2.00		
		Repair to damaged manholes including channels and benching :				
		.01 Existing manholes	No	2.00		
		SHREDDER PUMP SYSTEM				
		.01 Allow the sum of R 450 000 for the replacement and/or service of shredder pump system including commisioning and operator training	No	1.00	R 450,000.00	R 450,000.00
		.02 Attendance and profit	%	R 450,000.00		
		SEPTIC TANKS				
		Cleaning out, inspect and repair septic tanks				
		.01 Cleaning out of septic tanks and dispose of contents off-site	No	12.00		
	Carried forward					

SCHEDULE NO 2.5: INSTALLATION C5: WASTEWATER AND SEWER NETWORKS

CIVIL REPAIR
WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		French drains according to SANS 10400 - PP10				
		.01 Soak test as per DPW standard detail	No	6.00		
		.03 Perforated 110 mm PVC pipe	m	10.00		
		.04 Geo fabric, knittex 80 or similar approved. Colour to be approved by engineer	m ²	50.00		
		.05 Stone 19mm for soak away	m ³	12.00		
		HUBER ROTMAT MICRO STRAINER (Ro9 300x6)				
		All works to be executed by manufacturers approved service provider to manufacturers specification				
		Mechanical screen: Supply and Fit				
		.01 Strip brush	No	5.00		
		.02 Motor Gearbox complete	No	1.00		
		.03 Sealing strip	m	1.10		
		.04 Basket	No	1.00		
		.05 Weir bar strip	No	5.00		
		Grit Classifier Rosf3E				
		.01 Electrical drive motor BF40 1.1kW 11.5 u400/50 910 Nm incl sealing	No	1.00		
		.02 Wear ring grit 105/60x98	No	1.00		
		.03 Pin 80/59x97 to grit classifier	No	1.00		
		PITCHING, STONEMWORK AND PROTECTION AGAINST EROSION				
	703.08	Stone Pitching				
		.01 Grouted stone pitching	m ³	5.00		
		.02 Concrete edge beams (15MPa concrete)	m ³	5.00		
		Carried forward				

SCHEDULE NO 2.5: INSTALLATION C5: WASTEWATER AND SEWER NETWORKS						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		LANDSCAPING AND PLANTING PLANTS AGAINST EROSION				
		Trimming				
		.01 Hand Trimming	m ²	2.00		
		Preparing the areas for grassing				
		.01 Topsoiling				
		(ii) Topsoil obtained from other sources by the contractor (including all haul)	m ³	1.00		
		SEPTIC TANKS				
		Cleaning out, inspect and repair septic tanks:				
		.01 Cleaning out septic tanks and dispose of contents off-site	No	12.00		
		.02 Excavation in pickable soil for the placing of new septic tanks	m ³	24.00		
		.03 Supply and install prefabricated septic tank complete (5400 litre capacity - Calcamite or similar approved type)	No	1.00		
		Removal and disposal of septic tank contents as well as demolition, backfill and compaction of existing tanks	No	1.00		
		Compile and supply a complete set of operating and Maintenance Manuals for all installations specified				
		.01 Wastewater treatment works	No	1.00		
		.01 Manhole and inspection chambers				
		.01 New pre-case concrete manhole up ri 1.2m deep, including pre-cast cover and frame	number	1.00		
		New clean water pump CPM158, head max 30m, 2850 r/min	number	1.00		
	TOTAL	SCHEDULE NO 2.5: INSTALLATION C5: WASTEWATER AND SEWER NETWORKS - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE

						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	640,01	Pavement layers and asphalt surface repair				
		.01 Excavating and removing existing bituminous material	m ³	12.00		
		01 Material to be disposed of with the average depth of excavation up to 60mm				
		02 Excavating and spoiling material from an existing pavement and/or the underlying fill:	m ³	12.00		
		.01 Non-cemented material				
		.02 Asphalt surfacing (continuously graded medium, 60/70 penetration grade asphalt)	m ²	7.00		
		03 Surface patching of surfaced roads				
		01 Trimming the edges and edge breaks of the existing surfacing	m	250.00		
		04 Pothole repair using cold mix asphalt surfacing from the following sources				
		01 Commercial sources (30mm thick)	m ²	220.00		
		.05 Repair of segmented paving				
		01 Remove and discard damaged concrete block paving (80 mm interlock)	m ²	120.00		
		06 Excavation for repair of segmented paving (max. 300 mm depth)				
		01 Stockpile and re-use paving blocks	m ³	100.00		
		.01 Cast insitu concrete and formwork in edge beams, intermediate beams and kerbing:				
		01 Class 30 concrete	m ³	30.00		
	Carried forward					

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.02 Concrete block paving:				
		.01 Class, type and thickness similar to existing pavement for areas carrying mainly vehicular traffic (80 mm interlocking paving blocks (grey) on 20 mm bedding sand)	m ²	120.00		
		02 Replacement of jointing sand	m ²	1,000.00		
		Surface repairs of concrete pavements				
		.01 Preparation and sealing or resealing of old joints and cracks in existing concrete pavements				
		01 Expansion joints > 5 mm wide	m	80.00		
		.02 Construction Joints and weakened plane joints > 5 mm wide	m	25.00		
		.03 Cracks > 5 mm	m	12.00		
		02 Patching of concrete				
		.01 Sealed transverse joints				
		.01 Joint filler (closed-cell polythylene)	m	110.00		
		.02 Silicone sealant (grey)	m	60.00		
		.02 Steel reinforcement in concrete pavement				
		.01 Welded steel fabric (ref 245)	kg	50.00		
		.0125 MPa concrete of thickness 125 mm up to 150 mm	m ²	5.00		
		.03 Y12 high tensile steel reinforcing bars in concrete	t	1.00		
	700.00	.04 Excavation and disposal of concrete pavement				
	700.01	.01 Reinforced concrete (150 mm thickness)	m ³	10.00		
		Repair of kerbing:				
		.01 Patching of kerbs	m	10.00		
		02 Replacing of kerbs				
		.01 Barrier kerbs similar to existing undamaged barrier kerbs	m	50.00		
		.02 Semi-mountable kerbs (SANS Fig. 7)	m	160.00		
		.03 Removal of kerbs	m	250.00		
		Carried forward				

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		Breaking up and removing concrete edge beams, intermediate beams, etc.				
		.01 Concrete walkways	m ³	12.00		
		.02 Concrete edge beams and intermediate beams	m ³	14.00		
		Erection and repair of road traffic signs and traffic control devices.				
		.01 Erection or reinstatement of road sign boards				
		.01 Area not exceeding 2 m2	m ²	2.00		
		.02 Area exceeding 2 m2	m ²	5.00		
		.03 Area exceeding 2 m2	m ²	5.00		
		.04 Area exceeding 2 m2	m ²	5.00		
		Port of Entry Signage				
		.01 Replace Port of Entry signage with 5-year print vinyl and 5-year clear laminate vinyl 3000x2000mm secured on a 50x50x3mm square tubing frame (3 name boards)	PC Sum	1.00	R32,000.00	R 32,000.00
		.02 Attendance and profit on item .01 above	%	R 32,000.00		
		02 Road sign supports (overhead road sign structures excluded)				
		.01 Steel tubing of 76 mm diameter and 3 mm wall thickness	m	10.00		
	700.02	.03 Excavation and backfilling for road sign supports	m ³	5.00		
		.04 Extra over item 700.04.03 for cement treated soil backfill	m ³	6.00		
		.05 Hazard plates (600 x 150 mm)	No	10.00		
		.08 Repair of road sign faces	m ²	10.00		
		ROAD MARKINGS				
	700.03	01. Road marking paint:				
		Retro-reflective road-marking paint				
		.01 Longitudinal lines:				
		.01 100 mm to 150mm wide broken or unbroken lines, white, yellow or red	m	3,000.00		
		Carried forward				

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.02 Transverse lines and other markings				
		.01 Lettering and symbols, white or yellow markings	m ²	450.00		
		.02 Transverse lines, painted island and arrestor bed markings (any colour)	m ²	900.00		
		STORMWATER DRAINAGE				
		Cleaning of prefabricated culverts				
		.01 Cleaning of prefabricated culvert and inlet and outlet structures (average depth of material removed is more than 100 mm)				
		01 Prefabricated concrete pipes and portal culverts with maximum cross sectional dimension of:				
		01 Up to and including 500 mm	m	200.00		
		Cleaning of concrete drainage channels				
		.01 Concrete drainage channels and side drains	m	100.00		
		Chemical control of vegetation:				
		.01 300 mm wide strip	km	10.00		
		.02 Area covered by interlocking blocks	m ²	7,000.00		
		Concrete construction and repair				
		.01 Excavation:				
		.01 Soft material	m ³	146.00		
	700.05	.02 Cast in situ concrete and formwork In stormwater structures				
		.01 Class 25 concrete	m ³	3.00		
		.03 Backfill below channels	m ³	2.00		
		.04 Steel reinforcement				
		01 Welded steel mesh ref 245	m ²	10.00		
		Carried forward				

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		.05 Replacement of manhole covers, grid inlets, etc				
		01 SANS 558 Type 4 - covers, grids, etc				
		(i) Maximum dimension up to and including 300 mm	No	8.00		
		(ii) Maximum dimension 300 mm to 600 mm	No	8.00		
		02 SANS 558 Type 4 - frames only for covers, grid, etc				
		(i) Maximum dimension up to and including 300 mm	No	8.00		
		ANCILLARY ITEMS				
		.01 Flat-topped solid rubber speed bumps installed complete	No	5.00		
		02 Flat-topped solid stainless steel speed bumps installed complete	No	4.00		
		Inlet, Outlet, transition and similar structures (measured by components)				
		.01 Concrete class 30MPa - Stormwater channels	m3	10.00		
		.02 Finishing top surfaces of concrete smooth with a wood float	m ²	50.00		
		SEGMENTED PAVING				
	703.05	Concrete interlocking block paving complete including amongst others sand as specified				
		.01 Type S-A. 80mm thick, Black in colour				
		01. Class 25	m ²	10.00		
		02. Class 35	m ²	10.00		
		02. Type S-A, 60mm thick, Black in colour				
		01. Class 25	m ²	5.00		
		02. Class 35	m ²	5.00		
		.05 Pre-cast concrete edge restraint and intermediate beams 30MPa	m ²	5.00		
		Carried forward				

SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE						CIVIL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		Provision of approved herbicide and ant poison.				
		01 (a) Provision of materials	m2	850.00	R 40.00	R 34,000.00
		02. (b) Contractor's charges and profit added to the prime cost sum	%	34,000.00		
		02. Providing testing equipment:				
		(a) Rolling straight-edge	No	1.00		
		STORM WATER DRAINAGE				
		1 STORMWATER CULVERTS				
		01. Supply and lay interlocking concrete pipe culverts on class C bedding (class 100D)				
		(a) 450mm diameter	m	5.00		
		(b) 600mm diameter	m	5.00		
	TOTAL	SCHEDULE NO 2.6: INSTALLATION C6: ROADS AND STORM WATER DRAINAGE - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

NB TENDERERS MUST COMPLETE THE SCHEDULE OF QUANTITIES IN BLACK INK

SUMMARY OF SCHEDULE OF QUANTITIES: ELECTRICAL REPAIR WORK

ELECTRICAL REPAIR WORK

SCHEDULE NO 3.1: INSTALATION E1: BUILDING ELECTRICAL REPAIR WORK	
SCHEDULE NO 3.2: INSTALATION E2: STANDBY POWER RELATED CORRECTIVE WORK	
SCHEDULE NO 3.3: INSTALATION E3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK	

TOTAL OF SCHEDULE OF QUANTITIES - MECHANICAL REPAIR WORK	
CARRIED TO CALCULATION OF TENDER SUM	

SIGNED ON BEHALF OF TENDERER:

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	400.0	DISTRIBUTION BOARDS				
	400.01	Service distribution board				
		.01 Flush DB (+/- 500x 600mm)	No	3.00		
		.02 Flush mounted DB (+/- 1000 x 800mm)	No	3.00		
		.03 Surface mounted DB(+/- 400 x 550mm)	No	2.00		
		.04 Surface mounted DB(+/- 400 x 300mm)	No	6.00		
		.05 Flush mounted DB(+/- 360 x 380mm)	No	4.00		
		.06 Flush mounted DB (+/- 600 x 650mm)	No	4.00		
		.07 Flush mounted DB (+/- 300 x 300mm)	No	4.00		
		.08 Flush mounted DB (+/- 300 x 500mm)	No	2.00		
		.09 Flush mounted DB (+/- 600 x 600mm)	No	4.00		
		.10 Domestic single phase(+/- 300 x 450mm)	No	13.00		
		.11 Surface mounted DB(+/- 330 x 500mm)	No	2.00		
		.12 Flush mounted DB (+/- 330 x 500mm)	No	1.00		
		.13 Flush mounted DB (+/- 400 x 400mm)	No	1.00		
		.14 Flush mounted DB (+/- 400 x 500mm)	No	1.00		
		.15 Floorstanding D.B Alexandra Bay	No	1.00		
		.16 Floorstanding D.B. Vioolsdrift	No	1.00		
		.17 Floorstanding D.B. Onseepkans	No	1.00		
		Electrical Tests				
		.01 Insulation resistance	site	3.00		
		.02 Phase Voltage	site	3.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK
**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	400.02	.03 Current per Phase	site	3.00		
		.04 Illumination levels in lux	site	3.00		
	400.02	Supply and installation of circuit breakers (SABS approved)				
		.01 10-40A, 6kA single pole	No	6.00		
		.02 40-50A, 6kA single pole	No	2.00		
		.03 10-40A, 6kA double pole	No	1.00		
		.04 10-40A, 6kA tripple pole	No	2.00		
		.05 40-80A, 6kA tripple pole	No	1.00		
		.06 80-100A, 6kA tripple pole	No	1.00		
		.07 80-100A 15kA tripple pole	No	1.00		
		.08 100-160A 15kA tripple pole	No	1.00		
	400.03	Supply and installation of isolators (SABS approved)				
		.01 20-40A, 6kA double pole	No	2.00		
		.02 60A,6kA double pole	No	1.00		
		.03 60A,6kA tripple pole	No	1.00		
		.03 80A,6kA tripple pole	No	1.00		
	400.04	Supply and install contactors				
		.01 30A, 3 pole	No	1.00		
	400.05	Supply and install switching timers				
		01 QAT-R-Clip in timer	No	2.00		
	400.06	Supply and install earth leakage units (SABS approved)				
		01 60A, 6kA double pole	No	3.00		
	400.07	Supply and install surge arrestors				
		01 1 Pole and Neutral 27SV 5kA with Indication with indication	No	36.00		
	400.08	.02 3 Pole and Neutral 275V 5kA with Indication	No	2.00		
	401.00	LOW VOLTAGE CABLE INSTALLATIONS				
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK

ELECTRICAL
REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	401.01	Replace cabling				
		.01 16mm ² x 3-core PVC/SWA/PVC Cu	m	10.00		
		.02 10mm ² x 3-core PVC/SWA/PVC Cu	m	10.00		
		.03 6 mm ² x 3-core PVC/SWA/PVC Cu	m	20.00		
	401.02	Termination of low voltage cable				
		.01 16 mm ² x 3-core PVC/SWA/PVC Cu	No	2.00		
		.02 10mm ² x 3-core PVC/SWA/PVC Cu	No	4.00		
		.03 6 mm ² x 3-core PVC/SWA/PVC Cu	No	4.00		
	401.03	Jointing of cables				
		.01 10 mm ² x 3-core PVC/SWAJPVC Cu	No	2.00		
		.02 6 mm ² x 3-core PVC/SWAJPVC Cu	No	2.00		
		.03 16 mm ² x 3-core PVC/SWAJPVC Cu	No	2.00		
	401.4	Supply and install earth continuity conductor:				
		.01 10 mm ² BCEW	m	10.00		
		.02 6 mm ² BCEW	m	10.00		
		.03 4 mm ² BCEW	m	20.00		
	401.05	Terminate earth continuity conductor:				
		.01 10 mm ² BCEW	No	2.00		
		.02 6 mm ² - BCEW	No	4.00		
		.03 4 mm ² - BCEW	No	4.00		
	402.00	WIRING				
	402.01	Replace wiring:				
		.01 2,5 mm ² PVC insulated	metre	180.00		
		.02 4 mm ² PVC insulated	metre	80.00		
		.03 6 mm ² PVC insulated	metre	50.00		
		.04 2,5 mm ² BCEW	metre	50.00		
		.05 4 mm ² BCEW	metre	50.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK
**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.06 10 mm ² PVC insulated	metre	50.00		
		.07 6mm ² BCEW	metre	50.00		
	403.00	LIGHTING INSTALLATION				
	403.01	Re-lamp luminaire				
		.01 58W Fluorescentby equivalent SABS approved LED tubes	No	20.00		
		.02 36W Fluorescent by equivalent SABS approved LED tubes	No	36.00		
		.03 250W MV Lamp	No	10.00		
		.04 250W HPS Lamp	No	10.00		
		.05 70W HPS Lamp	No	10.00		
		.06 PL9W by equivalent SABS approved LED lamp	No	10.00		
		.07 Energy saver 16W/E27 by equivalent SABS approved LED lamp	No	10.00		
		.08 2D16W by equivalent SABS approved LED lamp	No	10.00		
		.09 100W GLS Lamp	No	10.00		
		.10 100W LED Floodlight Lamp	No	10.00		
		.12 Fluorescent Circular 40W Coolwhite	No	100.00		
		.13 Double 4ft Fluorescent	No	80.00		
		.14 Bulkhead - Round Outdoor IP65 - 12W	No	50.00		
		.15 Type J (Beka Series 30-Black, 31218)	No	120.00		
		.16 Type C (Beka Series 70-White, 71126)	No	300.00		
		.17 Traplight	No	50.00		
		.18 Type A (Beka Series 40-White, 41126)	No	100.00		
		.19 Type B (Beka Series 40-White, 42126)	No	100.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK

ELECTRICAL
REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	403.02	,20 .Single 4ft Fluorescent .21 Type P (Beka Roughguard 2x36W/ PV/ Tps Complete) ,22 .Triple 36W 2ft Fluorescent Service luminaire .01 Double 36W 2ft Fluorescent .02 Fluorescent Circular 40W Coolwhite .03 Double 4ft Fluorescent .04 Bulkhead - Round Outdoor IP65 - 12W .05 Type J (Beka Series 30-Black, 31218) .06 Type C (Beka Series 70-White, 71126) .07 Traplight .08 Type A (Beka Series 40-White, 41126) .09 Type B (Beka Series 40-White, 42126) .10 Single 4ft Fluorescent .11 Type P (Beka Roughguard 2x36W/ PV/ Tps Complete) .12 Triple 36W 2ft Fluorescent	No	33.00		
	403.03	Replace luminaire with equivalent SABS approved LED luminaire .01 Double 36W 2ft Fluorescent .02 Fluorescent Circular 40W Coolwhite 03 Double 4ft Fluorescent .04 Bulkhead - Round Outdoor IP65 - 12W .05 Type J (Beka Series 30-Black, 31218) .06 Type C (Beka Series 70-White, 71126) .07 Traplight	No	12.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK

**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.08 Type A (Beka Series 40-White, 41126)	No	21.00		
		.09 Type B (Beka Series 40-White, 42126)	No	24.00		
		.10 Single 4ft Fluorescent	No	8.00		
		.11 Type P (Beka Roughguard 2x36W/ PV/ Tps Complete)	No	4.00		
		.12 Triple 36W 2ft Fluorescent	No	12.00		
	403.04	Replace luminaire diffuser or lens				
		.01 Type B	No	18.00		
		.02 Type P	No	8.00		
		.03 Type R	No	4.00		
		.04 Type U	No	10.00		
		.05 Type W	No	14.00		
		.06 Type X	No	12.00		
	403.05	Supply and installation of internal luminaire components				
		.01 Choke for 36W Fluorescent	No	24.00		
		.02 Choke for 58W Fluorescent	No	12.00		
		.03 Fluorescent starter	No	38.00		
	403.06	Ceiling replacement:				
		.01 Luminaire removal and reinstallation	No	8.00		
	403.07	Switches replacement:				
		.01 Service light switch (1 & 2 lever, dimmer and watertight)	No	900.00		
		.02 Service Daylight switches (Photo cell)	No	6.00		
	403.08	Replace light switch				
		.01 16A, one lever, one way	No	8.00		
		.02 16A, two lever, one way	No	5.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK

ELECTRICAL
REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.03 16A, three lever, one way	No	3.00		
		.04 16A, one lever, two way	No	2.00		
		.05 16A water tight, robust	No	3.00		
	403.09	Replace Photo-electric switch				
		.01 16A unit with bracket and mounted in dummy bulkhead fitting	No	6.00		
	403.10	Replace Lampholder				
		Replace lampholder (Ceramic)	No	12.00		
	404.00	POWER OUTLETS				
	404.01	Service socket outlet				
		.01 16A, single SSO	No	22.00		
		.02 16A, double SSO	No	12.00		
		.03 16A, dedicated SSO	No	8.00		
	404.02	Replace socket				
		.01 16A, single SSO	No	10.00		
		.02 16A, double SSO	No	6.00		
		.03 16A, single SSO powerskirting mounted	No	12.00		
		.04 16A, dedicated SSO 'powerskirting mounted	No	4.00		
		.05 16A, single, dedicated SSO and Data points covers 'powerskirting mounted	No	16.00		
		.06 6A, unswitched socket outlet usa	No	6.00		
	404.03	Service isolator				
		.01 60 A, 2 pole	No	15.00		
		.02 30A, 2 pole	No	8.00		
	404.04	Replace isolators				
		.01 30A, 2 pole	No	3.00		
		.02 30A 2 pole with cord grip	No	4.00		
		.03 30A 2 pole in York box S15	No	3.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK

**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		.04 60A 2pole	No	4.00		
		Service socket outlet (single or double)	No	1,500.00		
		Service dedicated and UPS socket outlets (red and blue)	No	354.00		
		Service Isolators (air-cons, geysers and stoves)	No	269.00		
		Service and check photocell	No	24.00		
		Geyser components				
		,01 Domestic geyser element	No	12.00		
		,02 Geyser thermostat	No	12.00		
	404.05	Replace plug tops:				
		.01 3-pin 16A	No	8.00		
		.02 3-pin square 13A	No	6.00		
	405.00	FIXED APPLIANCE AND COMPONENTS				
	405.02	Replace domestic stove components:				
		.01 150 - 160 dia solid plate	No	14.00		
		.02 170 - 190 dia solid plate	No	12.00		
		.03 200 - 220 dia solid plate	No	3.00		
		.04 Five I six heat switch	No	12.00		
		.05 Oven bottom element	No	4.00		
		.06 Oven top element	No	4.00		
		Supply, install and remove existing domestic sunken stainless steel two plate stove similar to existing or as approved	No	10.00		
	405.03	Replace connection from isolator to fixed appliance, with flexible copex (sprague) conduit and conductors, e.g. stove or geyser				
		.01 Stove: 2 x 6 mm' PVC and 2,5 mm- BCEW conductors.	m	30.00		
		.02 Geyser: 2 x 4 mm' PVC and 2,5 mm' BCEW conductors.	m	20.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK
**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	406.00	WIRE WAYS CONDUITS AND ACCESSORIES				
	406.01	Replace conduit:				
		.01 20mm dia Galv. Steel	m	10.00		
		.02 25mm dia Galv. Steel	m	10.00		
		.03 32mm dia Galv. Steel	m	8.00		
	406.02	Supply and install outlet (draw) boxes				
		.01 100 x 50 Galv. Steel	No	3.00		
		.02 100 x 100 Galv. Steel	No	3.00		
		.03 50 x 100 mm white enamel extension box	No	6.00		
		.04 100 x 100 mm white enamel extension box	No	8.00		
		.05 Circular 20mm	No	6.00		
	406.03	Supply and install draw box cover plates(white enamel) to 'fit:				
		.01 To fit 100 x 50 box	No	3.00		
		.02 To fit 100 x 100 box	No	3.00		
		3.00 Circular galvanised box	No	6.00		
	406.04	Replace power skirting				
		.01 2-tier powder-coated galvanised steel	m	25.00		
	406.05	Replace wiring channel:				
		.01 OL 2000, 41.3 x 41.3 mm	m	18.00		
		.02 OL 9000, 127 x 76 mm	m	10.00		
		.03 White pvc 100 x 76 mm	m	20.00		
		.04 White pvc 40 x 40 mm	m	20.00		
	406.06	Supply and install Pratley boxes				
		.01 83 mm 0 - double entry	No	1.00		
		.02 127 mm 0 - 3 way	No	1.00		
		Supply and install 12V, 40A per hour rechargeable sealed Lead Acid batteries incl 7A charge	No	2.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK
**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	406.07	Supply and install 4 plate stove with oven and warm drawer similar or equal to existing	No	1.00		
		INSECT ELECTROCUTORS				
		Supply and install insect electrocutors (outdoor) 620mm x 130mm x 48mm with 2 x 20W tubes including heavy duty galvanised steel bracket mounted to existing pole or wall (similar approved)	No	5.00		
	407.00	EARTHING AND BONDING				
	407.01	Provide earthing and bonding in all Residential houses, ablution rooms, laundries and kitchens	Sum	1.00		
	408.00	LIGHTNING PROTECTION				
	408.01	Supply and install earth electrodes:				
		.01 16 mm dia 1.2 m long Cu rod and clamp	No	14.00		
	408.02	Provide cadweld joint on 70 mm' cable	No	14.00		
	408.03	Earth building roof structure	No	14.00		
	408.04	Testing of lightning earthing per building by a specialist contractor	No	68.00		
	408.05	Provide Certificate of Compliance by an accredited specialist contractor	Sum	1.00		
		BOOM GATES				
		.01 Service, repair, test and commissioning electric boom gates	No	4.00		
	409.00	.02 Replace boom gate at Alexander Bay LPoE with similar	No	2.00		
		FANS				
		Replace 102m3/h wall mounted fans complete with aluminium Louvre as existing	No	12.00		
		Replace 175m3/h wall mounted fans with Louvre as existing, complete with temperature control unit as existing	No	5.00		
		Replace 600mm x 400mm wall mounted aluminium powder coated UV resistant gravity louvre plugged to brick work as existing	No	2.00		
		Supply and replace 4200m3/h wall mounted fan complete with "Stop/start" unit as existing	No	2.00		
	TOTAL	SCHEDULE OF QUANTITIES No 3.1: INSTALLATION E1: BUILDING ELECTRICAL REPAIR WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE OF QUANTITIES No 3.2 INSTALLATION E2: STANDBY POWER RELATED CORRECTIVE WORK**

						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	800.00	GENERATOR				
	800.01	Replace starter battery	No	5.00		
	800.02	Supply and install padlocks	No	5.00		
	800.03	Add 12/24V DC Emergency light	No	3.00		
	800.04	First Aid kit	No	4.00		
	800.05	Service fuel modular filtration system with automatic water dump	No	4.00		
	800.06	Service fuel water separator with automatic water dump	No	1.00		
	800.06	Clean generator plant room	No	7.00		
	800.07	Provision of new Gen-sets in all Land Ports of Entry				
	800.07.1	100 kVA Gen-set in Alexander Bay LPOE	No	1.00		
	800.07.2	100kVA, 2 x 25kVA, 15kVA, 10 kVA Gen-sets in Vioolsdrift LPOE	Sum	1.00		
	800.07.3	100 kVA Gen-sets in Onseepkans LPOE	No	1.00		
	800.08	Provision of new Critical Generator Spares in all Land Ports of Entry				
	800.08.1	Alexander Bay LPOE				
	800.08.1.1	Deep Sea Control unit	No	1.00		
	800.08.1.2	Diesel engine	No	1.00		
	800.08.1.3	Generator switch	No	1.00		
	800.08.1.4	Fuel/Water separator	No	1.00		
	800.08.1.5	Diesel meter/gauge	No	1.00		
	800.08.1.6	Generator change over system	No	1.00		
	800.08.2	Vioolsdrift LPOE				
	Carried forward					

SCHEDULE OF QUANTITIES No 3.2 INSTALLATION E2: STANDBY POWER RELATED CORRECTIVE WORK

**ELECTRICAL
REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
HB 11.03.01	800.08.2.1	Deep Sea Control unit	No	1.00		
	800.08.2.2	Diesel engine	No	1.00		
	800.08.2.3	Generator switch	No	1.00		
	800.08.2.4	Fuel/Water separator	No	1.00		
	800.08.2.5	Diesel meter/gauge	No	1.00		
	800.08.2.6	Generator change over system	No	1.00		
	800.08.3	Onseepkans LPOE				
	800.08.3.1	Deep Sea Control unit	No	1.00		
	800.08.3.2	Diesel engine	No	1.00		
	800.08.3.3	Generator switch	No	1.00		
	800.08.3.4	Fuel/Water separator	No	1.00		
	800.08.3.5	Diesel meter/gauge	No	1.00		
	800.08.3.6	Generator change over system	No	1.00		
		Supply and install water jacket heater	No	1.00		
		Compile and supply a complete set of operating and maintenance manuals				
		.01 Generators Vioolsdrift	No	1.00		
		.02 Generators Alexander Bay	No	1.00		
		.01 Generators Onseepkans	No	1.00		
		Replace 12V sealed lead acid batteries for standby power generator	No	4.00		
		Replacement of Donaldson breather units similar as existing	No	1.00		
		UPS SYSTEM				
		Service UPS cabinets				
HB 11.03.02		.01 Tower 1100 10kVA Unit	No	1.00		
		.02 QP5000 10kVA Unit	No	1.00		
		.03 Tower 3100 10kVA Unit	No	1.00		
		Execute dummy load test annually for 3 years	No	3.00		
	Carried forward					

SCHEDULE OF QUANTITES No 3.2 INSTALLATION E2: STANDBY POWER RELATED CORRECTIVE WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
HB 11.03.03		Replace UPS batteries				
		.01 Tower 1100 10kVA/7kW Unit 12V, 9Ah	No	60.00		
		.02 QP5000 10kVA Unit 12V, 7Ah	No	50.00		
		.03 Tower 3100 10kVA Unit 12V, 9Ah	No	60.00		
HB 11.03.03		.01 Replace UPS battery charger card	No	1.00		
HB 11.03.03		.02 Replace UPS control card	No	3.00		
HB 11.03.03		.03 Replace UPS power supply card	No	3.00		
HB 11.03.03		.04 Replace UPS 16- 32A fuses	No	5.00		
	TOTAL	SCHEDULE OF QUANTITES No 3.2 INSTALLATION E2: STANDBY POWER RELATED CORRECTIVE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK

						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	800.00	GENERAL REPAIR				
	800.01	Excavate in all materials for trenches, backfill, compact and dispose of surplus material.	m ³	24.00		
	800.02	Extra over item HE 09.06(a) above for excavating in hard materials	m ³	12.00		
	800.03	Extra over item HE 09,06(a) above for excavating by hand in hard materials	m ³	19.00		
	800.04	Supply and Install plastic warning tape	m	150.00		
	2203.00	AREA LIGHTING SYSTEM - REPAIR CONTROL AREA				
	2203.01	Re-lamp luminaire:				
		.02 250W HPS Floodlight	No	24.00		
	2203.02	Service Luminaire				
		.02 250W HPS Floodlight	No	33.00		
	2203.03	Replace Luminaire with SABS approved LED luminaire				
		.01 250W HPS Floodlight	No	4.00		
		.02 80 MV Post Top	No	9.00		
	2203.04	Service area light pole	No	11.00		
	2203.05	Replace area light pole				
		.01 9 Meter Wooden pole	No	6.00		
	2203.06	Replace pole mounted brackets				
		01 Floodlight mounting for double floodlights	No	6.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	2204.00	SECURITY FENCE LIGHTING SYSTEM				
	2204.01	Re-lamp luminaire:				
		.01 250W HPS Floodlight	No	6.00		
		.02 400W HPS Floodlight	No	20.00		
		.03 80 MV Post Top	No	9.00		
	2204.01	Service Luminaire				
		.01 250W HPS Floodlight	No	15.00		
		.02 400W HPS Floodlight	No	18.00		
		.03 80W MV Post Top	No	9.00		
	2203.04	Replace luminaire with SABS approved luminaire				
		.01 250W HPS Floodlight	No	3.00		
		.01 250W HPS streetlight	No	3.00		
		.02 400W HPS Floodlight	No	2.00		
	2204.02	Service Security light pole	No	21.00		
	2204.03	Replace Security light pole				
		01 7m Wooden pole Floodlight	No	2.00		
	2204.04	Junction boxes including pole mount brackets				
		.01 Junction boxes type U2	No	4.00		
		.02 Junction boxes IP65 (Enclosure) 1.5mm thick 3CR12 stainless steel, 250mm high x 175mm wide x 75 mm deep complete with cable entry gland plates, mounting plates and pole mounting kit.	No	3.00		
	2205.00	STREET LIGHTING HOUSES				
	2205.01	Re-lamp luminaire:				
		.01 125W MV Floodlights	No	17.00		
	2205.02	Service Luminaire				
		.01 125W MV Floodlights	No	8.00		
	2205.03	Service high mast area light posts	No	13.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	2205.04	Replace luminaire with SABS approved LED luminaire				
		.01 125W MV Floodlights	No	4.00		
	2205.05	Replace area light pole				
		.01 7 Meter Wooden Poles	No	2.00		
		.01 3.5 Meter Fibreglass pole	No	4.00		
	2206.00	DISTRIBUTION KIOSKS				
	2206.01	Service Distribution Kiosk	No	7.00		
	2206.02	Remove rust and paint kiosk	No	4.00		
	2206.03	Supply and install padlocks (Key Alike)	No	10.00		
	2206.04	Replace door hinges	No	2.00		
	2206.05	Supply and install door handles	No	2.00		
	2206.06	Replace distribution kiosk (6 way complete)	No	1.00		
	800.05	Supply and install uPVC sleeves:				
		.01 110 mm diameter	m	24.00		
		.02 75mm diameter	m	15.00		
	800.06	Supply and delivery of PVS/SWA/PVC Cu low-voltage cable:				
		.01 16mm ² , 4-core	m	50.00		
		.02 10mm ² , 4-core	m	40.00		
		.03 6mm ² , 4-core	m	90.00		
	800.07	Lay PVC/SWA/PVC Cu LV cable:				
		.01 16mm ² , 4-core	m	50.00		
		.02 10mm ² , 4-core	m	40.00		
		.03 6mm ² , 4-core	m	90.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	800.08	Termination of PVC/SWA/PVC Cu LV cable:				
		.01 16mm ² , 4-core	No	8.00		
		.02 10mm ² , 4-core	No	12.00		
		.03 6mm ² , 4-core	No	18.00		
	800.09	Jointing of low voltage cable:				
		.01 10mm ² , 4-core	No	4.00		
		.02 6mm ² , 4-core	No	4.00		
	800.10	Supply and delivery of bare copper earth conductor:				
		.01 6 mm ²	m	90.00		
		.02 4 mm ²	m	90.00		
	800.11	Installation of bare copper earth conductors:				
		.01 6 mm ²	m	80.00		
		.02 4 mm ²	m	90.00		
	800.12	Supply and installation of circuit breakers:				
		.01 10-20A, 5kA, single pole	No	15.00		
		.02 25-60A, 5kA, triple pole	No	5.00		
	800.13	Supply and installation of contactors:				
		01 30A, 3 pole	No	3.00		
	800.14	Supply and installation of Internal luminaire components:				
		.01 Ballast for 250 W HPS	No	18.00		
		.02 Igniter for 250 W HPS	No	8.00		
		.03 Capacitor for 250 W HPS	No	10.00		
		.04 GES porcelain lamp holder	No	9.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	800.15	Replace Luminaire diffuser				
		.01 250W HPS Floodlight	No	5.00		
		.02 250W HPSE streetlight	No	4.00		
		.03 Beka Ray Post Top diffuser	No	5.00		
	800.16	Supply and install photocell	No	6.00		
	800.17	Supply and Install QAT-R-clip-in timer	No	5.00		
	800.18	Supply and Install end connectors and insulating sleeves	No	8.00		
	800.19	Supply and install 3 way parallel entry cable boxes				
		.01 No 1	No	8.00		
		.02 No 2	No	5.00		
		.03 No 3	No	3.00		
	801.00	MEDIUM AND LOW VOLTAGE: SUBSTATION				
		.01 Service substation building	No	3.00		
		.02 Provide labels, notices and schematics	No	3.00		
		.03 Service 11kV switch gear				
		.01 Merlin Gerlin RMG	No	6.00		
		.04 Check protection relays (VIP 300)				
		.01 O/C&EF	No	6.00		
		.05 Service transformer	No	6.00		
		.06 Oil test	No	6.00		
		.07 On-site insulating oil reconditioning:				
		.01 Transformers	No	2.00		
		.08 Replace silica gel	No	2.00		
		09 Service LV distribution board	No	4.00		
	Carried forward					

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK

SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK						ELECTRICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
	802.00	MV OVERHEAD RETICULATION SYSTEM				
	802.01	Service overhead MV system	m	80.00		
	802.02	Replace insulator	No	8.00		
	802.03	Re-tensioning of overhead conductors	No	4.00		
	803.00	TOOLS AND SPARES				
		.01 MV Switchgear system				
		.01 MV fuses 20-50A 12kV 40kA	No	3.00		
		.02 Cut out fuse element 10A type K	No	3.00		
	804	Testing of Completed electrical installation				
	804.01	Testing of all internal & external completed electrical installations by accredited contractor	Sum	1.00		
	804.02	Issue Test reports & Electrical Certificates of Compliance as per current SANS regulations by accredited electrical contractor	Sum	1.00		
		Supply and installation of domestic electricity meter	No	10.00		
		Service, repair, test and commissioning of electric boom gates	No	4.00		
		TRAFFIC BARRIERS (boom arm constructed of aluminium tubing powder coated in white with red reflective tape and boom break away system)				
		Electrical semi automatic operated traffic barrier with stainless steel (6mm 3CR12) boom cabinet with infrared protection beam and 60W 220V AC 50Hz motor gear box				
		.01 4.5 meters	No	1.00		
		Service of mechanical tyre-spike boom barriers				
		.01 4.5 meters	No	2.00		
	TOTAL	SCHEDULE OF QUANTITIES No 3.3 INSTALLATION E.3: EXTERNAL LIGHTING, MEDIUM & LOW VOLTAGE RELATED CORRECTIVE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

NB TENDERERS MUST COMPLETE THE SCHEDULE OF QUANTITIES IN BLACK INK

SUMMARY OF SCHEDULE OF QUANTITIES: MECHANICAL REPAIR WORK

	MECHANICAL REPAIR WORK
SCHEDULE NO 4.1: INSTALATION M1: ALEXANDER BAY LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS	
SCHEDULE NO 4.2: INSTALATION M2: VIOOLSDRIFT LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS	
SCHEDULE NO 4.3: INSTALATION M3: ONSEEPKANS LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS	
TOTAL - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS	
SCHEDULE NO 4.4: INSTALATION M4: ALEXANDER BAY LPoE CONVENTIONAL FIRE FIGHTING EQUIPMENT	
SCHEDULE NO 4.5: INSTALATION M5: VIOOLSDRIFT LPoE CONVENTIONAL FIRE FIGHTING EQUIPMENT	
SCHEDULE NO 4.6: INSTALATION M6: ONSEEPKANS LPoE CONVENTIONAL FIRE FIGHTING EQUIPMENT	
TOTAL - CONVENTIONAL FIRE FIGHTING EQUIPMENT	

TOTAL OF SCHEDULE OF QUANTITIES - MECHANICAL REPAIR WORK CARRIED TO CALCULATION OF TENDER SUM	

SIGNED ON BEHALF OF TENDERER:

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**SCHEDULE NO 4.1: INSTALATION M1: ALEXANDER BAY LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:**

						MECHANICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	100.00 100.01	GENERAL REPAIR UNITS				
		.01 Highwall Ceiling Cassette Split Type Air-Conditioning Units				
		.01 Repair Outdoor Unit fins	No	11		
		.02 Check settings and operation of all pressure switches and reset if necessary	No	12		
		.03 Check settings and operation of thermostat	No	11		
		.04 Repair refrigerant pipe insulation	m	120		
		.05 De-rust, neutralize and touch up paint	No	14		
		.06 Replace filters	No	15		
		.07 Carry out a leak test on refrigeration piping and components inclusive of evaporator and condenser	No	11		
		.08 Supply and install condensate drain pipe (25mm diameter)	m	150		
		.09 Repair indoor air guide vents	No	12		
		.10 Replace compressor vibration mountings	No	13		
		.11 Supply and Install Wall Mounted AC Controllers	No	10		
		.12 Supply Wall Mounted AC Controllers batteries	No	44		
		.12 Re-gasing of regrigerant	No	22		
		.13 Check and repair settings and operation of all safety switches, i.e. LP&HP switches, oil pressure switches, etc.	No	22		
		.14 Check running current of fans and compressor, settings and operation of overloads	No	22		
		.15 Replace Outdoor vibration mountings	Set	11		
		.16 Clean Outdoor fan blades and check unbalance	No	12		
Carried forward						

SCHEDULE NO 4.1: INSTALATION M1: ALEXANDER BAY LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:

**MECHANICAL REPAIR
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
	100.02	REPLACE AC UNITS				
		.01 Highwall Split Type Air-Conditioning Units				
		.01 High-wall Split Inverter type air-conditioning unit (2.6kW total cooling), heat pump.	No	4		
		.02 12000 Btu high wall split Inverter unit, heat pump	No	5		
		.03 18000 Btu Cassette split Inverter unit, heat pump.	No	2		
		.04 26000 Btu high wall split Inverter unit, heat pump	No	2		
		.02 Air Curtain				
		.01 Supply and Install New 900mm Air Curtain complete with Remote Contoller	No	1		
		.02 Supply and Install New 1200mm Air Curtain complete with Remote Contoller	No	1		
		.03 Wall Mounted Extractor Fans				
		.01 Wall Mounted Extractor Fan with Steel Casing at 35l/s	No	2		
		.02 Wall Mounted Extractor Fan with Steel Casing at 60l/s	No	2		
		.02 Operating and maintenance manuals				
		.01 Compile & supply a complete set of operating and maintenance manuals	Set	1		
TOTAL - CARRIED TO REPAIR SUMMARY: SCHEDULE NO 4.1: INSTALATION M1:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS
REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND
INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**SCHEDULE NO 4.1: INSTALATION M1: VIOOLSDRIFT LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:**

						MECHANICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	200.00 200.01	GENERAL REPAIR UNITS				
		.01 Highwall Ceiling Cassette Split Type Air-Conditioning Units				
		.01 Repair Outdoor Unit fins	No	150		
		.02 Check settings and operation of all pressure switches and reset if necessary	No	150		
		.03 Check settings and operation of thermostat	No	150		
		.04 Repair refrigerant pipe insulation	m	450		
		.05 De-rust, neutralize and touch up paint	No	200		
		.06 Replace filters	No	200		
		.07 Carry out a leak test on refrigeration piping and components inclusive of evaporator and condenser	No	200		
		.08 Clean evaporator and condenser fan blades and check unbalance	No	150		
		.09 Supply and install condensate drain pipe (25mm diameter)	m	420		
		.10 Repair indoor air guide vents	No	350		
		.11 Replace compressor vibration mountings	No	150		
		.12 Supply and Install Wall Mounted AC Controllers	No	65		
		.12 Supply Wall Mounted AC Controllers batteries	No	1446		
		.13 Re-gasing of regrigerant	No	150		
		.14 Check and repair settings and operation of all safety switches, i.e. LP&HP switches, oil pressure switches, etc.	No	150		
		.15 Check running current of fans and compressor, settings and operation of overloads	No	150		
Carried forward						

SCHEDULE NO 4.1: INSTALATION M1: VIOOLSDRIFT LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:

						MECHANICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
		.16 Replace Outdoor vibration mountings	Set	150		
		.17 Clean Outdoor fan blades and check unbalance	No	150		
		.02 Air Curtain				
		.01 Replace filters	No	6		
		.02 Repair Air Curtain Air guide vents	No	6		
		.03 Repair Air Cuitain motor	No	6		
		.04 Clean air intake screen	No	6		
		.03 Wall Mounted Extractor Fans				
		.01 Repair Fan Motors	No	120		
		.02 Repair All Fan thermostarters	No	120		
		.04 Evaporative Cooler				
		.01 Repair Evaporative Cooler Motors	No	25		
		.02 Repair All Fan thermostarters	No	25		
	200.02	REPLACE AC UNITS				
		.01 Highwall Split Type Air-Conditioning Units				
		.01 High-wall Split Inverter type air-conditioning unit (2.6kW total cooling), heat pump.	No	20		
		02 12000 Btu high wall split Inverter unit, heat pump	No	20		
		03 18000 Btu Cassette split Inverter unit, heat pump.	No	10		
		04 26000 Btu high wall split Inverter unit, heat pump	No	15		
		.02 Operating and maintenance manuals				
		.01 Compile & supply a complete set of operating and maintenance manuals	Set	1		
	200.03	REPLACE EVAPORATIVE COOLERS				
		Replace10550m3/h Evaporative Cooler, axial fan driven complete as existing by manufacturers approved installer				
		.01 Supply and install complete unit including roof connecting ducting as existing	No	15		
Carried forward						

SCHEDULE NO 4.1: INSTALATION M1: VIOOLSDRIFT LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:						MECHANICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
		Flexible, round insulated ducting. Supply and install				
		.02 .01 Ø460mm	m	350		
		.03 .02 Ø308mm	m	380		
		.02 Operating and maintenance manuals				
		.01 Compile & supply a complete set of operating and maintenance manuals	Set	1		
TOTAL - CARRIED TO REPAIR SUMMARY: SCHEDULE NO 4.2: INSTALATION M2:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**SCHEDULE NO 4.3: INSTALATION M3: ONSEEPKANS LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:****MECHANICAL REPAIR WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	300.00 300.01	GENERAL REPAIR UNITS				
		.01 Highwall Ceiling Cassette Split Type Air-Conditioning Units				
		.01 Repair Outdoor Unit fins	No	6		
		.02 Check settings and operation of all pressure switches and reset if necessary	No	6		
		.03 Check settings and operation of thermostat	No	6		
		.04 Repair refrigerant pipe insulation	m	45		
		.05 De-rust, neutralize and touch up paint	No	12		
		.06 Replace filters	No	12		
		.07 Carry out a leak test on refrigeration piping and components inclusive of evaporator and condenser	No	12		
		.08 Supply and install condensate drain pipe (25mm diameter)	m	44		
		.09 Repair indoor air guide vents	No	6		
		.10 Replace compressor vibration mountings	No	8		
		.11 Supply and Install Wall Mounted AC Controllers	No	6		
		.12 Supply Wall Mounted AC Controllers batteries	No	24		
		.12 Re-gasing of regrigerant	No	12		
		.13 Check and repair settings and operation of all safety switches, i.e. LP&HP switches, oil pressure switches, etc.	No	12		
		.14 Check running current of fans and compressor, settings and operation of overloads	No	12		
		.15 Replace Outdoor vibration mountings	Set	12		
		.16 Clean Outdoor fan blades and check unbalance	No	12		
Carried forward						

SCHEDULE NO 4.3: INSTALATION M3: ONSEEPKANS LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:

MECHANICAL REPAIR WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
	300.02	INSTALL NEW AC UNITS				
		.01 Highwall Split Type Air-Conditioning Units				
		.01 High-wall Split Inverter type air-conditioning unit (3.6kW total cooling), heat pump.	No	3		
		.02 12000 Btu high wall split Inverter unit, heat pump	No	2		
		.02 Air Curtain				
		.01 Supply and Install New 900mm Air Curtain complete with Remote Contoller	No	4		
		.02 Supply and Install New 1200mm Air Curtain complete with Remote Contoller	No	1		
		.03 Wall Mounted Extractor Fans				
		.01 Wall Mounted Extractor Fan with Steel Casing at 35l/s	No	1		
		.02 Wall Mounted Extractor Fan with Steel Casing at 60l/s	No	1		
		.02 Operating and maintenance manuals				
		.01 Compile & supply a complete set of operating and maintenance manuals	Set	3		
TOTAL - CARRIED TO REPAIR SUMMARY: SCHEDULE NO 4.3: INSTALATION M3:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS
REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND
INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 4.4: INSTALATION M4: ALEXANDER BAY LPoE - CONVENTIONAL FIRE FIGHTING EQUIPMENT						MECHANICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	400.00	CONVENTIONAL FIRE FIGHTING EQUIPMENT				
	401.00	GENERAL				
	401.01	Logging and recording of operating conditions, maintenance visits, samples, inspections, surveys, tests etc: as per technical specification.				
		.01 Conventional fire fighting equipment	Sum	1		
	401.02	Signage for fire fighting equipment				
		.01 Install new silk screened Fire Fighting Signage Mechanically mounted on walls, Photoluminescent in Alluminium Frame.				
		.01 190mm x 190mm	No	116		
	402.00	DETAILS OF REPAIR WORK TO EQUIPMENT				
	402.01	Repairs of Fire Extinguishers equipment:				
		.01 9kg DCP Fire Extinguisher	No	16		
		.02 5kg CO2 Fire Extinguisher	No	15		
		.03 Fire Extinguisher Cabinet for 9kg FE	No	18		
	403.00	OPERATING AND MAINTENANCE MANUALS				
		.01 Compile & supply a complete set of operating and maintenance manuals (3 copies required)	Set	1		
TOTAL - CARRIED TO REPAIR SUMMARY: SCHEDULE NO 4.4: INSTALATION M4:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS
REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND
INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 4.5: INSTALATION M5: VIOOLSDRIFT LPoE - CONVENTIONAL FIRE FIGHTING EQUIPMENT

MECHANICAL REPAIR
WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	500.00	CONVENTIONAL FIRE FIGHTING EQUIPMENT				
	501.00	GENERAL				
	501.01	Logging and recording of operating conditions, maintenance visits, samples, inspections, surveys, tests etc: as per technical specification.				
		.01 Conventional fire fighting equipment	Sum	1		
	501.02	Signage for fire fighting equipment				
		.01 Install new silk screened Fire Fighting Signage Mechanically mounted on walls, Photoluminescent in Alluminium Frame.				
		.01 190mm x 190mm	No	315		
	502.00	DETAILS OF REPAIR WORK TO EQUIPMENT				
	502.01	Repairs and Recharge Gas for Fire Extinguishers equipment:				
		.01 9kg DCP Fire Extinguisher	No	205		
		.02 4,5kg DCP Fire Extinguisher	No	210		
		.03 5kg CO2 Fire Extinguisher	No	18		
		.04 2,5kg CO2 Fire Extinguisher	No	16		
	502.01	Replace and installation of fire hydrant equipment				
		.01 Fire Hydrant valve	No	12		
		.02 Fire Hydrant nozzle	No	12		
		.03 Fire Booster Pumps System Repair	No	1		
	502.02	Replace and installation of fire hydrant				
		.01 Painting of Fire Hydrants	No	12		
		.02 Replace 30m long, 64mm diameter, percolating fire hose coils complete with quick coupling	No	5		
		.03 Pressure Monitor Guage to furtherst Hose Reels	No	6		
Carried forward						

SCHEDULE NO 4.5: INSTALATION M5: VIOOLSDRIFT LPoE - CONVENTIONAL FIRE FIGHTING EQUIPMENT						MECHANICAL REPAIR WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
	502.00	DETAILS OF REPAIR WORK TO EQUIPMENT				
	502.01	Replace and installation of fire hose reel equipment:				
		.01 Fire hose-reel valve	No	17		
		.02 Fire hose-reel nozzle	No	17		
		.03 Repair Hose-reel cabinet, closing mechanism	No	17		
	503.00	OPERATING AND MAINTENANCE MANUALS				
		.01 Compile & supply a complete set of operating and maintenance manuals (3 copies required)	Set	1		
TOTAL - CARRIED TO REPAIR SUMMARY: SCHEDULE NO 4.5: INSTALATION M5:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS
REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND
INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 4.6: INSTALATION M6: ONSEPKANS - CONVENTIONAL FIRE FIGHTING EQUIPMENT

MECHANICAL REPAIR
WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	600.00	CONVENTIONAL FIRE FIGHTING EQUIPMENT				
	601.00	GENERAL				
	601.01	Logging and recording of operating conditions, maintenance visits, samples, inspections, surveys, tests etc: as per technical specification.				
		.01 Conventional fire fighting equipment	Sum	1		
	601.02	Signage for fire fighting equipment				
		.01 Install new silk screened Fire Fighting Signage Mechanically mounted on walls, Photoluminescent in Alluminium Frame.				
		.01 190mm x 190mm	No	22		
	602.00	DETAILS OF REPAIR WORK TO EQUIPMENT				
	602.01	Repairs of Fire Extinguishers equipment:				
		.01 9kg DCP Fire Extinguisher	No	10		
		.02 4,5kg DCP Fire Extinguisher	No	8		
		.03 5kg CO2 Fire Extinguisher	No	6		
		.04 2,5kg CO2 Fire Extinguisher	No	4		
		.05 (1m x 1m) Fire Blanket	No	4		
	603.02	OPERATING AND MAINTENANCE MANUALS				
		.01 Compile & supply a complete set of operating and maintenance manuals (3 copies required)	Set	1		
TOTAL - CARRIED TO REPAIR SUMMARY: SCHEDULE NO 4.6: INSTALATION M6:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SUMMARY OF BILL OF QUANTITIES: CIVIL MAINTENANCE WORK

		CIVIL MAINTENANCE WORK
SoQ No.: 5.1	Mandatory periodical servicing, maintenance and operation all three ports of entries	
SoQ No.: 5.2	Alexander Bay LPoE- Structural and Building related maintenance work	
SoQ No.: 5.3	Alexander Bay LPoE- Plumbing, drainage and wet services (operational area maintenance work)	
SoQ No.: 5.4	Alexander Bay LPoE- Fencing, cleaning and site maintenance work	
SoQ No.: 5.5	Alexander Bay LPoE- Bulk water and external water reticulation related maintenance work	
SoQ No.: 5.6	Alexander Bay LPoE- Roads and stormwater drainage related maintenance work	
SoQ No.: 5.7	Alexander Bay LPoE- Septic tanks maintenance work	
SoQ No.: 5.8	Violsdrift LPoE - - Structural and Building related maintenance work	
SoQ No.: 5.9	Violsdrift LPoE - Plumbing, drainage and wet services related maintenance work	
SoQ No.: 5.10	Violsdrift LPoE - Fencing, gates, cleaning and site cleaning related maintenance work	
SoQ No.: 5.11	Violsdrift LPoE - Bulk water and external water reticulation related maintenance work	
SoQ No.: 5.12	Violsdrift LPoE - Roads and stormwater drainage related maintenance work	
SoQ No.: 5.13	Violsdrift LPoE- Sanitation related maintenance work	
SoQ No.: 5.14	Onseepkans LPoE - Structural and Building related maintenance work	
SoQ No.: 5.15	Onseepkans LPoE - Plumbing, drainage & wet services related maintenance work	
SoQ No.: 5.16	Onseepkans LPoE - Fencing, cleaning & site keeping installation related maintenance work	
SoQ No.: 5.17	Onseepkans LPoE - Bulk water & external water reticulation related maintenance work	
SoQ No.: 5.18	Onseepkans LPoE - Roads & stormwater drainage related maintenance work	
SoQ No.: 5.19	Onseepkans LPoE - Septic tanks related maintenance work	
TOTAL OF BILL OF QUANTITIES - CIVIL MAINTENANCE WORK CARRIED TO CALCULATION OF TENDER SUM		

SIGNED ON BEHALF OF TENDERER:

SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING, MAINTENANCE AND OPERATION ALL THREE LPOE						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1400.00	MANDATORY PERIODICAL SERVICINGS				
EJ.01	1401.00	MANDATORY PERIODICAL SERVICING - ALEXANDER BAY LPoE				
		.01 Logging and recording of all water meter readings on a monthly basis	month	36.00		
		.02 Logging and recording of all electricity meter readings on a monthly basis	month	36.00		
		.03 Potable water quality tests to be performed by a SANS accredited laboratory (approved authorized person) on a monthly basis	month	36.00		
		.04 Cleaning and sterilization of all storage tanks (frequently)	No	6.00		
CG.01		.05 Emptying of waste skip at Alexander Bay Port of Entry on a weekly basis measured monthly as per CG.01	month	36.00		
FN.02		.06 Servicing of dosing pumps	No	6.00		
		.07 Alexander Bay Port of Entry Pest, termite and rodent control (internal)	No	4.00		
		.08 Alexander Bay Port of Entry Pest, termite and rodent control (external)	No	4.00		
		.09 Alexander Bay Port of Entry Pest, rodent control bait station stations including poison	No	42.00		
CK.03		.10 Monitoring of storage tank levels on site st Alexander Bay Port of Entry	month	36.00		
	Carried forward					

SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING, MAINTENANCE AND OPERATION ALL THREE LPOE						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		Payment reduction .01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown .02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown .03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown Emergency Breakdown: .01 Emergency Breakdown (12 hours) response - As per specification SA	days days days No	 10.00	-R 2,000.00 -R 500.00 -R 500.00 	Rate Only Rate Only Rate Only
	Carried forward					

**SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING,
MAINTENANCE AND OPERATION ALL THREE LPOE**

**CIVIL MAINTENANCE
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	1401.00	MANDATORY PERIODICAL SERVICING VIOOLSDRIFT LPoE				
		.01 Logging and recording of all water meter readings on a monthly basis	month	36.00		
		.02 Logging and recording of all electricity meter readings on a monthly basis	month	36.00		
		.03 Potable water quality tests to be performed by a SANS accredited laboratory (approved authorized person) on a monthly basis	month	36.00		
		.04 Cleaning and sterilization of all storage tanks (frequently)	No	8.00		
CG.01		.05 Emptying of waste skip at Vioolsdrift Port of Entry on a weekly basis measured monthly as per CG.01	month	36.00		
EG.01		.06 Cleaning out septic tank system and dispose of contents off-site	m ³	22.00		
FN.02		.07 Servicing of dosing pumps	No	6.00		
FN.02		.08 Servicing of desludging pump	No	6.00		
FN.02		.09 Servicing of product feed pump	No	6.00		
FN.02		.10 Servicing of high lift pump	No	3.00		
FN.02		.11 Servicing of raw water substruction pumps and ensure standby pump is always operational	No	3.00		
FD.01		.12 Service water cooler units as per manufacturers specifications on a yearly basis	No	70.00		
		.12 Vioolsdrift Port of Entry Pest, termite and rodent control (internal)	No	4.00		
		.13 Vioolsdrift Port of Entry Pest, termite and rodent control (external)	No	4.00		
		.14 Vioolsdrift Port of Entry Pest, rodent control bait station stations including poison	No	60.00		
CK.03		.15 Monitoring of storage tank levels on site Vioolsdrift Port of Entry	month	36.00		
	Carried forward					

**SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING,
MAINTENANCE AND OPERATION ALL THREE LPOE**

**CIVIL MAINTENANCE
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
		Facility Management: .01 Harvest of vegetatiion on all reed beds at least once a year. Operation will incled cutting ogf the plants at a height of 300 mm above the media surface either powered brush cutters or hand using sickles. All cut off vegetation is to be removed from the media surface as far as possible and dispose of site .02 Servicing of sand filter units and filters on yearly basis including the replacement of silicat sand of approximately 200kg .03 Final effluent test samples and reach a laboratory withn 24 hours. All chemical and bacteriological analysis results are to be kept on record by the operator Payment reduction .01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown .02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown .03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown Emergency Breakdown: .01 Emergency Breakdown (12 hours) response - As per specification SA	 year year month days days days No	 3.00 3.00 36.00 10.00	 -R 2,000.00 -R 500.00 -R 500.00 	 Rate Only Rate Only Rate Only
		Carried forward				

**SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING,
MAINTENANCE AND OPERATION ALL THREE LPOE**

**CIVIL MAINTENANCE
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	1401.00	MANDATORY PERIODICAL SERVICING - ONSEEPKANS LPoE				
		01 Logging and recording of all water meter readings on a monthly basis	month	36.00		
		.02 Logging and recording of all electricity meter readings on a monthly basi	month	36.00		
		.03 Potable water quality tests to be performed by a SANS accredited laboratory (approved authorized person) on a monthly basis	month	36.00		
		.04 Cleaning and sterilization of all storage tanks (frequently)	No	3.00		
CG.01		.05 Emptying of waste skip at Onseepkans Port of Entry on a weekly basis measured monthly as per CG.01	month	36.00		
EG.01		.06 Cleaning out septic tank system and dispose of contents off-site	m ³	22.00		
FN.02		.07 Servicing of dosing pumps	No	6.00		
		.08 Onseepkans Port of Entry Pest, termite and rodent control (internal)	No	4.00		
		.09 Onseepkans Port of Entry Pest, termite and rodent control (external)	No	4.00		
		.14 Onseepkans Port of Entry Pest, rodent control bait station stations including poison	No	5.00		
CK.03		.10 Monitoring of storage tank levels on site Onseepkans Port of Entry	month	36.00		
		.11 Operation of Water filtration and purification system in accordance with DWA BlueDrop specifications, including all chemicals AND filters required on a montly basis	month	36.00		
	Carried forward					

SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING, MAINTENANCE AND OPERATION ALL THREE LPOE						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
		Emergency Breakdown				
		Call-out for repair of Emergency Breakdown (12 hours) response.	No	10.00		
		SCHEDULE OF NO 5.1 INSTALLATION 5.1: MANDATORY PERIODICAL SERVICING, MAINTENANCE AND OPERATION ALL FOUR PoE - CARRIED TO SUMMARY:				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES**NB****TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE OF NO 5.2 INSTALLATION 5.2: ALEXANDER BAY LPoE- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK****CIVIL MAINTENANCE WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	800.00 800.01	<u>SCHEDULE NO. 14: INSTALLATION</u> <u>STRUCTURAL AND BUILDING RELATED</u> <u>Maintenance of a complete installation:</u> The Contractor shall attend to the following • Doors (hinges, locksets, strike plates, • Windows (pegs, stays, etc.) • Pull handles • Glass putty • Fascia boards • Roof cladding and sheeting • Cornices • Ceiling boards and jointing strips • Sealant • Skirtings, etc.				
	800.02	1 Alexander Bay: Proper maintenance of Structural and Building related work of operational area and residential area. Maintenance is not limited to the above-mentioned <u>Maintenance report</u> The Contractor shall compile and submit a monthly facilities inspection report, in which damaged structural components and elements of buildings and facilities ("damages") shall be listed and quantified, only if such components and elements could not be maintained or corrected at the time of inspections, due to the nature of the damage, or the need for replacement of such components and elements.	points	360.00		
	800.03	1 Alexander Bay: Comprehensive monthly facilities inspection report Breakdown maintenance: Repair of damages is remunerated for from the payment items, within the maximum allowable downtime: <u>Payment reduction:</u> Payment reduction due to exceeding of maximum allowable down-time during damage repair Maintenance of tools and equipment on following page:	points	360.00		
			days		-R 2,000.00	Rate only
	Carried Forward					

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES**NB****TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE OF NO 5.2 INSTALLATION 5.2: ALEXANDER BAY LPoE- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK****CIVIL MAINTENANCE WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
		The Contractor shall compile and submit a complete and accurate Programme of the Works 14 days after site handover and updated monthly which is linked to the expenditure and project cash flow 1 Alexander Bay Programme of the Works <u>LATE SUBMISSION OF ACCEPTABLE PROGRAMME OF THE WORKS</u> Payment reduction: Alexander Bay: Payment reduction due to late submission of an adequate/acceptable Programme of the Works	points	360.00		
	800.06		days		-R 500.00	Rate only
	800.07	Maintenance Control Plan The Contractor shall compile and submit a complete and accurate monthly Maintenance Control Plan (see Additional Specification SA), which shall be utilised to log and record all faults, system checks, breakdowns and site inspections. 1 Alexander Bay: Complete and accurate Maintenance Control Plan	points	360.00		
	800.08	<u>Payment reduction for late submission of the Maintenance Plan: LATE SUBMISSION OF ACCEPTABLE MAINTENANCE CONTROL PLAN</u> Payment reduction: Alexander Bay: Payment reduction due to late submission of an adequate/acceptable Maintenance Control Plan	days		-R 500.00	Rate only
	TOTAL:	SCHEDULE NO 14 INSTALLATION CM1: Alexander Bay LPoE - STRUCTURAL AND BUILDING - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF NO 5.3 INSTALLATION 5.3: ALEXANDER BAY LPoE PLUMBING, DRAINAGE AND WET SERVICES-RESIDENTIAL AREA -RELATED MAINTENANCE WORK

**CIVIL MAINTENANCE
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		MAINTENANCE OF PLUMBING, DRAINAGE AND WET SERVICES Maintenance of completed installation: .01 Plumbing, drainage and wet services installation The maintenance scope is described in technical specifications: AA, PAA, CF, EG, KA	point	360.00		
	1502.00	Payment reduction .01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown .02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown .03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 2,000.00	Rate Only
			days		-R 500.00	Rate Only
			days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.3 INSTALLATION 5.3: ALEXANDER BAY LPoE - PLUMBING, DRAINAGE AND WET SERVICES - CARRIED TO SUMMARY:				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.4 INSTALLATION 5.4: ALEXANDER BAY LPoE FENCING, CLEANING AND SITE RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1800.00	MAINTENANCE OF FENCING AND GATES				
	1801.00	Maintenance of a completed installation:				
		.01 Fencing, Gates refudge removal and pest control a per specification	points	360.00		
		The maintenance scope is described in technical specification: CC				
	1802.00	MAINTENANCE OF SITE KEEPING INSTALLATION				
	1803.00	Maintenance of a completed installation:				
		.01 Cleaning of site, removal of waste and cutting grass SA 07.05	points	360.00		
		The maintenance scope is described in technical specifications: CG, CJ				
	1804.00	MAINTENANCE OF CLEANING OF BUILDINGS				
	1805.00	Maintenance of a completed installation:				
		.01 Cleaning of Buildings	points	360.00		
		The maintenance scope is described in technical specifications: CJ				
	1806.00	Payment reduction:				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.4 INSTALLATION 5.4: ALEXANDER BAY LPoE - FENCING, CLEANING AND SITE RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.5 INSTALLATION 5.5: ALEXANDER BAY LPoE BULK WATER AND EXTERNAL WATER RETICULATION -RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1900.00	MAINTENANCE OF BULK WATER AND EXTERNAL WATER RETICULATION				
	1901.00	Maintenance and servicing of completed installation:				
		.01 Bulk water, External water and pump systems	point	360.00		
		.02 Operation of Water filtration and purification system, including all chemicals, filters, etc required on a monthly basis	month	36.00		
		The maintenance scope is described in technical specifications: CE, CI, DA, DL, DN, EK, FN KA				
	1902.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.5 INSTALLATION 5.5: ALEXANDER BAY LPoE - BULK WATER AND EXTERNAL WATER RETICULATION -RELATED MAINTENANCE WORK				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.6 INSTALLATION 5.6: ALEXANDER BAY LPoE - ROADS AND STORMWATER DRAINAGE -RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2000.00	MAINTENANCE OF ROADS AND STORMWATER DRAINAGE				
	2001.00	Maintenance of completed installation:				
		.01 Roads and stormwater	point	360.00		
		The maintenance scope is described in technical specifications: CA, CB				
	2002.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
	2002.01	Road Markings				
		.01 Retro-reflective road- marking paint				
		01 Longitudinal lines:				
		(i) 100 mm wide broken or unbroken lines, white, yellow or red	m	250.00		
		.02 Transverse lines and other				
		(i) Broken or unbroken lines, white or yellow.	m2	12.00		
		(ii) Lettering and symbols, white or yellow, repainting existing markings	m2	36.00		
		(iii) Traffic island markings, white or yellow repainting existing markings	m2	65.00		
		.02 Setting out and premarking of lines (excluding traffic island markings, lettering and symbols)	km	1.00		
	TOTAL	SCHEDULE NO 5.5 INSTALLATION 5.5: ALEXANDER BAY LPoE - ROADS AND STORMWATER DRAINAGE -RELATED MAINTENANCE WORK				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.6 INSTALLATION 5.6: ALEXANDER BAY LPoE WASTEWATER AND SEWER NETWORKS - RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		SANITATION/SEPTIC TANKS AND SEWER NETWORKS				
	2601.00	Maintenance and servicing of completed installation:				
		.01 De-sludging of septic tanks and dispose of contents of site	No	12.00		
		.02 Sewer Networks	point	360.00		
		The maintenance scope is described in technical specifications: AA,PAA,CF,EG,KA				
	2602.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 107.50	Rate Only
	TOTAL	SCHEDULE NO 5.6 INSTALLATION 5.6: ALEXANDER BAY LPoE WASTEWATER AND SEWER NETWORKS - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY:				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES**NB****TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE OF NO 5.8 INSTALLATION 5.8: VIOOLSDRIFT LPoE- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK**

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		<u>SCHEDULE NO. 5.8: INSTALLATION</u>				
		<u>C1:VIOOLSDRIFT- STRUCTURAL AND</u>				
	800.00	<u>BUILDING -RELATED MAINTENANCE WORK</u>				
	800.01	<u>STRUCTURAL AND BUILDING RELATED WORK</u> Maintenance of a complete installation: The Contractor shall attend to the following during daily inspections of all structural components and elements of buildings and facilities: Preventative maintenance work and minor corrections of all structural and building related facilities, including components and elements such as, but not limited to: • Doors (hinges, locksets, strike plates, indicator locks) • Windows (pegs, stays, etc.) • Pull handles • Glass putty • Fascia boards • Roof cladding and sheeting • Cornices • Ceiling boards and jointing strips • Sealant • Skirtings, etc.				
		1 Violsdrift: Proper maintenance of Structural and Building related work of operational area and residential area. Maintenance is not limited to the above-mentioned	points	360.00		
	800.02	<u>Maintenance report</u> The Contractor shall compile and submit a monthly facilities inspection report, in which damaged structural components and elements of buildings and facilities ("damages") shall be listed and quantified, only if such components and elements could not be maintained or corrected at the time of inspections, due to the nature of the damage, or the need for replacement of such components and elements.				
	Carried Forward					

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES**NB****TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE OF NO 5.8 INSTALLATION 5.8: VIOOLSDRIFT LPoE- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK**

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		Brought forward				
	800.03	1 Violsdrift: Comprehensive monthly facilities inspection report Breakdown maintenance: Repair of damages is remunerated for from the payment items, within the maximum allowable downtime: <u>Payment reduction:</u> Payment reduction due to exceeding of maximum allowable down-time during damage repair Maintenance of tools and equipment on following page: The Contractor shall compile and submit a complete and accurate Programme of the Works 14 days after site handover and updated monthly which is linked to the expenditure and project cash flow	points	360.00		
	800.06	1 Violsdrift Programme of the Works <u>LATE SUBMISSION OF ACCEPTABLE PROGRAMME OF THE WORKS</u> <u>Payment reduction:</u> Violsdrift: Payment reduction due to late submission of an adequate/acceptable Programme of the Works	days		-R 500.00	Rate only
	800.07	Maintenance Control Plan The Contractor shall compile and submit a complete and accurate monthly Maintenance Control Plan (see Additional Specification SA), which shall be utilised to log and record all faults, system checks, breakdowns and site inspections.				
	800.08	1 Violsdrift: Complete and accurate Maintenance Control Plan <u>Payment reduction for late submission of the Maintenance Plan:</u> <u>LATE SUBMISSION OF ACCEPTABLE MAINTENANCE CONTROL PLAN</u> <u>Payment reduction: Violsdrift: Payment reduction due to late submission of an adequate/acceptable Maintenance Control Plan</u>	points	360.00		
			days		-R 500.00	Rate only
	TOTAL	SCHEDULE OF NO 5.8 INSTALLATION 5.8: VIOOLSDRIFT LPoE- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.6 INSTALLATION 5.9: VIOOLSDRIFT LPoE- PLUMBING, DRAINAGE AND WET SERVICES - RELATED MAINTENANCE WORK

CIVIL MAINTENANCE WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2601.00	Maintenance and servicing of completed installation: .01 Plumbing, drainage and wet services installation SA 07.01(Including solar geysers as per O&M Manual) The maintenance scope is described in technical specifications: AA,PAA,CF,EG,KA	point	360.00		
	2602.00	Payment reduction .01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown .02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown .03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 2,000.00	Rate Only
			days		-R 500.00	Rate Only
			days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.9 INSTALLATION 5.9: VIOOLSDRIFT LPoE- PLUMBING, DRAINAGE AND WET SERVICES - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY:				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.10: INSTALLATION 5.10: VIOOLSDRIFT LPoE- FENCING, GATES CLEANING, SITE KEEPING AND PEST CONTROL - RELATED MAINTENANCE WORK

CIVIL MAINTENANCE WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2800.00	MAINTENANCE OF FENCING AND GATES				
	2801.00	Maintenance and servicing of completed installation:				
		.01 Fencing, Gates refudge removal and pest control as per specification	points	360.00		
		The maintenance scope is described in technical specification: CC				
	2802.00	MAINTENANCE OF SITE KEEPING INSTALLATION				
	2803.00	Maintenance and servicing of completed installation:				
		.01 Cleaning of site, removal of waste and cutting grass SA 07.05	points	360.00		
		The maintenance scope is described in technical specifications: CG, CJ				
	2804.00	MAINTENANCE OF CLEANING OF BUILDINGS				
	2804.00	Maintenance and servicing of completed installation:				
		.01 Cleaning of Buildings	points	360.00		
		The maintenance scope is described in technical specifications: CJ				
	2806.00	Payment reduction:				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.10: INSTALLATION 5.10: VIOOLSDRIFT LPoE- FENCING, GATES CLEANING AND SITE KEEPING - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 5.11: INSTALLATION 5.11: VIOOLSDRIFT LPoE- BULK WATER AND EXTERNAL WATER RETICULATION - RELATED MAINTENANCE WORK**

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2900.00	SCHEDULE NO 5.11: INSTALLATION 5.11- BULK WATER AND EXTERNAL WATER RETICULATION - RELATED MAINTENANCE WORK				
	2900.00	MAINTENANCE OF BULK WATER AND EXTERNAL WATER RETICULATION				
	2901.00	Maintenance and servicing of completed installation:				
		.01 Bulk water, External water and water treatment plant as per specifications	point	360.00		
		The maintenance scope is described in technical specifications: CE,CI,DA,DL,DN,EK,FN KA				
		.02 Telemetry as per specification SA 07.20	point	360.00		
	2902.00	Facility management				
		Operation of Water purification system, including all pumps, tanks, flocculation device, chemicals(sufficient stock), filters(monthly), accuulation tanks, chemical tanks, electrical switchgear, PLC controls system and instrumentation etc required on a monthly basis in order to ensure automatic and manual operation for clean drinking water	month	36.00		
	2903.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.11: INSTALLATION 5.11: VIOOLSDRIFT- BULK WATER AND EXTERNAL WATER RETICULATION - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.12: INSTALLATION 5.12: VIOOLSDRIFT LPoE- ROADS AND STORMWATER DRAINAGE RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3000.00	MAINTENANCE OF ROADS AND STORMWATER DRAINAGE				
	3001.00	Maintenance and servicing of completed installation:				
		.01 Roads and stormwater	point	360.00		
		The maintenance scope is described in technical specifications: CA, CB				
	3002.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during malicious damage breakdown	days		-R 500.00	Rate Only
	3003.00	Road Markings				
		.01 Retro-reflective road- marking paint				
		.01 Longitudinal lines:				
		(i) 100 mm wide broken or unbroken lines, white, yellow or red	m	250.00		
		.02 Transverse lines and other				
		(i) Broken or unbroken lines, white or yellow.	m2	35.00		
		(iii) Traffic island markings, white or yellow repainting existing markings	m2	60.00		
	TOTAL	SCHEDULE NO 5.12: INSTALLATION 5.12: VIOOLSDRIFT LPoE- ROADS AND STORMWATER DRAINAGE RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.13: INSTALLATION 5.13:VIOOLSDRIFT LPoE - WASTEWATER AND SEWER NETWORKS - RELATED MAINTENANCE WORK

CIVIL MAINTENANCE WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3500.00	MAINTENANCE OF PLUMBING, DRAINAGE AND WET SERVICES				
	3501.00	Maintenance and servicing of completed installation:				
		.01 Waste Water Treatment Works as per specifications and sewer networks	point	360		
		Facility manangement				
		Operation of wastewater sysytem including sewer pump stations, Huber inlet systems, septic tanks, reed beds, drying beds, etc required on a monthly basis in order to ensure final effluent water is within limits.	month	36		
		The maintenance scope is described in technical specifications: AA,PAA,CF,EG,KA				
	3502.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency break	days		-R 2,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days		-R 500.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during damage breakdown	days		-R 500.00	Rate Only
	TOTAL	SCHEDULE NO 5.13: INSTALLATION 5.13: VIOOLSDRIFT LPoE - ROADS AND STORMWATER DRAINAGE RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF NO 5.14 INSTALLATION 5.14: ONSEEPKANS- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	800.00 800.01	<u>SCHEDULE NO. 14: INSTALLATION</u> <u>C1ONSEEPKANS - STRUCTURAL AND BUILDING -RELATED MAINTENANCE WORK</u> <u>STRUCTURAL AND BUILDING RELATED Maintenance of a complete installation:</u> The Contractor shall attend to the following during daily inspections of all structural components and elements of buildings and facilities: Preventative maintenance work and minor corrections of all structural and building related facilities, including components and elements such as, but not limited to: • Doors (hinges, locksets, strike plates, indicator locks) • Windows (pegs, stays, etc.) • Pull handles • Glass putty • Fascia boards • Roof cladding and sheeting • Cornices • Ceiling boards and jointing strips • Sealant • Skirtings, etc. 1 Onseepkans: Proper maintenance of Structural and Building related work of operational area and residential area. Maintenance is not limited to the above-mentioned				
	800.02	<u>Maintenance report</u> The Contractor shall compile and submit a monthly facilities inspection report, in which damaged structural components and elements of buildings and facilities ("damages") shall be listed and quantified, only if such components and elements could not be maintained or corrected at the time of inspections, due to the nature of the damage, or the need for replacement of such components and elements. 1 Onseepkans: Comprehensive monthly facilities inspection report Breakdown maintenance: Repair of damages is remunerated for from the payment items, within the maximum allowable downtime:	points	360.00		
		<u>Payment reduction:</u>	points	360.00		
	Carried Forward					

SCHEDULE OF NO 5.14 INSTALLATION 5.14: ONSEEPKANS- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	800.03	Payment reduction due to exceeding of maximum allowable down-time during damage repair Maintenance of tools and equipment on following page: The Contractor shall compile and submit a complete and accurate Programme of the Works 14 days after site handover and updated monthly which is linked to the expenditure and project cash flow 1 Onseepkans Programme of the Works <u>LATE SUBMISSION OF ACCEPTABLE PROGRAMME OF THE WORKS</u> Payment reduction: Onseepkans: Payment reduction due to late submission of an adequate/acceptable Programme of the Works	days	-	-R 500.00	Rate only
	800.06		days	-	-R 500.00	Rate only
	800.07	Maintenance Control Plan The Contractor shall compile and submit a complete and accurate monthly Maintenance Control Plan (see Additional Specification SA), which shall be utilised to log and record all faults, system checks, breakdowns and site inspections. 1 Onseepkans: Complete and accurate Maintenance Control Plan	points	360.00		
	800.08	<u>Payment reduction for late submission of the Maintenance Plan: LATE SUBMISSION OF ACCEPTABLE MAINTENANCE CONTROL PLAN</u> Payment reduction: Onseepkans: Payment reduction due to late submission of an adequate/acceptable Maintenance Control Plan	days	-	-R 500.00	Rate only
	TOTAL	SCHEDULE OF NO 5.14 INSTALLATION 5.14: ONSEEPKANS- STRUCTURAL AND BUILDING - RELATED MAINTENANCE WORK- CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 5.15: INSTALLATION 5.15: ONSEEPKANS LPoE- PLUMBING, DRAINAGE AND WET SERVICES - RELATED MAINTENANCE WORK

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3501.00	Maintenance and servicing of completed installation: .01 Plumbing, drainage and wet services instalation The maintenance scope is described in technical specifications: AA,PAA,CF,EG,KA	point	360.00		
	3502.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time	days		-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time	days		-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time	days		-R 107.50	Rate Only
	TOTAL	SCHEDULE NO 5.15: INSTALLATION 5.15: ONSEEPKANS LPoE- PLUMBING, DRAINAGE AND WET SERVICES - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 5.16: INSTALLATION 5.16: ONSEEPKANS LPoE- FENCING CLEANING AND SITE KEEPING INSTALLATION - RELATED MAINTENANCE WORK

CIVIL MAINTENANCE WORK

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3701.00	Maintenance and servicing of completed installation: .01 Fencing, Gates refudge removal and pest control a per specification The maintenance scope is described in technical specification: CC	points	360.00		
	3702.00	MAINTENANCE OF SITE KEEPING INSTALLATION				
	3703.00	Maintenance of a completed installation: .01 Cleaning of site, removal of waste and cutting grass The maintenance scope is described in technical specifications: CG, CJ	points	360.00		
	3704.00	MAINTENANCE OF CLEANING OF BUILDINGS				
	3705.00	Maintenance of a completed installation: .01 Cleaning of Buildings The maintenance scope is described in technical specifications: CJ	points	360.00		
	3706.00	Payment reduction: .01 Payment reduction due to exceeding of maximum allowable down-time .02 Payment reduction due to exceeding of maximum allowable down-time .03 Payment reduction due to exceeding of maximum allowable down-time	days		-R 1,075.00	Rate Only
			days		-R 107.50	Rate Only
			days		-R 107.50	Rate Only
	TOTAL	SCHEDULE NO 5.11: INSTALLATION 5.11: ONSEEPKANS LPoE- FENCING CLEANING AND SITE KEEPING INSTALLATION - RELATED MAINTENANCE WORK				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 5.17: INSTALLATION 5.17: ONSEEPKANS LPoE- BULK WATER AND EXTERNAL WATER RETICULATION - RELATED MAINTENANCE WORK**

						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3800.00	MAINTENANCE OF BULK WATER AND EXTERNAL WATER RETICULATION				
	3801.00	Maintenance and servicing of completed installation:				
		.01 Bulk water, External water and water treatment plant as per specifications	point	360.00		
		The maintenance scope is described in technical specifications: CE,CI,DA,DL,DN,EK,FN KA				
	3802.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time	days		-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time	days		-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time	days		-R 107.50	Rate Only
	TOTAL	SCHEDULE NO 5.17: INSTALLATION 5.17: ONSEEPKANS LPoE- BULK WATER AND EXTERNAL WATER RETICULATION - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 5.18: INSTALLATION 5.18: ONSEEPKANS LPoE- ROADS AND STORMWATER DRAINAGE- RELATED MAINTENANCE WORK						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3900.00	MAINTENANCE OF ROADS AND STORMWATER DRAINAGE				
	3901.00	Maintenance of completed installation:				
		.01 Roads and stormwater	point	360.00		
		The maintenance scope is described in technical specifications: CA, CB				
	3902.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time	days		-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time	days		-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time	days		-R 107.50	Rate Only
	TOTAL	SCHEDULE NO 5.18: INSTALLATION 5.18: ONSEEPKANS LPoE- ROADS AND STORMWATER DRAINAGE- RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB

TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 5.19: ONSEEPKANS- WASTEWATER AND SEWER NETWORKS-RELATED MAINTENANCE WORK						CIVIL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
		SANITATION/SEPTIC TANKS AND SEWER NETWORKS				
		Maintenance of completed installation:				
		.01 De-sludging of septic tanks and dispose of contents off-site	No	9.00		
		.02 Sewer Networks	point	360.00		
		The maintenance scope is described in technical specifications: AA,PAA,CF,EG,KA				
		Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		R 1,000.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		R 100.00	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days		R 100.00	Rate Only
	TOTAL	SCHEDULE NO 5.19: INSTALLATION 5.19: ONSEEPKANS- ROADS AND STORMWATER DRAINAGE- RELATED MAINTENANCE WORK- CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SUMMARY OF BILL OF QUANTITIES: ELECTRICAL MAINTENANCE WORK

		ELECTRICAL MAINTENANCE WORK
SoQ No.: 6.1	Alexander Bay LPoE - Building electrical - Operational Area related maintenance work	
SoQ No.: 6.2	Alexander Bay LPoE - Building electrical - Residentail area related maintenance work	
SoQ No.: 6.3	Alexander Bay LPoE - Standby power installation related maintenance work	
SoQ No.: 6.4	Alexander Bay LPoE - External lighting installation related maintenance work	
SoQ No.: 6.5	Vioolsdrift LPoE- Building electrical services related maintenance work	
SoQ No.: 6.6	Vioolsdrift LPoE- Building electrical - Residentail area related maintenance work	
SoQ No.: 6.7	Vioolsdrift LPoE - Standby power installation related maintenance work	
SoQ No.: 6.8	Vioolsdrift LPoE - External lighting installation related maintenance work	
SoQ No.: 6.9	Onseepkans LPoE - Building electrical services related maintenance work	
SoQ No.: 6.10	Onseepkans LPoE- Building electrical - Residentail area related maintenance work	
SoQ No.: 6.11	Onseepkans LPoE - Standby power installation related maintenance work	
SoQ No.: 6.12	Onseepkans LPoE - External lighting installation related maintenance work	

TOTAL OF BILL OF QUANTITIES - ELECTRICAL MAINTENANCE WORK	
CARRIED TO CALCULATION OF TENDER SUM	
.....	

SIGNED ON BEHALF OF TENDERER:

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITIES No.: 6.1 INSTALLATION 6.1: ALEXANDER BAY LPoE- BUILDING ELECTRICAL-OPERATIONAL AREA - RELATED MAINTENANCE WORK

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1600.00	MAINTENANCE OF BUILDING ELECTRICAL SERVICES				
	1601.00	Maintenance of completed installation:				
		.01 Building electrical services	point	360.00		
		The maintenance scope is described in technical specifications: AA, PAA,				
	1602.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
	1603.00	Call-out for repair of Emergency Breakdown (12 hours) response.	No	12.00		
	TOTAL	SCHEDULE OF QUANTITIES No.: 6.1 INSTALLATION 6.1: ALEXANDER BAY LPoE- BUILDING ELECTRICAL-OPERATIONAL AREA - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITIES No.: 6.2 INSTALLATION 6.2: ALEXANDER BAY LPoE - BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK

**ELECTRICAL
MAINTENANCE
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1700.00	MAINTENANCE OF BUILDING ELECTRICAL SERVICES				
	1701.00	Maintenance of completed installation:				
		.01 Building electrical services	point	360.00		
		The maintenance scope is described in technical specifications: AA, PAA,				
	1702.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
	1703.00	Call-out for repair of Emergency Breakdown (24 hours) response.	No	6.00		
	TOTAL	SCHEDULE OF QUANTITIES No.: 6.2 INSTALLATION 6.2: ALEXANDER BAY LPoE - BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**
**SCHEDULE OF QUANTITIES No:6.3 INSTALLATION 6.3: ALEXANDER BAY LPoE - STANDBY POWER
INSTALLATION - RELATED MAINTENANCE WORK**

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2100.00	MAINTENANCE OF STANDBY POWER INSTALLATION				
	2101.00	Maintenance of completed installation:				
		.01 Standby Power installations (Clean, dust, inspect and test-run genset as per specification)	point	360.00		
		The maintenance scope is described in technical specifications: HB				
	2102.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
	2103.00	Call-out for repair of Emergency Breakdown (24 hours) response.	No	10.00		
		Mandatory periodical services not included in preventative maintenance				
	Carried forward					

SCHEDULE OF QUANTITES No:6.3 INSTALLATION 6.3: ALEXANDER BAY LPoE - STANDBY POWER INSTALLATION - RELATED MAINTENANCE WORK						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	Brought forward					
	2104.00	GENERATOR				
	2104.01	Service 100 kVA genset	number	6.00		
	2104.02	Service CAT diesel engine 100 kVA unit	number	3.00		
	2104.03	Supply diesel fuel	litre	14,000.00		
	2104.04	Filter Cartridge for MK3 fuel water separator	number	3.00		
	2104.05	Filter Cartridge for MK4 fuel water separator	number	3.00		
	TOTAL	SCHEDULE OF QUANTITES No:6.3 INSTALLATION 6.3: ALEXANDER BAY LPoE - STANDBY POWER INSTALLATION - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITIES No.: 6.4 INSTALLATION 6.4: ALEXANDER BAY LPoE- EXTERNAL LIGHTING INSTALLATION - RELATED MAINTENANCE WORK

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2200.00	MAINTENANCE OF EXTERNAL LIGHTING INSTALLATION				
	2201.00	Maintenance of completed installation:				
		.01 External Lighting Installation	point	360.00		
		The maintenance scope is described in technical specifications: HB				
	2102.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate Only
		02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
		03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
	TOTAL	SCHEDULE OF QUANTITIES No.: 6.4 INSTALLATION 6.4: ALEXANDER BAY LPoE- EXTERNAL LIGHTING INSTALLATION - RELATED MAINTENANCE WORK				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 6.5: INSTALLATION 6.5: VIOOLSDRIFT LPoE- BUILDING ELECTRICAL SERVICES - RELATED MAINTENANCE WORK****ELECTRICAL
MAINTENANCE
WORK**

PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2700.00	MAINTENANCE OF BUILDING ELECTRICAL SERVICES				
	2701.00	Maintenance of completed installation:				
		.01 Building electrical services	point	360.00		
		The maintenance scope is described in technical specifications: AA, PAA,				
	2702.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time	days	-	-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time	days	-	-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time	days	-	-R 107.50	Rate Only
	2703.00	Call-out for repair of Emergency Breakdown (24 hours) response.	No	6.00		
	TOTAL	SCHEDULE NO 6.5: INSTALLATION 6.5: VIOOLSDRIFT LPoE- BUILDING ELECTRICAL SERVICES - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITES No.: 6.6 INSTALLATION 6.6: VIOOLSDRIFT LPoE - BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	2800.00	SCHEDULE OF QUANTITES No.: 6.6 INSTALLATION 6.6: VIOOLSDRIFT LPoE - BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK				
	2800.00	MAINTENANCE OF BUILDING ELECTRICAL SERVICES				
	2801.00	Maintenance of completed installation:				
		.01 Building electrical services	point	360.00		
	2802.00	The maintenance scope is described in technical specifications: AA, PAA, Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate Only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
		.03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate Only
	2803.00	Call-out for repair of Emergency Breakdown (24 hours) response.	No	6.00		
	TOTAL	SCHEDULE OF QUANTITES No.: 6.6 INSTALLATION 6.6: VIOOLSDRIFT LPoE - BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 6.7: INSTALLATION 6.7: VIOOLSDRIFT LPoE -STANDBY POWER INSTALLATION - RELATED MAINTENANCE WORK

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3100.00	MAINTENANCE OF STANDBY POWER INSTALLATION				
	3101.00	Maintenance of completed installation: .01 Standby Power installations (Clean, dust, inspect and test-run genset as per specification) The maintenance scope is described in technical specifications: HB	point	360.00		
	3102.00	Payment reduction .01 Payment reduction due to exceeding of maximum allowable down-time .02 Payment reduction due to exceeding of maximum allowable down-time .03 Payment reduction due to exceeding of maximum allowable down-time Mandatory periodical services not included in preventative maintenance items listed above:	days	-	-R 1,075.00	Rate Only
			days	-	-R 107.50	Rate Only
			days	-	-R 107.50	Rate Only
	3103.00	GENERATOR				
	3103.01	Service 100kVA, 2 x 25KVA, 15kVA and 10 kVA genset	number	6.00		
	3103.02	Service Perkins diesel engine 100kVA, 2 x 25kVA, 15kVA and 10 kVA unit	number	3.00		
	3103.03	Supply diesel fuel	litre	28,000.00		
	3103.04	Filter Cartridge for MK3 fuel water separator	number	6.00		
	3104.05	Filter Cartridge for MK4 fuel water separator	number	6.00		
		Call-out for repair of Emergency Breakdown (24 hours) response.	No	20.00		
	TOTAL	SCHEDULE NO 6.7: INSTALLATION 6.7: VIOOLSDRIFT LPoE -STANDBY POWER INSTALLATION - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 6.8: INSTALLATION 6.8: VIOOLSDRIFT LPoE - EXTERNAL LIGHTING INSTALLATION-RELATED MAINTENANCE WORK**

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3200.00	MAINTENANCE OF EXTERNAL LIGHTING INSTALLATION				
	3201.00	Maintenance of completed installation:				
		.01 External Lighting Installation	point	360.00		
		The maintenance scope is described in technical specifications: HB				
	3102.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time	days	-	-R 1,075.00	Rate only
		.02 Payment reduction due to exceeding of maximum allowable down-time	days	-	-R 107.50	Rate only
		.03 Payment reduction due to exceeding of maximum allowable down-time	days	-	-R 107.50	Rate only
	TOTAL	SCHEDULE NO 6.8: INSTALLATION 6.8: VIOOLSDRIFT LPoE - EXTERNAL LIGHTING INSTALLATION- RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 6.9: INSTALLATION 6.9: ONSEEPKANS LPoE - BUILDING ELECTRICAL SERVICES - RELATED MAINTENANCE WORK**

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3600.00	MAINTENANCE OF BUILDING ELECTRICAL SERVICES				
	3601.00	Maintenance of completed installation:				
		.01 Building electrical services	point	360.00		
		The maintenance scope is described in technical specifications: AA, PAA, CF, EG, KA				
	3602.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate only
		.03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate only
	3603.00	Call-out for repair of Emergency Breakdown (24 hours) response.	No	6.00		
	TOTAL	SCHEDULE NO 6.9: INSTALLATION 6.9: ONSEEPKANS LPoE - BUILDING ELECTRICAL SERVICES - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE OF QUANTITIES No.: 6.10 INSTALLATION 6.10: ONSEEPKANS LPoE- BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	3607.00	MAINTENANCE OF BUILDING ELECTRICAL SERVICES				
	3607.01	Maintenance of completed installation:				
		.01 Building electrical services	point	360.00		
		The maintenance scope is described in technical specifications: AA, PAA,				
	3607.02	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate only
		.02 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate only
		.03 Payment reduction due to exceeding of maximum allowable down-time during ordinary breakdown	days	-	-R 107.50	Rate only
	3607.03	Call-out for repair of Emergency Breakdown (24 hours) response.	No	6.00		
	TOTAL	SCHEDULE OF QUANTITIES No.: 6.10 INSTALLATION 6.10: ONSEEPKANS LPoE- BUILDING ELECTRICAL - RESIDENTIAL AREA - RELATED MAINTENANCE WORK - CARRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB **TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

SCHEDULE NO 6.11: INSTALLATION 6.11: ONSEEPKANS LPoE- STANDBY POWER INSTALLATION - RELATED MAINTENANCE WORK

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	4000.00	MAINTENANCE OF STANDBY POWER INSTALLATION				
	4001.00	Maintenance of completed installation: .01 Standby Power installation (Clean, dust, inspect and test-run genset as per specification) The maintenance scope is described in technical specifications: HB	point	360.00		
	4002.00	Payment reduction .01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown .02 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown .03 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate only
			days	-	-R 107.50	Rate only
			days	-	-R 107.50	Rate only
	4003.00	Call-out for repair of Emergency Breakdown (24 hours) response Mandatory periodical services not included In preventative maintenance	No	20.00		
	4004.00	GENERATOR				
	4004.01	Service 100 kVA genset	number	6.00		
	4004.02	Service John Deere diesel engine 100 kVA unit	number	3.00		
	4004.03	Supply diesel fuel	litre	10,300.00		
	4004.04	Filter Cartridge for MK3 fuel water separator	number	3.00		
	4004.05	Filter Cartridge for MK4 fuel water separator	number	3.00		
	TOTAL	SCHEDULE NO 6.11: INSTALLATION 6.11: ONSEEPKANS LPoE- STANDBY POWER INSTALLATION - RELATED MAINTENANCE WORK - CRRIED TO SUMMARY				

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB**TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**

**SCHEDULE NO 6.12: INSTALLATION 6.12: ONSEEPKANS LPoE - EXTERNAL LIGHTING
INSTALLATION -RELATED MAINTENANCE WORK**

						ELECTRICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	4000.00	MAINTENANCE OF EXTERNAL LIGHTING INSTALLATION				
	4001.00	Maintenance of completed installation:				
		.01 External Lighting Installation	point	360.00		
		The maintenance scope is described in technical specifications: HB				
	4002.00	Payment reduction				
		.01 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 1,075.00	Rate only
		.02 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 107.50	Rate only
		.03 Payment reduction due to exceeding of maximum allowable down-time during emergency breakdown	days	-	-R 107.50	Rate only
	4003.00	AREA LIGHTING SYSTEM - REPAIR CONTROL AREA				
	4003.01	Re-lamp luminaire:				
		.01 250W HPS Floodlight	number	2.00		
	4003.02	Service Luminaire				
		.01 250W HPS Floodlight	number	6.00		
	Carried forward					

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE SCHEDULE OF QUANTITIES IN BLACK INK

SUMMARY OF SCHEDULE OF QUANTITIES:MECHANICAL MAINTENANCE WORK

**MECHANICAL MAINTENANCE
WORK**

SCHEDULE NO 7.1: INSTALLATION M7: ALEXANDER BAY LPoE- HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS

.....

SCHEDULE NO 7.2: INSTALLATION M8: VIOOLSDRIFT LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS

.....

SCHEDULE NO 7.3: INSTALLATION M9: ONSEEPKANS LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS

.....

SCHEDULE NO 7.4: INSTALLATION M10: ALEXANDER BAY LPoE CONVENTIONAL FIRE FIGHTING EQUIPMENT

.....

SCHEDULE NO 7.5: INSTALLATION M11: VIOOLSDRIFT LPoE CONVENTIONAL FIRE FIGHTING EQUIPMENT

.....

SCHEDULE NO 7.6: INSTALLATION M12: ONSEEPKANS LPoE CONVENTIONAL FIRE FIGHTING EQUIPMENT

.....

**TOTAL OF SCHEDULE OF QUANTITIES - MECHANICAL MAINTENANCE WORK
CARRIED TO CALCULATION OF TENDER SUM**

.....

SIGNED ON BEHALF OF TENDERER:

.....

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES**NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 7.1: INSTALLATION M7: ALEXANDER BAY LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:**

						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	700.00	MAINTENANCE OF HEATING, VENTILATION AND AIRCONDITIONING				
	701.00	Maintenance of a complete installation				
		.01 Heating, Ventilation and Air Conditioning	Point	360		
		The maintenance scope is described in technical specifications,				
	702.00	Payment Reduction				
		.01 Payment Reduction due to exceeding of maximum allowable down-time during Emergency Breakdown	Day	-	-R 1,000.00	Rate only
		.02 Payment Reduction due to exceeding of maximum allowable down-time during Ordinary Breakdown	Day	-	-R 200.00	Rate only
		.03 Payment Reduction due to exceeding of maximum allowable down-time during Malicious Damage Repair	Day	-	-R 200.00	Rate only
	703.00	Mandatory periodical services not included in preventative maintenance items listed above				
		.01 Alexander Bay Operational Area				
		Provide Full service of Air-conditioning Units according to manufacturer's specifications (Bi-Annually)				
		.01 Highwall Split Unit	No	16		
		.02 Ceiling Cassette Split Unit	No	2		
		.03 Under-Ceiling Split Unit	No	2		
	703.00	.02 Alexander Bay Residential Area				
		Provide Full service of Air-conditioning Units according to manufacturer's specifications (Bi-Annually)				
		.01 Highwall Split Unit	No	38		
		.02 Allow training for End-user client	Hrs	16		
TOTAL - CARRIED TO MAINTENANCE SUMMARY: SCHEDULE NO 7.1: INSTALLATION M7:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES**NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 7.2: INSTALLATION M8: VIOOLSDRIFT LPoE- HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:**

						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1000.00	MAINTENANCE OF HEATING, VENTILATION AND AIRCONDITIONING				
	1001.00	Maintenance of a complete installation				
		.01 Heating, Ventilation and Air Conditioning	Point	360		
		The maintenance scope is described in technical specifications,				
	1002.00	Payment Reduction				
		.01 Payment Reduction due to exceeding of maximum allowable down-time during Emergency Breakdown	Day	-	-R 1,000.00	Rate only
		.02 Payment Reduction due to exceeding of maximum allowable down-time during Ordinary Breakdown	Day	-	-R 200.00	Rate only
		.03 Payment Reduction due to exceeding of maximum allowable down-time during Malicious Damage Repair	Day	-	-R 200.00	Rate only
	1003.00	Mandatory periodical services not included in preventative maintenance items listed above				
		.01 Vioolsdrift Operational Area				
		Provide Full service of Air-conditioning Units according to manufacturer's specifications (Bi-Annually)				
		.01 Highwall Split Unit	No	148		
		.02 Ceiling Cassette Split Unit	No	17		
		.03 Under-Ceiling Split Unit	No	8		
		.04 Air Curtain	No	8		
Carried forward						

SCHEDULE NO 7.2: INSTALLATION M8: VIOOLSDRIFT LPoE- HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:

						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
	1003.00	.02 Vioolsdrift Residential Area				
		Provide Full service of Air-conditioning Units according to manufacturer's specifications (Bi-				
		.01 Highwall Split Unit	No	500		
		.02 Evaporative Coolers:	No	35		
		Supply and install 850x526mm Chillcell filter pads sets as per manufacturers specification		32		
		Supply and install 360mm x 360mm uPVC adjustable outlet ceiling louver including fitting and cutting of ceiling board complete	No	20		
		Replace large pad frame beige cabinets - made from Permatuf corrosion-proofstructural polymer material as existing	No	20		
		Replace water pump, with an encapsulated motor including overload cut-out, stainless steel shaft and bearings, as per existing	No	20		
		Replace 950W electrical motor, fully enclosed with aluminium casing	No	20		
		Supply and replace high efficient axial fan complete, purpose designed and inherently balanced for existing evaporative systems	No	20		
		.03 Allow training for End-user client	Hrs	16		
TOTAL - CARRIED TO MAINTENANCE SUMMARY: SCHEDULE NO 7.2: INSTALLATION M8:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES**NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK****SCHEDULE NO 7.3: INSTALLATION M9: ONSEEPKANS LPoE - HEATING, VENTILATION AND AIRCONDITIONING SYSTEMS:**

						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	900.00	MAINTENANCE OF HEATING, VENTILATION AND AIRCONDITIONING				
	901.00	Maintenance of a complete installation				
		.01 Heating, Ventilation and Air Conditioning	Point	360		
		The maintenance scope is described in technical specifications,				
	902.00	Payment Reduction				
		.01 Payment Reduction due to exceeding of maximum allowable down-time during Emergency Breakdown	Day	-	-R 1,000.00	Rate only
		.02 Payment Reduction due to exceeding of maximum allowable down-time during Ordinary Breakdown	Day	-	-R 200.00	Rate only
		.03 Payment Reduction due to exceeding of maximum allowable down-time during Malicious Damage Repair	Day	-	-R 200.00	Rate only
	903.00	Mandatory periodical services not included in preventative maintenance items listed above				
		.01 Onsepkans Operational Area				
		Provide Full service of Air-conditioning Units according to manufacturer's specifications (Bi-Annually)				
		.01 Highwall Split Unit	No	6		
		.02 Air Curtain	No	2		
	903.00	.02 Onsepkans Residential Area				
		Provide Full service of Air-conditioning Units according to manufacturer's specifications (Bi-Annually)				
		.01 Highwall Split Unit	No	6		
		.02 Allow training for End-user client	Hrs	16		
TOTAL - CARRIED TO MAINTENANCE SUMMARY: SCHEDULE NO 7.3: INSTALLATION M9:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK**SCHEDULE NO 7.4: INSTALLATION M10: ALEXANDER BAY LPoE - CONVENTIONAL FIRE FIGHTING EQUIPMENT**

						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1000.00	MAINTENANCE OF CONVENTIONAL FIRE FIGHTING EQUIPMENT				
	1001.00	Maintenance of a completed installation				
		.01 Fire Fighting Equipment	Point	360		
		The maintenance scope is described in technical specifications:				
	1002.00	Payment reduction:				
		.01 Payment Reduction due to exceeding of maximum allowable down-time during Emergency Breakdown	Day	-	-R 1,000.00	Rate only
		.02 Payment Reduction due to exceeding of maximum allowable down-time during Ordinary Breakdown	Day	-	-R 200.00	Rate only
		.03 Payment Reduction due to exceeding of maximum allowable down-time during Malicious Damage Repair	Day	-	-R 200.00	Rate only
		.04 Call-out for repair of Emergency Breakdown (24 hours) response	No	-	-	Rate only
	1003.00	Mandatory periodical Servicing and Cleaning not included in preventative maintenance items listed above				
		.01 Statutory annual servicing of 9kg, 4.5kg DCP and 5kg 2,5kg CO ₂ Fire extinguishers Cabinets (Number of times over 3 years : (3))	No	18		
		.02 Statutory annual servicing of 5kg CO ₂ Fire extinguishers (Number of times over 3 years : (3))	No	15		
		.03 Statutory annual servicing of 9kg DCP Fire extinguishers (Number of times over 3 years : (3))	No	16		
		.05 Fire Fighting Equipment Training	hrs	8		
TOTAL - CARRIED TO MAINTENANCE SUMMARY: SCHEDULE NO 7.4: INSTALLATION M10:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 7.5: INSTALLATION M11: VIOOLSDRIFT LPoE- CONVENTIONAL FIRE FIGHTING EQUIPMENT						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1100.00	MAINTENANCE OF CONVENTIONAL FIRE FIGHTING EQUIPMENT				
	1101.00	Maintenance of a completed installation				
		.01 Fire Fighting Equipment and Fire Detection System	Point	360		
		The maintenance scope is described in technical specifications:				
	1102.00	Payment reduction:				
		.01 Payment Reduction due to exceeding of maximum allowable down-time during Emergency Breakdown	Day	-	-R 1,000.00	Rate only
		.02 Payment Reduction due to exceeding of maximum allowable down-time during Ordinary Breakdown	Day	-	-R 100.00	Rate only
		.03 Payment Reduction due to exceeding of maximum allowable down-time during Malicious Damage Repair	Day	-	-R 100.00	Rate only
		.04 Call-out for repair of Emergency Breakdown (24 hours) response	No	-	-	Rate only
	1103.00	Mandatory periodical Servicing and Cleaning not included in preventative maintenance items listed above				
		.01 Statutory annual servicing of 4.5kg DCP Fire extinguishers (Number of times over 3 years : (3))	No	210		
		.02 Statutory annual servicing of 5kg CO ₂ Fire extinguishers (Number of times over 3 years : (3))	No	18		
		.03 Statutory annual servicing of 9kg DCP Fire extinguishers (Number of times over 3 years : (3))	No	205		
		.04 Statutory annual servicing of 2,5kg CO ₂ Fire extinguishers (Number of times over 3 years : (3))	No	16		
Carried forward						

SCHEDULE NO 7.5: INSTALLATION M11: VIOOLSDRIFT LPoE- CONVENTIONAL FIRE FIGHTING EQUIPMENT

SCHEDULE NO 7.5: INSTALLATION M11: VIOOLSDRIFT LPoE- CONVENTIONAL FIRE FIGHTING EQUIPMENT						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
Brought forward						
	1103.00	.05 Statutory annual servicing of Fire hydrants (Number of times over 3 years : (3))	No	12		
		.06 Statutory annual servicing of 30m long, 25mm diameter Fire hose-reels (Number of times over 3 years : (3))	No	17		
		.07 Statutory annual servicing and testing of Fire booster pump system. (Number of times over 3 years : (3))	No	3		
		.08 Statutory annual testing and servicing of Fire detection system inclusive of Fire Panel and smoke detectors, sounders, call points, control panel etc: for Period of Three(3).	No	3		
		.09 Fire Fighting Equipment Training	hrs	12		
	1104.00	GENERAL INFORMATION LOGGING AND RECORDING FOR PORT OF ENTRY				
		Logging and recording of operating conditions, maintenance visits, samples, inspections, surveys, tests etc.: as per technical specification				
		.01 Conventional fire fighting equipment (Number of times over 3 years : (3))	Sum	1		
		Update all as build information and locations of assets				
		.02 Labeling of all conventional fire fighting equipment with identifying tags and recording of details (Number of times over 3 years : (3))	Sum	1		
TOTAL - CARRIED TO MAINTENANCE SUMMARY: SCHEDULE NO 11: INSTALLATION M11:						

DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE

TENDER NO. H25/008 AI

LAND PORTS OF ENTRY: ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS APPOINTMENT OF SERVICE FOR THE 36 MONTHS REPAIR, MAINTENANCE AND SERVICING OF BUILDINGS, CIVIL, MECHANICAL AND ELECTRICAL INFRASTRUCTURE AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

BILL OF QUANTITIES

NB TENDERERS MUST COMPLETE THE BILL OF QUANTITIES IN BLACK INK

SCHEDULE NO 7.6: INSTALLATION M12: ONSEEPKANS LPoE - CONVENTIONAL FIRE FIGHTING EQUIPMENT						MECHANICAL MAINTENANCE WORK
PAYMENT REFERS TO	ITEM NO	DESCRIPTION	UNIT	QUANTITY	RATE	AMOUNT
	1200.00	MAINTENANCE OF CONVENTIONAL FIRE FIGHTING EQUIPMENT				
	1201.00	Maintenance of a completed installation				
		.01 Fire Fighting Equipment	Point	360		
		The maintenance scope is described in technical specifications:				
	1202.00	Payment reduction:				
		.01 Payment Reduction due to exceeding of maximum allowable down-time during Emergency Breakdown	Day	-	-R 1,000.00	Rate only
		.02 Payment Reduction due to exceeding of maximum allowable down-time during Ordinary Breakdown	Day	-	-R 100.00	Rate only
		.03 Payment Reduction due to exceeding of maximum allowable down-time during Malicious Damage Repair	Day	-	-R 100.00	Rate only
		.04 Call-out for repair of Emergency Breakdown (24 hours) response	No	-	-	Rate only
	1203.00	Mandatory periodical Servicing and Cleaning not included in preventative maintenance items listed above				
		.01 Statutory annual servicing of 4.5kg DCP Fire extinguishers (Number of times over 3 years : (3))	No	8		
		.02 Statutory annual servicing of 5kg CO ₂ Fire extinguishers (Number of times over 3 years : (3))	No	6		
		.03 Statutory annual servicing of 9kg DCP Fire extinguishers (Number of times over 3 years : (3))	No	10		
		.04 Statutory annual servicing of 2,5kg CO ₂ Fire extinguishers (Number of times over 3 years : (3))	No	4		
		.05 Fire Fighting Equipment Training	hrs	6		
TOTAL - CARRIED TO MAINTENANCE SUMMARY: SCHEDULE NO 7.6: INSTALLATION M12:						

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

PART C3 SCOPE OF WORK

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

C3.1 SCOPE OF WORK – GCC 2015 3rd Edition

PG-01.1 (EC) SCOPE OF WORKS – GCC 3rd Edition (2015)

Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)		
Tender no:	<i>H25/008 AI</i>	Reference no:	<i>WCS 056397</i>

C3. Scope of Works

CONTENTS

C3.1 STANDARD SPECIFICATIONS

C3.2 PROJECT SPECIFICATIONS

A: GENERAL

- PS-1 PROJECT DESCRIPTION
- PS-2 DESCRIPTION OF SITE AND ACCESS
- PS-3 DETAILS OF CONTRACT
- PS-4 CONSTRUCTION AND MANAGEMENT REQUIREMENTS
- PS-5 CONSTRUCTION PROGRAMME
- PS-6 SITE FACILITIES AVAILABLE
- PS-7 SITE FACILITIES REQUIRED
- PS-8 REQUIREMENTS FOR ACCOMMODATION OF TRAFFIC
- PS-9 OCCUPATIONAL HEALTH AND SAFETY
- PS-10 ADVERSE WEATHER CONDITIONS
- PS-11 FEATURES REQUIRED SPECIAL ATTENTION
- PS-12 CERTIFICATES OF PAYMENT
- PS-13 CONSTRUCTION IN RESTRICTED AREAS
- PS-14 DRAWINGS
- PS-15 LEGISLATION
- PS-16 INSURANCE AMOUNTS
- PS-17 TIMES FOR COMPLETION
- PS-18 PRACTICAL COMPLETION
- PS-19 PENALTIES
- PS-20 NON-WORKING DAYS AND HOURS

B: AMENDMENTS TO THE PARTICULAR SPECIFICATIONS

Variations and additions to the following SANS 1200 Standardised Specifications:

SANS 1200 A : General
SANS 1200 AB : Engineer's office

C3.3 PARTICULAR SPECIFICATIONS

A: TECHNICAL SPECIFICATIONS

AA Plumbing and drainage Installations
AB Building electrical installations
BA Roof Coverings
BB Carpentry joinery for roofs and ceilings
BC Waterproofing of concrete roofs
BD Walls
BE Floors
BF Pest Control
BH Fittings
BJ Paintwork
BK Structural Concrete
CA Roads
CB Storm water drainage
CC Fencing and gates
CE Water distribution networks
CF Sewer networks
CG Solid waste management
CJ Site keeping and cleaning
DA Borehole pump system
DC Borehole siting and drilling
DF Portable water disinfection and sedimentation units
DH Operation of portable water works
DL Chlorination systems for the disinfection of drinking water at remote borehole installations
DW Water supply
EA Waste water inlet works
EB Waste water pump systems
EF Sludge treatment and disposal
EG Septic tank and conservancy tanks and disposal fields
EJ Water quality testing
EK Valves and sluice gates for water treatment plants
EM Operation of waste water works
FD Heating ventilation and air-conditioning systems
FF Kitchen equipment installations
FN Clear water pump systems
HA Medium and low voltage switch gear systems
HB Standby power systems
HC Low voltage reticulation
HD Substation transformers
HE Exterior lighting installations
JC Conventional fire-fighting equipment
KA Water audit

B: PARTICULAR SPECIFICATIONS

PAA Plumbing and drainage installations
PFD Heating Ventilation and Air-conditioning systems
PJC Conventional Fire Fighting Equipment

CE: ADDITIONAL SPECIFICATIONS

SA General Maintenance
SB Operating and Maintenance Manuals

SC	General decommissioning, testing and commissioning procedures
SD	General Training
SF	General Operation
SH	HIV / AIDS requirements (PW1544)
SI	Occupational Health and Safety
SN	Implementation of Labour-intensive infrastructure projects under the Expanded Public Works Programme (EPWP)
SL	Employment and training of youth worker on the expanded public works programme (EPWP) infrastructure projects: national youth service (NYS).

C3.4 STANDARD SPECIFICATIONS:

The standard specifications on which this contract is based are the **South African Bureau of Standards Standardized Specifications for Civil Engineering Construction SABS 1200**. *(Note to compiler. "SABS" has been changed to "SANS"; the SABS 1200 specifications are due to be replaced in the foreseeable future by SANS 2100)*

Although not bound in nor issued with this Document, the following Sections of the Standardized Specifications of SABS 1200 shall form part of this Contract:

1. SABS 1200 - Standardised Specifications for Civil Engineering Construction*
2. SABS - Standard Specifications*
3. PW 371 - Specification of Materials and Methods to be used. Fourth revision, October 1993.**
4. Guide for architects concerning drainage, water supply and storm water drainage**
5. PW 343- Building specifications for Regional Offices**
6. Standard Specification for the Electrical Equipment and Installation for Mechanical Services, Issue VIII December 1984**
7. Standard Electrical Specifications, January 1984, GPS 24-0367**
8. SANS 10400 - The application of the National Building Regulations**
9. Department of Public Works - Standard Electrical Specifications**
10. Standard Specifications for Air Conditioning and Ventilation Installations – Issue XI, 1998**
11. Standard Specifications for Refrigeration Services – Issue VII, 1998**
12. FPO/G61/3E Guide for Architects**
13. Department of Water Affairs – Green Drop * Blue Drop Requirements (Version 1.0-2010) **
14. Guideline for the Implementation of Labour – Intensive Infrastructure Projects under Expanded Public Works Programme**

* Not issued with this document, but available at the Contractor's expense from SA Bureau of Standards, Private Bag X191, Pretoria, 0001.

** Not issued with this document, but available from the Director General, Department of Public Works, Private Bag X65, Pretoria, 0001, or any office of the Regional Representative of this Department

*** Not issued with this document, but available from the Department of Water Affairs (www.dwa.gov.za)

3.5 PROJECT SPECIFICATIONS:

Status

The Project Specification, consisting of two parts, forms an integral part of the contract and supplements the Standard Specifications.

Part1 A contains a general description of the works, the site and the requirements to be met.

Part B contains variations, amendments and additions to the Standardized Specifications and, if applicable, the Particular Specifications.

In the event of any discrepancy between a part or parts of the Standardised of Particular Specifications and the Project Specification, the Project Specification shall take precedence. In the event of a discrepancy between the specifications, (including the Project Specifications) and the drawings and / or the Bill of Quantities, the discrepancy shall be resolved by the Engineer before the execution of the work under the relevant item.

3.5.1 GENERAL

PS-1 PROJECT DESCRIPTION:

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)

Each installation requires work that may include any one or more of the activities as set out in clause PS3 below: i.e. decommissioning, repair, reconditioning, testing, re-commissioning and maintenance during the 36-month Contract. The work also include compilation of operating and maintenance manuals as well as training of User Client operators and all maintenance personnel.

Labour intensive practices under the Expanded Public Works Programme (EPWP) shall be implemented to a value of not less than 10% of the tendered Contract amount for wages paid to local labour.

NOTE: Repair and maintenance work will be carried out within facilities that are occupied by User Client's personnel and associates.

PS 2 DESCRIPTION OF SITE AND ACCESS

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS Land Ports of Entry is the property of the Department of Public Works. The location of the sites are described below:

ALEXANDEY BAY Land Ports of Entry is situated on the border between South Africa and Namibia. The Port of Entry is approximately 227 km from Springbok.

VIOOLSDRIFT Land Ports of Entry is situated on the border between South Africa and Namibia. The Port of Entry is approximately 115 km from Springbok.

ONSEEPKANS Land Ports of Entry is situated on the border between South Africa and Namibia. The Port of Entry is approximately 215 km from Springbok.

The contractor will be granted access to all the installations that need to be repaired and maintained at the date of site handover. Access will be given to completed installations that were kept in a working condition during a previous similar Contract.

PS 3 DETAILS OF THE CONTRACT

All work forming part of this Contract is divided into installations. The work to be performed as part of an installation under this Contract mainly consists of the following:

1. The various installations at the Land Ports of Entry form part of the new Repair and Maintenance Programme.
2. The full Maintenance from the inception of the Contract on all facilities, buildings, installations, infrastructure and equipment regardless of any other repair related works that may occur during the Contract Period.
3. No distinction will be made between prior to practical completion and completed installations for the purpose of maintenance.

4. The Contractor will have the opportunity at the start of the contract to point out items which are not in a perfect working order by means of an assessment and verification report. The Contractor must submit a written report of these items within 28 days of the date of site hand over. Failing to submit the report **within the allowed time will render any and all defective items part of the Contractor's maintenance responsibility as set out in the relevant Technical and Particular Specifications.**
5. Typically the following installations shall be assessed:
- Structural and Building related works
 - Plumbing, drainage and wet services
 - Fencing, cleaning and site keeping
 - Bulk water and external water reticulation and water purification works
 - Roads and storm water drainage
 - Building electrical
 - External lighting
 - Standby power generators
 - Medium and low voltage equipment
 - Heating, ventilation and air-conditioning systems
 - Conventional firefighting equipment

These items will be serviced and repaired as per the relevant tendered rates. The detail Assessment and Verification report shall provide an overview of problem areas at the beginning of the contract period. This shall include testing of all equipment as well as all civil, electrical and mechanical services. The detail Assessment and Verification report shall include photos with a description of problem areas.

The Assessment and Verification report must be submitted one calendar month after site handover. A penalty of R 500 per day shall be imposed for late submission.

Payment for the Assessment and Verification report shall be included in the fixed preliminary and general charges.

6. The contractor will further more at the start of the contract perform annual maintenance on all the installations as specified in the BOQ, as part of the Contractor' maintenance obligation.
7. Maintenance will be the responsibility of the contractor and will be evaluated on a monthly basis by the Engineer. The remuneration for maintenance work and responsibilities will be certified accordingly
8. The description of the Works given below is not necessarily complete and shall not limit the work to be carried out by the Contractor under this Contract. Work measured in the bills of quantities serves as a guide on work expected to be done. **Work will only be executed upon a site instruction issued by the consultants.**

PS 3.1 GENERAL ITEMS

- Compile and supply a complete site plan of Alexander Bay, Vioolsdrift and Onseepkans Land ports of Entry Operational and Residential Areas
- Compliance with the Occupational Health and Safety Act and Construction Regulations 2014 and monthly audits.
- Updating of existing Land Ports of Entry Key Plans
- HIV / Aids Awareness campaigns and training including awareness workshops and awareness campaigns. Also included is the provision of condoms, posters, booklets, videos, etc. and monthly reporting.
- Site recordkeeping based on the maintenance control plan.
- Consumption monitoring (Electrical and Water)
- BMA Contingency infrastructure (provision of Easter and Christmas season facilities) and any peak season as identified by the client.
- Utilisation of a National Call Centre enabling the user departments to report breakdowns.

- Expanded Public Works Programme (EPWP): Implementation of labour intensive practices under the Expanded Public Works Programme (EPWP) to a value of not less than 10% of the tendered contract amount for wages paid to local labour.

PS 3.1.1 Repair and Servicing items in the contract includes:

- Building Structural Elements (Repair actions required to damages and deteriorated elements such as minor touch-up, painting to corroded elements and repair and realignment of locksets, doors, windows, gutters, roofs, etc.). Replacement of damaged floor coverings.
- Water-proofing of concrete roofs.
- Plumbing and Drainage (servicing of sanitary fittings, valves and taps, replacement of damaged/missing components)
- Electrical Installations (servicing of Distribution Boards, Luminaires, Light switches, socket outlets and geyser components as well as Bulk lamp replacement and statutory tests required). Issuing C.O.C's for all buildings.
- Fencing (clearing of fence route, retightening of fence elements, replacement of damaged fences and redressing existing fences)
- Refuse removal (removal of collected refuse from site to registered dumping site)
- Pest Control (Internal and External Termite and Rodent control and preventative measures)
- Water Distribution Networks (servicing and recalibration of water meters and valves, scouring of water pipelines, cleaning of manholes, cleaning of chambers as well as the sterilisation of water reservoirs and repair/service of water treatment package plant)
- Pumping equipment (servicing/reconditioning of water pumps) and reporting.
- Conformation to water standards (testing of water quality)
- Water Audit including compilation of database, meter management system and data loggers for essential services
- Statutory Registration of Water use & Blue Drop / Green Drop Requirements
- Roads (grading of gravel roads, replacement of washed-out jointing sand, repair of interlocking paving sections, repair to road markings and chemical control of vegetation, concrete repair). Installation of embankment-stabilisation Léffe/stein retaining blocks.
- Storm water (repair of structures and cleaning of drainage channels, inlet- and outlet structures)
- External Electrical (servicing of external lighting luminaires, bulk lamp replacement, servicing of light poles, distribution kiosks and overhead distribution system). Replace damaged luminaires with new LED-type luminaires.
- Standby Power Generators (mandatory generator services as per the manufacturers specifications, testing, cleaning, and supply of diesel)
- Replacement of 4 Generators, which has reached the end of serviceable lifetime.
- Air-Conditioning Units (full servicing of units, testing and cleaning of Air-Conditioning units). Replacement of out-dated units, which has reached the end of serviceable lifetime.
- Fire Fighting (statutory servicing, cleaning and recharging equipment as well as firefighting training and a fire plan for each of the service buildings).
- Water Treatment Works (Servicing of pumps, supply of chemicals, filters and silica sand and ensure maintenance of all valves, filters, sand filters, electrical equipment, pumps and motors).
- Waste Water Treatment Works (Service Huber Inlet, Service all Valves and flow measuring devices, replace drying bed sand, cut reed beds, etc.)

PS 3.1.2 Preventative Maintenance items in the contract includes:

The maintenance actions (Additional Specifications) of the following items as per specification SA: Maintenance and Servicing, to be measured monthly as per the performance indicators on the Maintenance Scorecards:

- Plumbing and Drainage
- Electrical Installations
- Fencing, Refuse Removal and Pest Control

- Cleaning and Site Keeping
- External Water and Sewer Networks
- Roads and Storm water Drainage
- External lighting and Standby Power
- Heating, Ventilation and Air-Conditioning Systems
- Fire Fighting Equipment
- Sewer and Water Treatment Plants

PS 3.2 Periodic / Routine Maintenance tasks and Servicing in the contract includes:

- Log all water meter readings and calculate losses on a monthly basis and report in the prescribed format.
- Maintain and operate water purification plant to produce potable water in accordance with Blue Drop Specification.
- Sample potable water supply and chemical analyses to be provided by an accredited laboratory on a monthly basis.
- Log all electricity meter readings on a monthly basis and report in the prescribed format.
- Monitoring of essential services.
- Remove and empty waste from skip to external waste disposal site on a regular basis.
- De-sludge and cleaning of septic tanks on a regular basis as required.
- Sample wastewater effluent and chemical analyses to be provided by an accredited laboratory on a monthly basis – operate wastewater inlet works in accordance with Green Drop Specification.
- Service submersible pumps annually.
- Statutory annual servicing of fire extinguishers.
- Pest and vermin control (internal and external).
- Providing diesel for standby generators for the duration of the contract to ensure that standby power is available at all times and mandatory periodical servicing of Standby Generators. Servicing generators every 200 running hours.
- Site keeping and cleaning of the Ports of Entry.
- Supply of potable drinking water in case of water shortages.
- Cleaning of Administration Buildings and Public Ablutions on a daily basis.
- Water and waste water quality tests.
- Supply of consumables for ablutions.
- Annual servicing of all air-conditioning units.

Maintenance of each of the above installations will be the responsibility of the Contractor and will be evaluated on a monthly basis by the Engineer. The remuneration for maintenance work and responsibilities will be certified accordingly.

PS 3.3 DEPARTMENT OF WATER AND SANITATION INCENTIVE BASED REGULATION MANAGEMENT AND ADMINISTRATION

- Potable water quality tests to be performed by approved SANAS laboratory on a monthly basis on the water delivered to the consumers for determinants specified.
- Potable water quality tests to be performed by an approved SANAS laboratory on a monthly basis on the water abstracted from boreholes for determinants specified.
- Sewage effluent compliance quality tests to be performed by an approved SANAS laboratory for determinants specified.
- Raw sewage 24 h composite sample and analysis for determinants specified.
- Special testing required by the engineer shall include remuneration for all water and wastewater related analysis, in terms of either compliance monitoring, or required to determine risks. All operational sampling and monitoring shall be the Contractor's responsibility remunerated under Operation of an Installation.
- Full SANS 241 (Part 1) set of 34 x chemical, 8 x physical determinants and 6 x micro biological determinants for annual water quality risk assessment.
- Compile and submit to the Engineer for approval a Water Safety Plan in terms of the requirements of SANS 241 (Part 2), inclusive of risk based operational – and compliance monitoring programmes. Water demand management, including loss reduction and water use efficiency business plan Compile and submit to the Engineer for approval a Wastewater Risk Abatement Plan, inclusive of risk based operational

- and compliance monitoring programmes, storm/ground water ingress monitoring and control planning.
- Operation as per Technical Specification DH09 comprising Maintain spreadsheet/database with drinking water system process control and maintenance information, including but not limited to: system input volumes, individual water consumption, system pressures, compliance results, operational process control results, chemical consumption, hour meter readings, volt meter readings, ammeter readings, breakdowns, etc., for ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS Land Ports of Entry, and submission to the Client in a format similar to the Department of Water Affairs's incentive based regulation programmes.
- Operation as per Technical Specification EM04.08 comprising Maintain spreadsheet/database with wastewater treatment process control and maintenance information, including but not limited to: raw wastewater flow rates, effluent flow rates, irrigation rates, compliance results, operational process control results, chemical consumption, hour meter readings, volt meter readings, ammeter readings, breakdowns, etc., at ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS Land Ports of Entry, and submission to the client in a format similar to the Department of Water and Sanitation's incentive based regulation programmes

PS 3.4 ROUTINE MAINTENANCE WORK

Maintenance of each of the above installations will be the responsibility of the Contractor and will be evaluated on a monthly basis by the Engineer. The remuneration for maintenance work and responsibilities will be certified accordingly.

Details of the required routine- and preventative maintenance are given in the relevant technical specifications and in Additional Specification SA: General Maintenance.

PS 4 CONSTRUCTION AND MANAGEMENT REQUIREMENTS

The Contractor shall be responsible for minor construction works as part of the corrective maintenance, as set out in the Bill of Quantities and as per relevant specification. The Contractor shall be responsible for all management to do work as indicated in SANS 1200 A.

PS 5 CONSTRUCTION PROGRAMME

When drawing up his construction programme, the Contractor shall take into account the time for completion for the repair work of each installation as indicated in Clause 42.1 as amended in Part 1 of the Contract Data.

- Repair Work – 12 months
- Maintenance Work – 36 months

If the programme submitted by the Contractor in terms of Clause 12 of the General Conditions of Contract, has to be revised because the Contractor is falling behind in his programme, he shall submit a revised programme of how he intends to regain lost time to ensure practical completion of repair work of each installation, and completion of the Works within the periods stipulated Part 1 of the Contract Data or within a granted extension of time and also to ensure that other contractors have access to the site to start their work on the dates as shown in the original programme. Proposals to increase the tempo of work must incorporate positive steps to increase production either by more labour and plant on the Site, or by using the available labour and plant in a more efficient manner.

Instructions by the Engineer to expedite progress shall not be the subject of additional compensation to the Contractor unless the instruction explicitly states that the Contractor is entitled to additional compensation and cites the amount of such compensation or the basis on which it is to be determined.

Failure on the part of the Contractor to submit or to work according to the programme or revised programmes shall be sufficient reason for the Engineer to take steps as set out in Clause 55 of the General Conditions of Contract as amended in Part 1 of the Contract Data.

The approval by the Engineer of a programme shall have no contractual significance other than that the Engineer will be satisfied if the work is carried out according to the programme. The said approval

shall not limit the right of the Engineer to instruct the Contractor to vary the programme if necessary. The Contractor is also referred to Clause PS 8 and Clause PS 12 when preparing this programme.

NOTE: For reasons of limited access, it may not be possible to carry out the repair work on some of the installations in parallel with repair work on other installations. The repair work of some of the installations shall follow sequentially as indicated in the specifications.

The Contractor shall organise his work in such a manner as to cause the minimum inconvenience to the User Client's personnel and operations.

PS 6 SITE FACILITIES AVAILABLE

PS 6.1 CAMP SITE AND STORE ROOM

(a) Campsite

A site establishment area is available and will be indicated to the Contractor. An area for the campsite was developed by the previous contractor and the infrastructure and facilities can be utilised for the new contract but must be repaired and maintained during the contract to ensure that the facility maintains an esthetical value for the ports of Entry.

(b) Store Room

None of the existing service buildings may be used for storage. The contractor must provide his own store room facilities for the duration of the contract.

The existing and new facilities must comply with the South African National Building Regulations and Standards in all aspects.

PS 6.2 WATER, ELECTRICITY AND SEWERAGE

(a) Water supply

The Contractor must make his own arrangements for water supply. Water will be available at specific points not necessarily adjacent to working areas. Water will be available free of charge but wastage will not be tolerated. The Contractor must supply his own standard fittings to couple up at the points where water is available.

(b) Electrical power supply

Electrical power supply is available on the Site and will be free of charge. The Contractor must make his own arrangements for a connection to the electrical power supply. The Contractor will be responsible, at his own cost, for the distribution of electricity for construction and domestic use.

(c) Sewerage connection

Refer to Sub clause PSA 4.2 in connection with toilet requirements. Chemical toilets shall be used.

Note: The Employer shall not be held responsible for any losses or inconvenience due to a disruption in the supply of water and/or electricity.

PS 6.3 PARKING FACILITIES

Parking facilities are available on site.

PS 7 SITE FACILITIES REQUIRED FOR THE ENGINEER

PS 7.1 GENERAL

The Contractor shall provide on the Site, for the duration of the repair phase and for the exclusive use of the Engineer and/or his Representative (as applicable), the various facilities described hereunder. The duration of the repair phase is stated in Part 1 of the Contract Data. All such facilities shall be provided promptly on the commencement of the Contract and failure on the part of the Contractor to provide any facility required in terms of this specification shall constitute grounds for the Engineer to withhold payment of the Contractor's Preliminary and General items until the facility has been provided or restored, as the case may be.

PS 7.2 OFFICE ACCOMMODATION

The Contractor shall provide on Site, 1(one) office for the exclusive use of the Engineer. Such office shall comply with and be furnished in accordance with the requirements of Sub clause 3.2 of SABS 1200 AB. The Contractor shall maintain the offices in accordance with the requirements of Sub clause 5.2 of SABS 1200 AB.

Irrespective the type of material of which an office is constructed, the Contractor shall ensure that the temperature inside the office is always between 20°C and 24°C.

Such office accommodation shall be provided within the Contractor's site establishment facilities.

PS 7.3 CARPORTS

The Contractor shall provide on Site 1 carport for the exclusive use of the Engineer, in accordance with requirements of Sub clause PSAB 3.3 of the Project Specifications.

PS 7.4 SITE MEETING VENUE

The Contractor shall provide within its own site establishment facilities, a suitably furnished office or other venue capable of comfortably accommodating a minimum of six (6) persons at site meetings. The Engineer shall be allowed free use of such venue for conducting any other meetings concerning the Contract at all reasonable times.

PS 7.5 TELEPHONE AND COMPUTER FACILITIES

The Contractor shall, in accordance with the requirements of Sub clause PSAB 4 of the Project Specifications provide one (1) Cellular phone and one (1) 20GB/month (data— only) LTE13G Wi-Fi-Router and one (1) computer for the duration of the contract for the use of the Engineer and his representative. The average call cost at business rates (over the 36 month contract period) shall not exceed R 1,100-00 per month for the cell phone. 'Roaming' shall be activated on the cellular telephone as local cellular network reception is not available at all sites.

PS 7.7 CALL CENTRE

A call centre has been established by the Employer to log, route and monitor incoming breakdown calls.

The call centre is administered centrally and is responsible for the routing of breakdown calls on The Contractor shall be responsible for the fixed and variable call costs incurred by the call centre for a relevant contract. The Contractor shall be re-reimbursed from an amount included in the Bill of Quantities, on written instruction of the Engineer. Operating costs of the call centre will be calculated, based on the number of breakdowns logged per contract, and invoiced on a monthly basis.

The Contractor is entitled to a percentage of the value of each payment in relation to the call centre to cover his expenses in this regard (see payment item PSA 8.9).

PS 8 REQUIREMENTS FOR ACCOMMODATION OF TRAFFIC

Requirements for the accommodation of traffic shall be in accordance with Clause 8.1 of the GCC (2015). Where road surfaces and other components of roads are repaired, the Contractor shall plan his work in such a way that existing traffic volumes are accommodated on the same road until work is complete. No service roads shall be constructed for purposes of accommodation of traffic during corrective maintenance,

PS 9 OCCUPATIONAL HEALTH AND SAFETY

The Contractor shall be required to comply with the Occupational Health and Safety Act 85 of 1993, Construction Regulations 2014 and related regulations. Non-compliance with these regulations, in any way whatsoever, will be adequate reason for suspending the Works.

The proposed type of work, materials to be used and hazards likely to be encountered on this Contract are detailed in the Scope of Work, Pricing Data and Drawings. The Employers' health and safety specifications (sub clause 5(1) (b)) of the regulations will be issued separately.

The Contractor shall in terms of sub clause 7(1) (a) provide a comprehensive health and safety plan detailing his proposed compliance with the regulations, for approval by the Employer.

The Contractor shall at all times be responsible for full compliance with the approved plan as well as the Construction Regulations and no extension of time will be considered for delays due to noncompliance with the abovementioned plan or regulations.

A payment item is included in the Bill of Quantities to cover the Contractor's cost for compliance with the Occupational Health and Safety Act 85 of 1993, Construction Regulations 2014 and related regulations, as stated above.

Access to the Works will be given after OHS Plan is approved.

PS 10 ADVERSE WEATHER CONDITIONS

Adverse weather conditions shall be managed in terms of additional Clause 2.2, included in the Contract Data.

The statement to be submitted by the Contractor in terms of Clause 49 of the General Conditions of Contract shall be prepared in accordance with the standard payment certificate prescribed by the Engineer and shall comprise at least two sets of A4-size paper copies.

All costs for the preparation and submission of the statements shall be borne by the Contractor.

PS 11 FEATURES REQUIRING SPECIAL ATTENTION

PS 11.1 INSTALLATIONS AT FACILITIES

The installations at all facilities shall be carefully checked for damage and all damages shall be listed and discussed with the Engineer before commencement of repair and maintenance work. The Contractor shall present copies of all correspondence in this regard for discussion at the following site meeting.

PS 11.2 SECURITY

(a) Restrictions on movement and limited access

The Contractor's personnel, vehicles and equipment will be restricted to areas of construction only. The Contractor shall comply with any requirements that the Engineer may have in this regard and shall take note that for security reasons the access to some areas, may be limited.

(b) Prohibition on taking of photographs

The Contractor's attention is drawn to the Defence Act, 1957 (Act No 44 of 1957) and the Correctional Services Act, 1998 (Act No 111 of 1998) which clearly state that the taking of photographs is prohibited and that even the possession of a camera on Site is an offence. Permission to take photographs of damaged equipment may be arranged by the Engineer.

(c) Security check on personnel

The Employer may require the Contractor to have his personnel or a certain number of them security-classified, if so required by any competent authority.

In the event of the Employer or any competent authority requiring the removal of a person or persons from the site for security reasons, the Contractor shall do so forthwith and the Contractor shall thereafter ensure that such person or persons are denied access to the site and/or to any documents or information relating to the work. In such circumstances the Contractor shall indemnify the Employer and the Engineer and shall hold the Employer and the Engineer harmless against any and all claims of whatever nature arising.

(d) Access cards to security areas

Should the work fall within a security area, the Contractor must obtain from the Engineer access cards for his security-cleared personnel and employees who work within such an area. The Contractor must comply with any regulations or instructions issued from time to time, concerning the safety of persons and property, by the Department of Correctional Services or SA Police services.

PS 11.3 SITE TO BE KEPT CLEAN

During progress of the work and upon completion thereof, the Site of the Works shall be kept and left in a clean and orderly condition. The Contractor shall store materials and equipment for which he is responsible in an orderly manner, and shall keep the Site free from debris and obstructions.

All redundant materials, rubbish and waste arising from the work must be removed from the Site at the Contractor's cost and the site and buildings left clean and tidy.

PS 11.4 FACILITIES TO OTHER CONTRACTORS

In addition to the requirements of Clause 18 of the General Conditions of Contract the Contractor must make allowances for other Contractors on the Site. This may involve adapting his programme to accommodate the work of other contractors and ensuring access to their sites along prescribed routes over the Site of this Contract.

PS 11.5 SUBCONTRACTORS

In addition to the requirements of Clause 6 of the General Conditions of Contract as amended in Part 1 of the Contract Data, the Contractor shall be responsible for work carried out by subcontractors on his behalf. The Engineer will not liaise directly with such subcontractors. Problems related to payments, programming, workmanship, etc., shall be the responsibility of the Contractor and the subcontractor, and the Engineer will not become involved.

PS 11.6 SABS SPECIFICATIONS AND CODES OF PRACTICE

All reference in this document to South African Bureau of Standards specifications and codes of practice, or any other standard specifications or codes of practice, including National Building Regulations, shall be deemed to be references to the latest issues of such specifications and codes.

PS 11.7 MATERIALS

The monthly payment for materials brought onto the Site will only be applicable for repair work and not for maintenance work.

Unless otherwise instructed in writing by the Engineer, all proprietary materials are to be used, mixed, applied, fixed, etc. strictly in accordance with the manufacturer's recommendations.

PS 11.8 BORROW PITS

There will be no designated borrow pits. The Contractor shall utilise the material on Site or import material from commercial sources.

PS 11.9 PROTECTION OF FURNITURE AND EQUIPMENT

Most of the work to be done inside buildings and occupied houses will be carried out in places where there is furniture and other equipment.

The Contractor shall be responsible for moving the furniture and equipment in order to provide working space for his personnel. The programme shall be drawn up in such a way as to keep the movement of furniture and equipment to the very minimum and the Contractor shall be solely responsible for any damage to furniture or equipment.

PS 11.10 TESTING AND QUALITY CONTROL

The Contractor shall engage the services of an approved independent laboratory or other institution as applicable for quality testing, to ensure that his work complies with the Specifications.

No separate payment will be made for such testing, the cost of which will be deemed to be included in the Contractor's rates bid for the items of work that require testing in accordance with the Specifications.

The onus to produce work that conforms in quality and accuracy of detail to the requirements of the Specifications and Drawings rests with the Contractor, and the Contractor shall, at his own expense, institute a quality-control system and provide experienced engineers, foremen, surveyors, materials technicians, other technicians and technical staff, together with all transport, instruments and equipment to ensure adequate supervision and positive control of the Works at all times.

The cost of supervision and process control, including testing carried out by the Contractor, will be deemed to be included in the rates bid for the related items of work.

The Contractor's attention is drawn to the provisions of the various Specifications regarding the minimum frequency of testing required. The Contractor shall, at his own discretion, increase this frequency where necessary to ensure adequate control.

On completion and submission of every part of the work to the Engineer for examination, the Contractor shall furnish the Engineer with the results of the relevant tests to indicate compliance with the Specifications.

PS 12 CERTIFICATES OF PAYMENT

The statement to be submitted by the Contractor in terms of Clause 6.10.1 of the General Conditions of Contract shall be prepared in accordance with the standard payment certificate prescribed by the Professional Service Provider and shall comprise at least two sets of A4-size paper copies.

The Contractor shall be responsible for payments to all nominated sub-contractors. However, monthly payment certificates to sub-contractors will form part of the main Contractors statements to enable the Professional Service Provider to monitor payments to sub-contractors.

All costs for the preparation and submission of the statements shall be borne by the Contractor.

Monthly report submitted with the statement for payment to the Engineer for compliance to EPWP reporting requirements and CPG reporting requirements. This report shall be submitted in the provided format and electronically (Excel® format) stating the following details for the current month:

- Labour
 - Worker's full name
 - Worker's ID Number
 - Work performed by the worker
 - Rate per hour/day
 - Hours worked
 - Residential address of worker
 - Total paid for month to labour, suppliers and subcontractors
- Local Suppliers
 - Supplier's full name
 - Supplier's company registration certificate
 - Company address
 - Total paid for month to suppliers
 - Copy of invoices and proof of payment for the month
- Local subcontractors
 - Subcontractor's full name
 - Subcontractor's company registration certificate
 - Company address
 - Total paid for month to Subcontractor
 - Copy of invoices and proof of payment for the month

PS 13 CONSTRUCTION IN RESTRICTED AREAS

Working space in certain areas may be restricted. The construction method used in these restricted areas largely depends on the Contractor's Plant. However, the Contractor must note that

measurement and payment will be according to the specified cross-sections and dimensions irrespective of the method used, and that the rates and prices submitted will be deemed to include full compensation for difficulties encountered while working in restricted areas. No extra payment nor any claim for payment due to these difficulties will be considered.

PS 14 DRAWINGS

The Contractor will, in terms of Clause 13 of the General Condition of Contract, be provided free of charge with three paper prints of each drawing issued to him.

All information in the possession of the Contractor that is required by the Engineer's representative to complete the as-built drawings must be submitted to the Engineer's representative before a Certificate of Completion will be issued.

Only figured dimensions shall be used and drawings shall not be scaled unless required by the Engineer. The Engineer will provide the dimensions that may have been omitted from the Drawings.

PS 15 LEGISLATION

(a) Changes in legislation

Reference in the General Conditions of Contract and in any other standard document forming part of this Contract to legislation which has been amended or superseded by other legislation since the most recent publication of such standard document, shall be deemed to be a reference to the amended or replacement legislation.

Such amended or replaced legislation shall be applicable during the Contract Period provided the amendment or replacement occurred more than 28 days before the closing date for bids in terms of Clause 46.4 of the General Conditions of Contract as amended in Part 1 of the Contract Data.

(b) The Occupational Health and Safety Act

The Contractor shall be required to comply with the Occupational Health and Safety Act, 1993: Construction Regulations, 2003 as promulgated in Government Gazette No 25207 and Regulation Gazette No 7721 of 18 July 2003. Non-compliance with these regulations, in any way whatsoever, will be adequate reason for suspending the Works.

The proposed type of work, materials to be used and hazards likely to be encountered on this Contract are detailed in the Scope of Work, Pricing Data and Drawings. The Employers' health and safety specifications (sub clause 4(1)) of the regulations will be issued separately.

The Contractor shall in terms of sub clause 5(1) provide a comprehensive health and safety plan detailing his proposed compliance with the regulations, for approval by the Employer. The Contractor shall at all times be responsible for full compliance with the approved plan as well as the Construction Regulations and no extension of time will be considered for delays due to non-compliance with the abovementioned plan or regulations.

A payment item is included in the Bill of Quantities to cover the Contractor's cost for compliance with the OHS Act and the abovementioned Construction Regulations 2003.

PS 16 INSURANCE AMOUNTS

The amounts for which the Contractor must insure the Works in terms of Clause 35 of Part 1 of the Contract Data are stated in the Agreement.

PS 17 TIMES FOR COMPLETION

Times for completion of repair work to installations as well as the maintenance down-time for different types of breakdowns are given under Clause 5.5.1 of Part 1 of the Contract Data. The time for completion will start on the date of access to an installation.

PS 18 PRACTICAL COMPLETION

(a) The Contractor shall be entitled in terms of Clause 51.1 of the General Conditions of Contract to receive a Certificate of Practical Completion when the Works to be executed under the Contract have been completed to the stage where:

- (i) All materials which are required to be replaced have been replaced and installed to the satisfaction of the Engineer; and
- (ii) All repair works have been completed.

(b) The Engineer shall issue to the Contractor and the Employer a Certificate of Completion in terms of Clause 51.4 of the General Conditions of Contract except where a thirty day commissioning period, as stated in paragraph (c) below, is applicable.

(c) Where indicated at the end of this paragraph, the issuing of a Certificate of Practical Completion for a certain installation will be followed by a thirty day commissioning period. The tasks of the Contractor during the thirty day commissioning period are described in Additional specification SC: General Decommissioning, Testing and Commissioning Procedures. After the completion of the thirty day commissioning period to the satisfaction of the Engineer, a certificate of completion will be issued to the Contractor as described in Clause 51.4 of the General Conditions of Contract.

PS 19 PENALTIES

Penalties in terms of Clause 43.1 of the General Conditions of Contract for late completion of repair work to different installations are given under Clause 43.1 of Part 1 of the Contract Data. Payment reductions for exceeding the maintenance down-time for different types of breakdowns are given under the applicable pay items in the Bill of Quantities for Additional specifications SA: General Maintenance. Penalties will run concurrently where applicable.

(a) Penalty for failing to meet undertakings and/or conditions pertaining to Targeted Procurement for the award of points

If the bid adjudication points awarded to the Contractor are found to be based on incorrect or false information or the conditions pertaining to the award of points are not met and the Contractor fails to substantiate that such failure is due to a reason acceptable to the Employer (as being) beyond the Contractor's control, the Contractor shall be liable for and pay to the Employer, an amount determined in accordance with clause 2 and subject to clause 1 both of the Works Information, Part 2 of the Conditions of Bid.

(b) Payment reduction for non-performance

If the Contractor shall fail to rectify a fatal breakdown, an emergency maintenance breakdown, an ordinary maintenance breakdown and damage breakdown within the time as stipulated in Additional Specifications SA: General Maintenance, the Contractor shall be liable to the Employer for the sum/sums stated in the Bill of Quantities for Additional Specification SA as a payment reduction for every hour/day down-time counting from the hour/day the breakdown was reported to the Contractor until the day it was repaired. These payment reductions will be cumulative and will run concurrently.

Where indicated above that the money will be recovered from the Contractor by means of payment reductions, the fixed negative amounts in the rate column of the Bill of Quantities will be used to reduce payments due to the Contractor.

The imposition of such payment reductions shall not relieve the Contractor from his obligation to complete the Works or from any of his obligations and liabilities under the Contract.

(c) Application of penalties to be accumulative

The imposition of all penalties in terms of this clause shall be accumulative and shall not relieve the Contractor from his obligation to complete the Works or from any of his obligations and liabilities under the Contract.

PS 20 NON-WORKING DAYS AND HOURS

Whenever any special non-working days stated in Clause 1.6 and Clause 38 of Part 1 of the Contract Data fall within the days allowed or stipulated in the Contract in terms of Clause 1.6 of Part 1 of the Contract Data, such special non-working days shall also be excluded from the calculation of the number of working days concerned.

The Contractor shall not work on any statutory public holidays or on any public holidays declared by the Government to be statutory non-working days, except for work related to repair fatal and emergency breakdowns which influences the functionality of any of the installations.

Working hours might be limited and the Contractor shall work in close cooperation with the User Client and Engineer in this regard. Working hours for the different installations are indicated at the end of this clause where applicable.

The Engineer shall be entitled at any time during the Contract, to vary the normal working hours specified in the Bid documents, including increasing or decreasing the total number of hours per day during which the Contractor may execute the Works or specific portions thereof.

If any variation by the Engineer of the normal working hours specified in the Bid Documents should result in an increase or a decrease in the total number of hours per week during which the Contractor is permitted to execute the Works or any particular portions of Works, then the time allowed in the Contract for the completion of the respective part of the Works to which the varied normal working hours apply shall be adjusted proportionately in relation to:

- a) The remaining time allowed for completion of the specific part or parts of the Works; and
- b) The extent of the variation in the total normal working hours per week.

B AMENDMENTS TO THE STANDARD SPECIFICATIONS:

The following variations and additions to the SANS 1200 Standardised Specifications referred to in the last clause of Portion 1 apply to this Contract. The prefix PS indicates an amendment to SANS 1200. The letters and numbers following these prefixes respectively indicate the relevant Standardised Specification and clause number in SANS 1200.

PSA GENERAL

PSA 1 SCOPE

REPLACE SUBCLAUSE 1.1 WITH THE FOLLOWING:

"1.1 This specification covers requirements, principles and responsibilities of a general nature that are normally applicable to all Civil Engineering Contracts, as well as the requirements for the Contractor's establishment on the Site."

PSA 2 INTERPRETATIONS

PSA 2.3 DEFINITIONS

- (a) General

ADD THE FOLLOWING DEFINITIONS:

"General conditions: The General Conditions of Contract specified for use with this Contract, and the Contract Data.

Specified: As specified in the standardised and standard specifications, the Drawings or the Scope of Work.

Permanent Works: as defined in Clause 1.1.17 of the General Conditions of Contract shall for the purpose of this Contract, be regarded as the repair work and maintenance work as defined in Sub clause SA 02.06 of Additional Specification SA: General Maintenance."

- (c) Measurement and payment

REPLACE THE DEFINITIONS FOR "fixed charge", "time-related charge" AND "value related charge" WITH THE FOLLOWING:

"Fixed charge: A charge that is not subject to adjustment on account of variation in the value of the Contract price or the Contract Time of Completion.

Time-related charge: A charge, the amount of which varies in accordance with the Time for Completion of the repair work, adjusted in accordance with the provisions of the Contract.

Value-related charge: A charge, the amount of which varies pro rata with the final value of the measured repair work executed and valued in accordance with the provisions of the Contract."

PSA 2.4 ABBREVIATIONS

(a) Abbreviations relating to standard documents ADD THE FOLLOWING ABBREVIATION:
"CKS: SABS Co-ordinating Specification."

PSA 3 MATERIALS

PSA 3.1 QUALITY

ADD THE FOLLOWING:

"All manufactured materials supplied shall be new materials unless the contrary is specified. All materials specified in accordance with SABS Specifications shall bear the SABS mark, whether so specified or not."

ADD THE FOLLOWING SUBCLAUSE:

PSA 3.3 ORDERING OF MATERIALS

The quantities set out in the Bill of Quantities have been carefully determined from calculations based on data available at the time and should therefore be considered to be approximate quantities only. Before ordering materials of any kind the Contractor shall check with the Engineer whether or not the scope of the work for which the materials are required is likely to change substantially. No liability or responsibility whatsoever shall be attached to the Employer for materials ordered by the Contractor except when ordered in accordance with written confirmation issued by the Engineer."

PSA 4 PLANT

PSA 4.2 CONTRACTOR'S OFFICES, STORES AND SERVICES

ADD THE FOLLOWING PARAGRAPH BEFORE THE FIRST PARAGRAPH:

"The Contractor's construction camp shall be fenced off and shall contain all offices, stores, workshops, testing laboratories, toilet facilities, etc. The camp shall always be kept in a neat and orderly condition. No personnel may reside on the Site. No night-watchman may be on the Site after hours."

ADD THE FOLLOWING TO THE SECOND PARAGRAPH:

"One chemical toilet per 10 workmen shall be provided and must be screened from public view and its use shall be enforced.

The Contractor shall, where applicable, make the necessary arrangements for the removal of night soil."

PSA 5 CONSTRUCTION

PSA 5.4 PROTECTION OF OVERHEAD AND UNDERGROUND SERVICES

REPLACE THE HEADING AND THE CONTENTS OF THIS SUBCLAUSE WITH THE FOLLOWING:

PSA 5.4 LOCATION AND PROTECTION OF EXISTING SERVICES

PSA 5.4.1 Location of existing services

Before underground or excavation work is carried out, the Contractor shall ascertain the presence and position of all services likely to be damaged or interfered with by his activities. He shall obtain up-to-date plans from the Engineer for this purpose, showing the position of services in the area where he intends to work. As services can often not be reliably located from such plans, the Contractor shall determine the exact position of such services by means of suitable detecting equipment and afterwards by careful hand excavation where necessary in order to expose the services at the positions of possible interference by his activities. This procedure shall also be followed in respect of services not shown on the plans but believed to be present.

All such services, the positions of which have been located at the critical points, shall be designated as 'known' services and their positions shall be indicated on a separate set of Drawings, a copy of which shall be furnished to the Engineer.

While he is occupying the Site, the Contractor shall be liable for all damage caused by him to known services as well as for consequential damage, whether caused directly by his operations or by the lack of proper protection.

PSA 5.4.2 Protection during repair and maintenance work

The Contractor shall exercise all the necessary care to prevent damage to known services during repair and maintenance work. Where applicable, major excavating equipment and other Plant shall not be operated dangerously close to these services. Where necessary, excavation in close proximity to these services shall be carefully carried out with suitable hand tools, excluding picks wherever their use could damage the services. No additional payment will apply to such more difficult work. Services left exposed shall be suitably protected from damage.

PSA 5.4.3 Alterations and repairs to existing services

Unless the contrary is clearly specified or ordered, the Contractor shall not carry out alterations to existing services. When this is necessary, the Contractor shall inform the Engineer, who will either make arrangements for such work to be executed by the owner of the service, or instruct the Contractor to make such arrangements himself.

When existing services are damaged by the Contractor, he shall immediately inform the Engineer, or when this is not possible, the relevant authority, and obtain instructions as to who should carry out repairs. In urgent cases the Contractor shall take the necessary steps to minimise damage to and interruption of the service. No repairs of telecommunication cables or electric power lines and cables shall be attempted.

The Employer will accept no liability for damages due to a delay in having such alterations or repairs effected. The Contractor shall provide all reasonable opportunity, access and assistance to persons carrying out alterations or repairs of existing services."

ADD THE FOLLOWING SUBCLAUSE:

PSA 5.9 SITE MEETINGS

The Contractor will be required to attend regular site meetings, normally held once a month to discuss general progress, quality of work, problems, claims, payments, etc., but not matters concerning the day-to-day running of the Contract."

PSA 6 TOLERANCES

ADD THE FOLLOWING SUBCLAUSE:

PSA 6.4 GENERAL

No guarantee is given that the full specified tolerances will be available independently of each other, and the Contractor is cautioned that the liberal or full use of any one or more of the tolerances may deprive him of the full or any use of tolerances relating to other aspects of the work.

Except where the contrary is specified or when clearly not applicable, all quantities for measurement and payment shall be determined from the 'authorised' dimensions. These are specified dimensions or those shown on the Drawings or, if changed, as finally prescribed by the Engineer, without any allowance for the specified tolerances. Except if otherwise specified, all measurements for determining quantities for payment will be based on the 'authorised' dimensions.

If the work is therefore constructed in accordance with the 'authorised' dimensions plus or minus the tolerances allowed, quantities will be based on the 'authorised' dimensions regardless of the actual dimensions to which the work has been constructed.

When the work is not constructed in accordance with the 'authorised' dimensions plus or minus the tolerances allowed, the Engineer may nevertheless, at his sole discretion, accept the work for payment. In such cases no payment shall be made for quantities of work or material in excess of those calculated for the 'authorised' dimensions, and where the actual dimensions are less than the 'authorised' dimensions minus the tolerance allowed, quantities for payment shall be based on the actual dimensions as constructed."

PSA 8 MEASUREMENT AND PAYMENT

PSA 8.1 MEASUREMENT

PSA 8.1.2 Preliminary and general items or section (for repair phase only)

PSA 8.1.2.2 Bid sums

REPLACE THE CONTENTS OF THIS SUBCLAUSE WITH THE FOLLOWING:

"The Contractor's bid sums under items PSA 8.3 and PSA 8.4 shall collectively cover all charges during the repair phase for

- risks, costs and obligations in terms of the General Conditions of Contract, the Contract Data and of this Standardised Specification, except where provision is made in these Project Specifications to cover compensation for any of these items;
- head-office and site overheads and supervision;
- profit and financing costs;
- expenses of a general nature not specifically related to any item or items of permanent or temporary work;
- providing facilities on Site for the Contractor's personnel, including offices, storage facilities, workshops, ablutions, for providing services such as water, electricity, sewerage, sewage and rubbish disposal, for access roads and all other facilities required, as well as for the maintenance and removal on completion of the Works of these facilities and the cleaning-up of the camp site on completion of the Works;
- providing facilities for the Engineer and his staff as specified in SABS 1200 AB and in these Project Specifications"

PSA 8.2 PAYMENT

PSA 8.2.1 Fixed-charge and value-related items

REPLACE THE CONTENTS OF THIS SUBCLAUSE WITH THE FOLLOWING:

"Payment of fixed charges in respect of item 8.3.1 will be made as follows:

Eighty per cent (80%) of the sum bid will be paid when the facilities have been provided and approved. The remaining 20% will be paid when the repair works have been completed, the facilities have been removed and the camp site has been cleared and cleaned.

Payment for the sum bid under item 8.3.2 will be made in three separate instalments as follows:

(a) The first instalment, which is 40% of the sum, will be paid when the Contractor has fulfilled all his obligations to date under this Standardised Specification, the General Conditions of Contract and the Contract Data, and when the value of work certified for payment, excluding materials on Site and payments for preliminary and general items, is equal to not less than 5% of the total value of the repair work listed in the Bills of Quantities.

(b) The second instalment, which is 40% of the sum, will be made when the amount certified for payment, including retention monies but excluding this second instalment, exceeds 50% of the repair work.

(c) The final payment, which is 20% of the sum, will be made when the repair works have been certified as completed and the Contractor has fulfilled all his obligations to date under this Standardised Specification, the General Conditions of Contract and the Contract Data.

Should the value of the measured repair work finally completed be more or less than the Bid Sum for repair work, the sum bid under item 8.3.2 will be adjusted up or down in accordance with the provisions of Clause 50 of the General Conditions of Contract as amended in Part 1 of the Contract Data, and this adjustment will be applied to the third instalment. No adjustment will apply to item 8.3.1 in respect of variations in the value of work done or after the finally authorised Time for Completion."

Note: Payment under item 8.3.2 will only be applicable to repair work.

PSA 8.2.2 Time-related items

REPLACE THE CONTENTS OF THIS SUBCLAUSE WITH THE FOLLOWING:

"Subject to the provisions of Subclasses 8.2.3 and 8.2.4, payment under item 8.4.1 (time- related item) will be made monthly in equal amounts for each installation, calculated by dividing the sum bid for the item by the repair phase period for the installation in months, provided always that the total of the monthly amounts so paid for the item is not out of proportion with the progress of the work on the installation as a whole.

Should the Engineer grant an extension of Time for Completion of the repair works on the installation, the Contractor will be entitled to an increase in the sum bid for the time- related item, which increase shall be in the same proportion to the original sum bid as the extension of time is to the original Time for Completion of the repair works.

Payment of such increased amounts will be deemed full compensation for all additional time-related preliminary and general costs due to the circumstances pertaining to the extension of time granted for an installation. The length of the repair phase for each installation is indicated in Part 1 of the Contract Data.

In the Bills of Quantities separate provision is made for time-related items for each installation individually. Time-related payment for an installation shall only be made when the repair work on the installation is in progress and shall end when the time for completion or an extension of time granted by the Engineer expires. When repair work on more than one installation is in progress, time-related payment will be made for each installation and the conditions as stated above shall apply to each installation individually."

PSA 8.3 BILLED FIXED-CHARGE AND VALUE-RELATED ITEMS

REPLACE THE ITEMS WITH THE FOLLOWING:

PSA 8.3.1 Fixed preliminary and general charges Unit: Sum

PSA 8.3.2 Value-related preliminary and general charges Unit: Sum

The bid sums shall include full compensation for all fixed and value-related preliminary and general charges as described in Sub clause PSA 8.1.2.2. Payment will be made as described in Sub clause PSA 8.2.1."

PSA 8.4 BILLED TIME-RELATED ITEMS

REPLACE THIS ITEM WITH THE FOLLOWING:

PSA 8.3.2 Time-related preliminary and general charges Unit: Month

(a) ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS Land Ports of Entry

The bid sums shall include full compensation for all time-related preliminary and general charges as described in Sub clause PSA 8.1.2.2. Payment will be made as described in Sub clause PSA 8.2.2

Note: The total amount bid for items PSA 8.3.1, PSA 8.3.2 and PSA 8.4.1 shall not exceed 15% of the total amount for repair work, excluding value-added tax.

PSA 8.8 TEMPORARY WORKS

REPLACE ITEM 8.8.4 WITH THE FOLLOWING:

PSA 8.8.4 Location and protection of existing services:

PSA 8.8.4.1 Provision of detecting devices for:

- (a) Water and sewer pipes
- (b) Electrical and other cables

The bid sums shall cover the cost of providing and operating suitable equipment for as long as it is needed to locate all the existing services likely to be affected by the construction activities. Alternatively, an approved specialist firm may be employed to carry out the work.

PSA 8.8.4.2 Hand excavation necessary for locating and exposing existing services in all material:

- (a) In roadways Unit: m3
- (b) In all other areas Unit: m3

The rates shall cover the cost of excavation by means of hand tools within authorised dimensions, for all precautionary measures to protect the services from damage during excavation and backfilling, and for subsequent backfilling and compacting. Compaction of material in all areas except in roadways shall be to 90% of the modified AASTHO density.

The rate for hand excavation in roadways shall include compensation for compacting excavated or selected backfill materials to 93% modified AASTHO density.

The tendered rates shall also include for keeping excavations safe, for dealing with surface and subsurface water, for removing surplus excavated material from Site, for transporting all material, and for supplying adequate supervision during both excavation and backfilling operations.

PSA 8.9 ADDITIONAL TESTS:

- (a) Additional tests required by the Engineer Unit: Sum
- (b) Attendance and profit Unit: %

An amount has been allowed in the Bill of Quantities under sub item (a) to cover the cost of additional tests required by the Engineer. The Engineer will have the sole authority to spend the amount or part thereof.

The bid percentage under sub item (b) will be paid to the Contractor on the value of each payment made to the testing authority.

Note in connection with sub item (a):

The Contractor is responsible for both the cost of normal testing as described in Sub clause PS 8.10 in portion 1 of the Project Specifications and for the cost of any additional test that indicates that the Specifications have not been complied with.

PSA 8.10 SECTIONAL FENCING FOR THE PROTECTION OF THE WORKFORCE **Unit: m**

The bid rate shall include full compensation for the supply, delivery, initial erection and finally removal from the site of the sectional fencing. The cost to move the fencing will not be paid for separately but shall be deemed to be included in the rate bid.

PSA 8.11 MAINTENANCE MATERIAL:

Supply and deliver maintenance material to the site:

- (a) Description of type of service for which material is needed:
- (i) Description of specific material Unit: litre, m², m, number (ii) Etc. for other types of material.
- (b) Etc. for other types of service.

The unit of measurement shall be the litre, square metre, metre or number as applicable to each item ordered on the written instructions of the Engineer.

The bid rates shall include full compensation for supplying and delivering to the maintenance store(s) of the Employer on the Site of the Works each item as billed and shall include for all labour, material, waste and, transport.

A complete book keeping system with delivery notes and order "invoices" shall be kept by the Contractor and the cost thereof shall be deemed to be included in the rates bid for the various items.

The rates bid will be fixed for the full duration of the repair and maintenance phases and shall be applicable to any quantity "ordered" irrespective of size, contents, volume of container or the number. The actual square metre size of the "ordered" items will be calculated to two decimal points for payment purposes. No "rounding-off" to the nearest square metre quantity will be allowed. It is expected that the maintenance material will be ordered in small quantities throughout the duration of the Contract."

PSA 8.12 COMPLIANCE WITH OHS ACT AND CONSTRUCTION REGULATIONS 2003

Unit: sum

The bid sum shall include full compensation to the Contractor for compliance with all the requirements of the OHS Act and the Construction Regulations 2003 at all times during the repair and maintenance phase, as described in PS 13 of Portion 1 of the Project Specifications. The successful bidder shall provide the Engineer with a complete breakdown of this bid sum.

This sum will be paid to the Contractor in equal monthly amounts for the entire duration of the contract period.

PSAB ENGINEER'S OFFICE

PSAB 3 MATERIALS

PSAB 3.1 NAMEBOARDS

REPLACE THE FIRST SENTENCE OF SUB-CLAUSE 3.1 OF SABS 1200AB WITH THE FOLLOWING:

"The Contractor shall supply and erect at locations approved by the Engineer, the number of contract name boards specified in the Project Specifications, which, unless otherwise specified in the Contract, shall comply with the recommendations for the standard board of the South African Association of

Consulting Engineers, with regards to size, painting, decorating and detail, and the requirements described hereunder."

PSAB 3.2 OFFICE BUILDING(S)

REPLACE THE WORDS: "as scheduled" IN PARENTHESIS IN THE FIRST LINE OF SUBCLAUSE 3.2 OF SABS 1200 AB WITH: "as specified in Portion 1 of the Project Specifications";

AND REPLACE SUBCLAUSE 3.2(j) OF SABS 1200 AB WITH THE FOLLOWING:

"(j) A heater and fan / air-conditioning unit both of such capacity that the inside of the office(s) is always at a temperature of between 20°C and 24°C."

ADD THE FOLLOWING SUBCLAUSE IN CLAUSE 3:

PSAB 3.3 CAR-PORT

The Contractor shall construct the number of carports indicated in Portion 1 of the Project Specifications, for the sole use of the Engineer and his staff. Each car-port shall be constructed so that the vehicle parked under it is always protected against the direct rays of the sun. The carport area shall be at least 20 m² and the floor shall be covered with a layer of crushed stone to alleviate dusty and muddy conditions. The carport(s) shall be positioned so as to provide easy and convenient access to the Engineer's office."

PSAB 4 PLANT

PSAB 4.1 TELEPHONE

REPLACE THE WORDS: "Department of Post and Telecommunications" WITH "Telkom" AND ADD THE FOLLOWING AT THE END OF SUBCLAUSE 4.1 OF SABS 1200 AB:

"In addition to a Telkom telephone and subject to satisfactory transmission and reception quality in the vicinity of the Site, the Contractor shall provide the number of cellular telephones and associated service contracts from a reputable cellular service provider, as specified in the Project Specifications, for the exclusive use of the Engineer and his staff."

ADD THE FOLLOWING NEW SUBCLAUSES TO CLAUSE 4 OF SABS 1200 AB:

PSAB 4.3 TELEFAX FACILITIES

No telefax facilities required.

PSAB 4.4 SURVEY EQUIPMENT

No survey equipment is required.

PSAB 5 CONSTRUCTION

PSAB 5.4 TELEPHONE

REPLACE THE CONTENTS OF SUBCLAUSE 5.4 OF SABS 1200 AB WITH THE FOLLOWING:

PSAB 5.4.1 Telkom telephones

The Contractor shall advise Telkom promptly of any faults which develop in the telephone service and shall, in such circumstances, arrange for the earliest possible restoration of the said service. The Contractor shall ensure that the telephone account is promptly paid.

PSAB 5.4.2 Cellular telephones

The Contractor shall advise the cellular service provider of any faults which develop in the cellular telephone service and/or the cellular telephone handsets and shall, in such circumstances, arrange for the earliest possible restoration of the said service.

The costs of any necessary repairs and/or the replacement of components to the handsets of the cellular telephones shall be for the Contractor's account.

The Contractor shall ensure that all accounts for cellular phone calls and the respective service contracts are promptly paid."

ADD THE FOLLOWING NEW SUBCLAUSES TO CLAUSE 5 OF SABS 1200 SB:

PSAB 5.7 TELEFAX FACILITIES

No telefax facilities required.

PSAB 5.8 SURVEY EQUIPMENT

No survey equipment is required.

C3.6 STANDARD MINIMUM REQUIREMENTS

In terms of section 5(2) of the Construction Industry Development Board Act, 2000 (Act no. 38 of 2000) (the Act), the Construction Industry Development Board is empowered to establish and promote best practice standards, Standard Requirements and Guidelines which includes the following but not limited to:

- C3.61 cidb Best Practice: Green Building Certification, No. 34158 Government Gazette, 1 April 2011
- C3.6.2 cidb Standard for Developing Skills through Infrastructure Contracts, No. 36760 Government Gazette, 23 August 2013
- C3.6.3 cidb Standard for Indirect Targeting for Enterprise Development through Construction Works Contracts, No 36190 Government Gazette, 25 February 2013
- C3.6.4 Preferential Procurement Policy Framework Act, 2000: Preferential Procurement Regulations, 2017, No. 40553 Government Gazette, 20 January 2017
- C3.6.5 cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts, No. 41237 Government Gazette, 10 November 2017
- C3.6.6 cidb Standard for Minimum Requirements for Engaging Contractors and Sub-Contractors on Construction Works Contracts, No. 41237 Government Gazette, 10 November 2017
- C3.6.7 cidb Standard for Minimum Requirements for Engaging Contractors and Sub- Contractors on Construction Works Contracts, No. 42021 Government Gazette, 9 November 2018
- C3.6.8 cidb Standard for Developing Skills through Infrastructure Contracts, No. 43495 Government Gazette, 3 July 2020

C3.7 CONTRACT PARTICIPATION GOALS AND CIDB BUILD PROGRAMME

The contractor shall achieve in the performance of the contract the following Contract Participation Goals (CPGs) as indicated below. Provision for pricing of compliance with the achieving the CPGs is made in the Contract Participation Goal Section of the Bills of Quantities and it is explicitly pointed out that all requirements in respect of the aforementioned are deemed to be priced thereunder and no additional claims in this regard shall be entertained:

C3.7.1 Minimum Targeted Local Material Manufacturer Contract Participation Goal

The Minimum Targeted Local Building Material Manufacturers CPG is *applicable* to this project.

It is the requirement of the employer that the contractor enhances the use of local Small, Micro and Medium Enterprise Local Material Manufacturers (SMME's) in executing this contract, irrespective whether a minimum percentage Participation Goals is applicable or not.

The Minimum Targeted Local Manufacturers of Material Contract Participation Goal, in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020.

A Targeted Local Material Manufacturer is a targeted enterprise that operates or maintains a factory or establishment that produces on its premises materials or goods required by the principal contractor for the performance of the contract.

Note: Adapted from SANS 10845-7:2015, definition 2.13

Preference shall be given to the Targeted Local Material Manufacturer where feasible in **ZF Mgcawu District Municipality**, and provided that:

- (a) Such materials comply in all respects with the specific requirements of PW371 and SANS specifications,
- (b) The non-availability of such materials shall not adversely affect the desired progress of the specific works,
- (c) The use of such suppliers shall not constitute grounds for any claim for increased cost in respect thereof,
- (d) Materials of at least **15% (Fifteen Percent)** of the total value of materials purchased excluding VAT to be sourced from within **200km** radius of the project site,
- (e) Materials of at least **15% (Fifteen Percent)** of the total value of materials purchased excluding VAT to be sourced from within **200km** radius of the project site.

Failure to achieve the minimum **15% (Fifteen Percent)** Targeted Local Material Manufacturer participation expressed as a percentage of the original tender amount, excluding allowances and VAT, will result in a **5% (Five Percent)** penalty of the prorated targeted value of materials not complied with unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

The bidder shall submit monthly reports in terms of monthly achievement and accumulative targets achieved including audited supporting documentation to the Employer's Representative.

C3.7.2 Minimum Targeted-Local Building Material Suppliers Contract Participation Goal

The Minimum Targeted Local Building Material Suppliers CPG is applicable to this project.

It is the requirement of the employer that the contractor enhances the use of local Small, Micro and Medium Enterprise Local Material Suppliers (SMME's) in executing this contract, irrespective whether a minimum percentage Participation Goals is applicable or not.

The Minimum Targeted Local Manufacturers of Material Contract Participation Goal shall be achieved in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. 41237 of 10 November 2017, as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract..

A targeted supplier is a targeted enterprise that

- a) owns, operates or maintains a store, warehouse or other establishment in which goods are bought, kept in stock and regularly sold to wholesalers, retailers or the public in the usual course of business; and
- b) engages, as its principal business and in its own name, in the purchase and sale of goods.

Note: Adapted from SANS 10845-7:2015, definition 2.14

Preference shall be given to the local material suppliers where feasible in the **ZF Mgcawu District Municipality**, and provided that:

- (a) Such materials comply in all respects with the specific requirements of PW371 and SANS specifications,
- (b) The none availability of such materials shall not adversely affect the desired progress of the specific works,
- (c) The use of such suppliers shall not constitute grounds for any claim for increased cost in respect thereof,

- (d) Materials of at least **15% (Fifteen Percent)** of the total value of materials purchased excluding VAT to be sourced from within **200km** of the project site,
- (e) Material of at least **15% (Fifteen Percent)** of the total value of materials purchased excluding VAT to be sourced from within **200km** of the project site.

Failure to achieve the minimum **15% (Fifteen Percent)** Targeted Local Material Manufacturer participation expressed as a percentage of the original tender amount, excluding allowances and VAT, will result in a **5% (Five Percent)** penalty of the prorated targeted value of materials not complied with, unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

The bidder shall submit monthly reports in terms of monthly achievement and accumulative targets achieved including audited supporting documentation to the Employer's Representative.

C3.7.3 Minimum Targeted Local Labour Skills Development Contract Participation Goal

The Minimum Targeted Local Labour Skills Development CPG is *applicable* to this project.

It is the requirement of the employer that the contractor enhances the use of local labour in executing this contract. This is required to be done through the use of both traditional building techniques and labour-intensive construction techniques careful and considered construction planning and implemented in the project irrespective whether a minimum percentage Participation Goal is applicable or not.

The Minimum Targeted Local Skills Development Contract Participation Goal shall be achieved in accordance with the cidb Standard for Contract Participation Goals for Targeting Enterprises and Labour through Construction Works Contracts as published in the Government Gazette Notice No. No. 48491 of 28 April 2023 and the cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.

Targeted labour: individuals who:

- a) are employed by the principal contractor, sub-contractor or targeted enterprises in the performance of the contract;
- b) are defined as the target group in the targeting data; and
- c) permanently reside in the target area or who are recognized as being residents of the target area on the basis of identification and association with and recognition by the residents of the target area.

Adapted from SANS 10845-7:2015, definition 2.12

Targeting of labour by skills categories is only permissible within categories of semi-skilled and unskilled labour.

Contract participation goals for semi-skilled and unskilled labour shall be limited to on-the-job training to targeted labour to enable such labour to master the basic work techniques required to undertake the work in accordance with the requirements of the contract and in a manner that does not compromise worker health and safety. In the case of targeted labour, the certification of records shall be in accordance with SANS 10845-8.

Beneficiaries will be sourced from the **Northern Cape Province** for the full duration of the Construction Period, employed by either the principal contractor, sub-contractors or targeted enterprises. The total number of working days to complete the Works amount to **1095** working days. The minimum CPG participation for Targeted Local Labour Skills Development is **5% (Five Percent)**, expressed as a percentage of the total number of working days required to complete the Works. The contractor shall attain or exceed the CPG in the performance of the contract. Failure to achieve the minimum Targeted Local Labour Skills Development CPG will result in a payment reduction of **R5 000** (Excluding VAT), per working day which training has not been provided to the workforce in attendance, unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

The bidder shall submit monthly reports in terms of monthly achievement and accumulative targets achieved including audited supporting documentation to the Employer's Representative.

C3.7.4 CIBD BUILD PROGRAMME: Minimum Targeted Enterprise Development Contract Participation Goal

The Minimum Targeted Enterprise Development CPG is *applicable* to this project.

The aim of this best practice standard for indirect targeting for enterprise development in accordance with the Standard for Indirect Targeting for Enterprise Development (published in Government Gazette 36190 of 25 February 2013), as amended in cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract. is to promote enterprise development by providing for a minimum contract participation goal (CPG) of **five percent (5%)** of the contract amount as defined in the Standard (Tender amount, excluding allowances and VAT on selected contracts to be undertaken by joint-venture partners or to be sub-contracted to developing contractors that are also to be beneficiaries of enterprise development support from the main contractor.

The lead partner or main contractor shall dedicate a **minimum five percent (5%)** of the tender value at the time of award, excluding allowances and VAT, to provide developmental support to targeted subcontractor or joint venture partner applicable to contracts in Grades 7 to 9, General Building and Civil Engineering contracts. Preference will be given to **Civil Engineering, General Building, Electrical and Mechanical** Enterprises.

The contractor shall attain or exceed the enterprise development goal in the performance of the contract. Failing to achieve the Participation Goal will result in A) a thirty percent (30%) penalty of the value not achieved, excluding VAT, unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

The bidder shall submit monthly reports in terms of monthly achievement and accumulative targets achieved including audited supporting documentation to the Employer's Representative.

C3.7.4.1 Criteria

The main or lead partner of the successful bidder shall:

- (a) There must be a needs analysis for indirect targeting and development or skill standard and should be development in at least any two developmental areas namely;
 - Administrative and cost control systems
 - construction management systems and plans
 - planning, tendering and programming
 - business; technical; procurement skills
 - legal compliance
 - credit rating/history; financial loan capacity/history
 - contractual knowledge
- (b) The above needs analysis shall be mutually agreed upon between contractor and targeted enterprise
- (c) The contractor shall appoint an enterprise development coordinator to:
 - perform needs analysis on the targeted enterprise to identify developmental goals
 - develop a project specific enterprise development plan to improve the targeted enterprise/s performance in the identified developmental areas
 - provide internal mentorship support to improve the targeted enterprise/s performance
 - monitor and submit to the employer's representative a monthly enterprise development report thereby reporting on the progress of the agreed development areas with the targeted enterprise/s
 - submit a project completion report to the Employer's representative for each targeted enterprise.

C3.7.4.2 Management

The contractor shall provide a competent person/s to provide internal mentorship to the Targeted Enterprise/s in the two agreed developmental areas.

C3.7.4.3 Competence Criteria for an Enterprise Development Co-ordinator

The enterprise development co-ordinator shall have the following competencies:

- Minimum experience of 5 years in the construction industry at Managerial level as a Site Agent, Contracts Manager, Site Manager, Construction Manager, Business Development Manager or Enterprise Development Manager.
- Minimum experience of 2 years in training and development in Building or Construction; and
- National Diploma or B Degree in the Built Environment or Business Management

C3.7.4.4 Format of Communications

The contractor shall submit to the Employer's Representative:

- *Project interim reports* in the specified format (**ED105P**) detailing interim values of the CPG that was achieved together with an assessment of the enterprise development support provided should be tabled and discussed at least monthly at progress meetings between employer's representative and the contractor;
- *Project completion report* in the specified format (**ED101P**) to the Employer's Representative for acceptance within 15 days of achieving practical completion. The report shall include the value of the CPG that was certified in accordance with the contract, cidb registration numbers of each and every targeted enterprise, and the value of the subcontracted works or of the joint venture entered into; and the participation parameter
- *Enterprise development declaration* (**ED104P**).

C3.7.4.5 The Key Personal

The contractor shall appoint an Enterprise Development Co-ordinator and a competent person/s to provide internal mentorship.

C3.7.4.6 Management Meetings

The contractor shall report to the Employer's Representative on the implementation and progress of the targeted enterprise development and CPG at monthly progress site meetings.

C3.7.4.7 Forms for contract administration

The contractor shall submit to the Employer's Representative the following proformas:

- Form ED 105P Project Interim Report
- Form ED 104P Enterprise Development Declaration
- Form ED 101P Project Completion Report

C3.7.4.8 Records

The contractor shall:

- keep records of the targeted enterprise development
- keep records of the payments made to the targeted enterprises in relation to the CPG.
- ensure all the documentation required in terms of the Standard is provided with each monthly progress payment certificate and according to a prescribed format where applicable.

C3.7.4.9 Payment Certificates

The contractor shall:

- achieve the measurable CPG and providing enterprise development support to the targeted enterprise/s as per the Standard.
- submit payment certificates to the Employer Representative at intervals determined in the Contract.

C3.7.4.10 Compliance requirements

Non-compliance with the Best Practice Project Assessment Scheme

The wording of regulation 27A of the cidb regulations makes provision for the Board to enforce the cidb code of conduct in the event of clients being found to be in breach of the best practice project assessment scheme.

- Not including the requirements of the cidb standards in the conditions of tender
- Not registering the award of contract on the cidb Register of Projects (RoP)
- Not reporting practical completion on the cidb Register of Projects (RoP)

3.7.5 **CIDB BUILD PROGRAMME: Minimum Targeted Contract Skills Development Goal (CSDG)**

The Minimum Targeted Contract Skills Development CPG is *applicable* to this project.

The contractor shall achieve or exceed in the performance of the contract the Contract Skills Development Goal (CSDG) established in the Standard for Developing Skills through Infrastructure Contracts (published in Government Gazette No 48491 of 23 April 2023 and the cidb Best Practice Project Assessment Scheme Notice No. 43726 of 18 September 2020 – Condition of Contract.

Failing to achieve the targeted Contract Skills Development Goal will result in A) a **thirty percent (30%)** penalty of the value of the portion not achieved, excluding VAT, and B) the issuing of completion certificates only after the completion certificate of achieving the skills development goal, counter-signed by the relevant individuals has been submitted, unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

The contractor shall apportion the learners in the different construction activities based on the scope of work. The cost of accommodating learners will be determined by using Table 3 in the Standard and this cost will be used to determine the value in Rand and will be added to the provision for training as provided for in the Preliminary and General section in the Bill of Quantities/Pricing schedules/Activity schedule.

C3.7.5.1 Methodology

The contractor shall achieve the measurable contract skills development goal by providing opportunities to learners requiring structured workplace learning using one or a combination of any of the following in relation to work directly related to the contract or order:

Method 1: structured workplace learning opportunities for learners towards the attainment of a part or a full occupational qualification;

Method 2: structured workplace learning opportunities for apprentices or other artisan learners towards the attainment of a trade qualification leading to a listed trade (GG No. 35625, 31 August 2012) subject to at least sixty percent (60%) of the artisan learners being holders of public TVET college qualifications;

Method 3: work integrated learning opportunities for University of Technology or Comprehensive University students completing their national diplomas;

Method 4: structured workplace learning opportunities for candidates towards registration in a professional category by a statutory council listed in Table 1 above.

The contract skills participation goals, expressed in Rand, shall not be less than the contract amount multiplied by a percentage (%) factor given in Table 2 in the Standard for the applicable class of construction works.

Table 2: Contracting skills development goals for different classes of engineering and construction works contracts

Class of construction works as identified in terms of Regulation 25 (3) of the Construction Industry Regulations 2004		Construction skills development goal (CSDG) (%)
Designation	Description	
CE	Civil Engineering	0.25
CE and GB	Civil engineering and General Building	0.375
EE	Electrical Engineering works (buildings)	0.25
EP	Electrical Engineering works (infrastructure)	0.25
GB	General Building	0.5
ME	Mechanical Engineering works	0.25
SB	Specialist	0.25

The contractor shall apportion the learners in the different construction activities based on the scope of work. The cost of accommodating learners will be determined by using Table 3 in the Standard and this cost will be used to determine the value in Rand and will be added to the provision for training as provided for in the Preliminary and General section in the Bill of Quantities/Pricing schedules/Activity schedule.

Table 3: Notional Cost of Training per Headcount

Source: cidb Standard for Skills Development

Type of Training Opportunity	Provision for stipends (Unemployed learners only)	Provisions for mentorship	Provisions for additional costs*	Total costs	
				Unemployed learners	Employed learners
Method 1					
Occupational qualification	R7 000	R0	R9 000	R16 000	R9 000
Method 2					
TVET College graduates	R14 000	R0	R9 000	R23 000	N/A
Apprenticeship	R14 000	R0	R12 000	R26 000	R12 000
Method 3					
P1 and P2 learners	R24 000	R20 000	R4 500	R48 500	N/A
Method 4					
Candidates with a 3 year diploma	R37 000	R20 000	R4 500	R61 500	R20 000
Candidates with 4 year qualification	R47 000	R20 000	R4 500	R71 500	R20 000

Note: the required CPG will be recalculated based on the awarded tender amount and "Contract amount" once the beneficiaries have been appointed and actual costs are known. The notional cost of providing training opportunities will increase by CPI on an annual basis based on April CPI. Should the rates increase after bid award or during construction the rates will be adjusted as a remeasuarble item.

- The successful contractor may employ part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates directly or through a Skills Development Agency (SDA), (A1 - List of cidb accredited SDAs).
- The successful contractor must employ at least sixty percent (60%) of the learners from an FET / TVET college should the contractor select to have part/full occupational qualification learners and trade qualification learners contributing to the CSDG.

- (c) The successful contractor shall employ at least **10% (Ten Percent)** from eligible part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates in the employment of the employer.
- (d) The successful contractor shall ensure that no single method shall contribute more than seventy five percent (75%) of the CSDG for the contract.
- (e) The successful contractor may only place thirty three percent (33%) employed employees or that of his subcontractors contributing to the CSDG.
- (f) The contractor shall employ at least sixty percent (60%) of the learners from a Public FET / TVET college should the contractor select to have trade qualification learners (Method 2) contributing to the CSDG.
- (g) One of the objectives of the project is to train **10% (Ten Percent)** Occupational qualifications, trade qualification, work integrated learners – P1 and P2 learners, professional candidates.

C3.7.5.2 Management

- (a) The successful contractor must keep site records regarding the part/full occupational qualification learners', trade qualification learners', work integrated learners' or candidates' progress, site attendance, hours worked and other relevant information as required by the Standard.
- (b) The successful contractor shall provide the required number of appropriately qualified mentors to the maximum number of part/full occupational qualification learners, trade qualification learners, work integrated learners in the proportion as specified in the Standard.
- (c) The successful contractor shall provide a supervisor to manage the training of the part/full occupational qualification learners, trade qualification learners, work integrated learners, candidates.
- (d) The successful contractor shall submit to the employer's representative a baseline training plan in the specified format (Pro-forma A2) for the part/full occupational qualification learners, trade qualification learners, work integrated learners, candidates within 30 days of start of the contract.
- (e) The successful contractor shall submit to the employer's representative project interim report in the specified format (Pro-forma A3) on the progress of each of part/full occupational qualification learner, trade qualification learner, work integrated learner, candidate every three months.
- (f) The successful contractor shall submit to the employer's representative the names and particulars in the specified format (Pro-forma A4) of the supervisor, mentors for the part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates within 30 days of start of the contract.
- (g) The successful contractor shall keep a daily record of all the part/full occupational qualification learners, trade qualification learners, work integrated learners, candidates on site and their daily activities and shall be made available to the employer's representative on request.
- (h) The successful contractor shall submit to the employer's representative the reports on the progress and status of the part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates with the monthly invoice for the payment certificate.
- (i) The successful contractor shall have health and safety inductions for all part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates.
- (j) The successful contractor shall conduct entry and exit medical tests of all part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates.
- (k) The successful contractor shall provide personal protective equipment (PPE) to all part/full occupational qualification learners, trade qualification learners, work integrated learners or candidates at the start of their employment on site.

- (I) Based on the agreed skills methods the contractor may employ part/full Occupational Qualification Learners and /or Trade Qualification Learners and/or Work Integrated Learners and/or Candidates directly or through a Skills Development Agency (SDA), training provider or skills development facilitator (Form A1 - List of cidb accredited SDAs). The contractor shall ensure that no more than one Method shall be applied to any individual concurrently in the calculation of the CSDG for the contract.

C3.7.6 NATIONAL YOUTH SERVICE TRAINING AND DEVELOPMENT PROGRAMME (NYS)

The National Youth Service Training and Development Programme is *not applicable* to this project.

The programme shall be implemented in terms of the Implementation of the National Youth Service Programme under the Expanded Public Works (EPWP) and shall be priced in the CPG section of the Bills of Quantities. Monthly reports are to be submitted to the Employer's Representative.

Failure by the contractors to achieve the specified number to be trained in the NYS section of the CPG section within the Bills of quantities will result in a payment reduction as per bill of quantities per person, excluding VAT unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

C3.7.7 LABOUR-INTENSIVE WORKS

Labour Intensive Works is *applicable* to this project.

Where labour intensive work is specified in the Bill of Qualities and indicated by "LI" the contractor must price for and include in rates. Contractors are expected to use their initiative to identify additional activities that can be done labour-intensively to comply with the set minimum labour intensity target. Allowance must be made for submitting monthly reports illustrating the value of the works executed under Labour Intensive Works.

Failure by the contractor to achieve the specified value of the Labour Intensive Participation Goal as stipulated within the Bills of quantities will result in a thirty percent (30%) penalty of the value of the works not done by means of labour intensive methods, excluding VAT, unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control.

Employer's objectives:

The employer's objectives are to deliver public infrastructure using labour-intensive methods in accordance with EPWP Guidelines.

Labour-intensive works:

Labour-intensive works shall be constructed/maintained using local workers who are temporarily employed in terms of the scope of work. A **thirty percent (30%)** penalty of the value of the works will be imposed on items where unauthorised use of plant was used to carry out work which was to be done labour-intensively.

Labour-intensive competencies of supervisory and management staff:

Contractors shall only engage supervisory and management staff in labour-intensive works that have completed the skills programme including Foremen/ Supervisors at NQF level 4 "National Certificate: Supervision of Civil Engineering Construction Processes" and Site Agent/ Manager at NQF level 5 "Manage Labour-Intensive Construction Processes" or equivalent QCTO qualifications (See Appendix C) at NQF outlined in Table 1

C3.7.7.1 GENERIC LABOUR-INTENSIVE SPECIFICATION

Contractors are referred to the Guidelines for the Implementation of Labour-intensive Infrastructure Projects under the Expanded Public Works Programme (EPWP) for the generic labour-intensive specification applicable to the contract.

This specification establishes general requirements for activities which are to be executed by hand involving the following:

- trenches having a depth of less than 1.5 metres
- storm water drainage

- roads
- sidewalks and non-motorised transport infrastructure
- water and sanitation

Precedence

Where this specification is in conflict with any other standard or specification referred to in the Scope of Works to this Contract, the requirements of this specification shall prevail

Hand excavateable material

Hand excavateable material is:

a) granular materials:

- i) whose consistency when profiled may in terms of table 2 be classified as very loose, loose, medium dense, or dense; or
- ii) where the material is a gravel having a maximum particle size of 10mm and contains no cobbles or isolated boulders, no more than 15 blows of a dynamic cone penetrometer is required to penetrate 100mm;

b) Cohesive materials:

- i) whose consistency when profiled may in terms of table 2 be classified as very soft, soft, firm, stiff and stiff / very stiff; or
- ii) where the material is a gravel having a maximum particle size of 10mm and contains no cobbles or isolated boulders, no more than 8 blows of a dynamic cone penetrometer is required to penetrate 100mm;

Note

- 1) A boulder is material with a particle size greater than 200mm, a cobble and gravel is material between 60 and 200mm.
- 2) A dynamic cone penetrometer is an instrument used to measure the in-situ shear resistance of a soil comprising a drop weight of approximately 10 kg which falls through a height of 400mm and drives a cone having a maximum diameter of 20mm (cone angle of 60° with respect to the horizontal) into the material being used.

Table 2: Consistency of materials when profiled			
GRANULAR MATERIALS		COHESIVE MATERIALS	
CONSISTENCY	DESCRIPTION	CONSISTENCY	DESCRIPTION
Very loose	Crumbles very easily when scraped with a geological pick.	Very soft	Geological pick head can easily be pushed in as far as the shaft of the handle.
Loose	Small resistance to penetration by sharp end of a geological pick.	Soft	Easily dented by thumb; sharp end of a geological pick can be pushed in 30-40 mm; can be moulded by fingers with some pressure.
Medium dense	Considerable resistance to penetration by sharp end of a geological pick.	Firm	Indented by thumb with effort; sharp end of geological pick can be pushed in up to 10 mm; very difficult to mould with fingers; can just be penetrated with an ordinary hand spade.
Dense	Very high resistance to penetration by the sharp end of a geological pick; requires many blows for excavation.	Stiff	Can be indented by thumb-nail; slight indentation produced by pushing geological pick point into soil; cannot be moulded by fingers.

Very dense	High resistance to repeated blows of a geological pick.	Very stiff	Indented by thumb-nail with difficulty; slight indentation produced by blow of a geological pick point.

Trench excavation

All hand excavateable material in trenches having a depth of less than 1,5 metres shall be excavated by hand.

Compaction of backfilling to trenches (areas not subject to traffic)

Backfilling to trenches shall be placed in layers of thickness (before compaction) not exceeding 100mm. Each layer shall be compacted using hand stampers;

- to ninety percent (90%) Mod AASHTO;
- such that in excess of 5 blows of a dynamic cone penetrometer (DCP) is required to penetrate 100 mm of the backfill, provided that backfill does not comprise more than ten (10%) gravel of size less than 10mm and contains no isolated boulders, or
- such that the density of the compacted trench backfill is not less than that of the surrounding undisturbed soil when tested comparatively with a DCP.

Excavation

All excavateable material including topsoil classified as hand excavateable shall be excavated by hand. Harder material may be loosened by mechanical means prior to excavation by hand. Any material which presents the possibility of danger or injury to workers shall not be excavated by hand.

Clearing and grubbing

Grass and bushes shall be cleared by hand.

Shaping

All shaping shall be undertaken by hand.

Loading

All loading shall be done by hand. Haulage equipment should be selected in a manner that allows loading by hand to the greatest extent possible.

Haul

Excavation material shall be hauled to its point of placement by means of wheelbarrows where the haul distance is not greater than 150m.

Offloading

All material, however transported, is to be off-loaded by hand, unless tipper-trucks are utilised for haulage.

Spreading

All material shall be spread by hand.

Compaction

Small areas may be compacted by hand provided that the specified compaction is achieved. Appropriate rollers should be used where higher (than can be achieved by hand) levels of compaction are required or for large areas.

Grassing

All grassing shall be undertaken by sprigging, sodding, or seeding by hand.

Stone pitching and rubble concrete masonry

All stone required for stone pitching and rubble concrete masonry, whether grouted or dry, must to be collected, loaded, off loaded and placed by hand.

Sand and stone shall be hauled to its point of placement by means of wheelbarrows where the haul distance is not greater than 150m.

Grout shall be mixed and placed by hand.

Manufactured Elements

Elements manufactured or supplied by the Contractor, such as manhole rings and cover slabs, precast concrete planks and pipes, masonry units and edge beams shall not individually, have a mass of more

than 320kg. Where the mass of an element exceeds 55 kg, consideration should be given to the size of the element relative to its total mass related to the number of workers who would be needed to lift such mass

C3.8 Submission of Accrual Reports

The Contractor shall submit accrual reports to the client representative at the end of March and September each year for the duration of the Service Contract period from the date of appointment up to and including project closeout. This is to ensure that PMTE complies with the accounting framework GRAP, which requires that PMTE disclose all its accruals as at the end of each reporting date.

C.3.9 Submission of Monthly Local Material Utilisation Report (Local Content)

The contractors shall be responsible for record keeping, documenting and submission of monthly local material utilization report with supporting documentation to the Employer's representative within 7 working days of the beginning of the successive month, in terms of DTI&C designated industry/sector/sub-sector schedule as per the PA36 and Annexures C attached to the tender document. The final percentage achievement to be reconciled upon completion of the project and form part of the final account.

Failure by the contractors to achieve the specified percentage of local content per designated industry/sector/sub-sector as listed will result in a thirty percent thirty percent (30%) penalty of the value not achieved, excluding VAT, unless the contractor can prove to the Employer's satisfaction that the non-achievement was beyond his/her control. Allowance must be made for submitting monthly reports illustrating the value of local material utilisation report.

Examples of calculating CPGs and related penalties

CPGs values are based on the Tender Amount at the time of the award. Determining the actual values is based either on the Tender Amount including allowances and Vat or the Tender Amount at the time of award excluding allowances and VAT, where Allowances include the following:

- Provisional amounts
- CPG allowances
- Nominated and/or selected subcontractors
- Contract price adjustment (Not provided for within the B of Q by NDPWI)
- Contingency amounts (Not provided for within the B of Q by NDPWI)

CPG values in the CPG Bill of Quantities Section will be recalculated based on the “Tender Amount” or the “Contract Amount” which ever applicable and the provisional amounts adjusted accordingly. Sanctions (penalties) are applicable to all CPGs where the contractor fails to achieve the minimum specified requirements, unless the contractor can prove to the Employer’s satisfaction that the non-achievement was beyond his/her control. No penalties will be applied should the CPG value, based on the original “Tender Amount” or the “Contract Amount”, has been achieved.

1.1 Targeted Local Building Material Manufacturers CPG

When applicable, the CPG is expressed as a percentage of the “Contract Amount”, i.e. the Tender Amount at the time of award excluding allowances and VAT.

CPG calculation example:

“Tender Amount” = R150 Mil all inclusive of allowances and VAT

“Contract Amount” = R130 Mil (Tender Amount at the time of award excluding allowances and VAT)

CPG to be achieved = 5% as specified in the Scope of Works (PG01.1)

CPG target value = R130 Mil x 5% = R 6, 5 Mil (Value of material to be purchased from local manufacturers, excluding VAT)

Calculation of penalty:

Percentage penalty applicable = 10% as specified in the Scope of Works (PG01.1)

CPG target value = R6, 5 Mil excluding VAT

CPG Achieved = R5, 5 Mil (R1 Mil shortfall) excluding VAT

Penalty = R1 Mil x 10% = R100 000 excluding VAT

1.2 Targeted Local Building Material Suppliers CPG

When applicable, the CPG is expressed as a percentage of the “Contract Amount”, i.e. the Tender Amount at the time of award excluding allowances and VAT.

CPG calculation example:

“Tender Amount” = R150 Mil all inclusive of allowances and VAT

“Contract Amount” = R130 Mil (Tender Amount at the time of award excluding allowances and VAT)

CPG to be achieved = 5% as specified in the Scope of Works (PG01.1)

CPG target value = R130 Mil x 5% = R 6, 5 Mil (Value of material to be purchased from local suppliers, excluding VAT)

Calculation of penalty:

Percentage penalty applicable = 20% as specified in the Scope of Works (PG01.1)

CPG target value = R6, 5 Mil excluding VAT

CPG Achieved = R5, 5 Mil (R1 Mil shortfall) excluding VAT

Penalty = R1 Mil x 20% = R200 000 excluding VAT

1.3 Targeted Local Labour Skills Development CPG

When applicable, the CPG is expressed as a percentage of the total number working days required to complete the Works.

CPG calculation example:

“Tender Amount” = R150 Mil all inclusive of allowances and VAT

“Contract amount” = R130 Mil (Tender Amount at the time of award excluding allowances and VAT)

Number of working days required to complete the Works based on the construction period = 600 days

CPG percentage participation to be achieved = 30% as specified in the Scope of Works (PG01.1)

Required number of working days training to be provided = 180 days (600 x 30%)

Calculation of penalty:

Payment reduction = R 5 000 per day for not providing training as specified in the Scope of Works (PG01.1)

CPG = 600 working days x 30% = 180 working days training to be provided

CPG Achieved = 160 days (20 days shortfall where no training was provided)

Penalty = 20 days x R5 000 payment reduction per day= R100 000 excluding VAT

1.4 Cidb BUILD Programme: Enterprise Development

When applicable, the Enterprise Development CPG expressed as a percentage of the “Contract amount” = Tender amount at the time of award excluding allowances and VAT. Failure to achieve the minimum Targeted Local Labour Skills Development CPG will result in a payment reduction of an amount specified in the Scope of Works (PG01.1) per working day where training was not provided.

The monetary value of training to be provided is stipulated in the CPG BoQ section. The number of beneficiaries to be trained is dependent on the “Contract Amount” as well the number of beneficiaries appointed which will generally resort under the Grade 1 and 2 cidb categories. The provisional amount will therefore be adjusted in terms of the “contract Amount”, the number of beneficiaries to be trained and the actual cost for providing the training.

Part 1: Calculation of 5% CPG example:

“Tender Amount” = R150 Mil all inclusive of allowances and VAT

“Contract Amount” = R130 Mil (Tender Amount at the time of award excluding allowances and VAT)

CPG percentage participation to be achieved = 5% as specified in the Scope of Works (PG01.1)

CPG value = R6, 5 Mil (Value of work to be subcontracted to emerging enterprises)

Calculation of penalty

Percentage penalty applicable = 30% as specified in the Scope of Works (PG01.1)

CPG Minimum 5% = R6, 5 Mil

Achieved = R5, 5 Mil (Only subcontracted work to the value of R5, 5 Mil, i.e. R1 Mil shortfall)

Penalty = R1 Mil x 30% = R300 000 Excl. VAT

Part 2: Calculations in terms of training to be done:

The number of enterprises to be developed is subject to the contract amount and the apportionment of the work as per Example 1 below.

Number of enterprises to be trained = 6 x 1 GB subcontractors

Total cost for training = R 1 660 000

Calculation of penalty

Total number of enterprises to be trained = 6

Total number trained = 4 (2 Shortfall)

Training cost per beneficiary = R1 660 000 / 6 = R 276 666, 67 per beneficiary

Penalty = R 276 666, 67 x 2 x 30% = R166 000 Excl. VAT

B of Q Item	Description	Unit	Rate	Quantity	Amount (R)
5	Enterprise Development				
5.1	Enterprise Development of Targeted Enterprise or JV partners				
5.1.1	Appointment of training co-ordinator	Per Quarter	45 000	8	360 000
5.1.2	Appointment of Mentor /Training Service provider	Per Quarter	135 000	8	1 080 000
5.1.3	Needs Analysis and Enterprise Development Plan per Targeted Enterprise	No.	5 000	6	30 000
5.1.4	Monitoring and Interim reporting per targeted enterprise	Per Quarter	20 000	8	160 000
5.1.5	Project Completion report per Targeted Enterprise	No.	5 000	6	30 000
	Provisional Sum to be carried over to CPG bill of quantities				1 660 000

“Contract amount” Tender amount excl. allowances and VAT.

130 000 000

B of Q Item	Description	Unit	Rate	Quantity	Amount (R)
	CPG Monetary value (5%) to be subcontracted to beneficiaries for training	6 500 000			
	No of enterprises based on the CPG value	6	Grade 1 / 2 GB/CE,ETC.		
	Contract period (months)	24			
	Note: Rates to be determined by PQS and adjusted to accepted quotation amounts				

1.5 Cidb BUILD Programme: Skills Development (Principal contractor including subcontractors and consultants)

When applicable, the contract skills development participation goals, expressed in Rand, shall be no less than the “contract amount” multiplied by a percentage (%) factor for the applicable class of construction works.

The monetary value of training to be provided is stipulated in the CPG BoQ section. The number of beneficiaries to be trained is dependent on the “Contract Amount” as well the number of beneficiaries appointed which will generally resort under the Grade 1 and 2 cidb categories. The provisional amount will therefore be adjusted in terms of the “Contract Amount”, the number of beneficiaries to be trained from which *Method* and the actual cost for providing the training.

CPG Calculation

Table 2: Contracting skills development goals for different classes of engineering and construction works contracts

Source: cidb Standard for Developing Skills through Infrastructure Contracts as published in the Government Gazette Notice No. 43495 of 3 July 2020 (Page 7)

Class of construction works as identified in terms of Regulation 25 (3) of the Construction Industry Regulations 2004		Construction skills development goal (CSDG) (%)
Designation	Description	
CE	Civil Engineering	0.25
CE and GB	Civil engineering and General Building	0.375
EE	Electrical Engineering works (buildings)	0.25
EP	Electrical Engineering works (infrastructure)	0.25
GB	General Building	0.5
ME	Mechanical Engineering works	0.25
SB	Specialist	0.25

“Contract amount” = Tender amount at the time of award excluding allowances and expenses, and VAT

Contractor CPG:

CPG calculation

“Contract amount” x factor from Table 3 above.

CPG calculation example:

“Tender Amount” = R150 Mil for GB, all inclusive of allowances and VAT

“Contract Amount” = R130 Mil (Tender Amount at the time of award excluding allowances and VAT)

Factor for GB = 0, 5% (as per Table 2 above)

CPG in R value = R130 Mil x 0, 5% = R650 000 i.e. total notional cost of training to amount to R650 000

Calculation of penalty:

Percentage penalty applicable = 30% as specified in the Scope of Works (PG01.1)

CPG value = R650 000

Achieved = R550 000 = R100 000 Shortfall

Penalty = R100 000 x 30% = R30 000 Excl. VAT

Calculations based on “Contract Amount” after bid award and appointment of beneficiaries

Actual CPG training requirement value after award upon selecting method/s of training and appointment of beneficiaries = R676 000 (Table 4 below) and the provisional amount allowed for to be adjusted accordingly. The new monetary value of training required will then form the basis for determining penalties applicable. No penalties will be applied should the CPG value, based on the “Contract Amount” be achieved.

Table 4: Notional cost recalculation upon appointment of beneficiaries.

Source: cidb Standard for Developing Skills through Infrastructure Contracts as published in the Government Gazette Notice No. 43495

of 3 July 2020 (Page 10)

Skills Types	Number of learners	Notional Cost / Learner / Quarter	Notional cost / learner / year	Total Notional Cost over 12 months Contract
Method 2: Workplace learning opportunities, with unemployed TVET graduates	2	R23 000	R92 000	R184 000
Method 3: Candidacy for an unemployed learner with a 3-year qualification	2	R61 500	R246 000	R492 000
Total	4			R676 000

Note: the required CPG will be recalculated based on the awarded Tender amount and "Contract Amount" once the beneficiaries have been appointed and actual costs are known

Note: The notional cost of providing training opportunities will increase by CPI on an annual basis based on April CPI as published by Stats SA. The rates will be adjusted as an adjustment to the provisional amounts should the rates increase after bid award or during the construction period

1.6 National Youth Service Programme (NYS) CPG

When applicable, a separate NYS Bill of Quantities will be included in the tender documentation will indicate the number of beneficiaries to be trained.

Calculation of penalty:

Payment reduction per person not trained as stipulated in the NYS Bill of Quantities = R 2 500 per person.

Total number of NYS Beneficiaries as stipulated in the NYS Bill of Quantities = 25

Total Number of NYS beneficiaries trained = 20 (shortfall of 5 beneficiaries)

Penalty = 5 x R2 500 = R12 500 Excl. VAT

1.7 Labour Intensive Works CPG

When applicable, the work to be done by way of Labour intensive methods are specified in the Bills of Quantities with a "LI".

CPG calculation example:

"Tender Amount" = R150 Mil all inclusive of allowances and VAT

"Contract Amount" = R130 Mil (Tender Amount at the time of award excluding allowances and VAT)

CPG value = R10 Mil (Total value of labour-intensive works specified in the Bills of Quantities)

Calculation of penalty:

CPG value = R10 Mil

Percentage penalty applicable = 30% as specified in the PG01.1 Scope of Work

CPG Achieved = 9 Mil (R1 Mil shortfall)

Penalty = R1 Mil x 30% = R300 000 Excl. VAT

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

PART C4 SITE INFORMATION

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

C4.1 SITE INFORMATION – GCC 2015 3rd Edition

PG-03.1 (EC) SITE INFORMATION – GCC 3rd Edition (2015)


Project title:	ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS (APPOINTMENT OF A CONTRACTOR)				
Tender no:	<i>H25/008 AI</i>	WCS no:	<i>056397</i>	Reference no:	<i>WCS 056397</i>

C4 Site Information

The location of each facility is briefly described below:


Alexandra Bay Land Port of Entry:

Alexandra Bay LPOE is located at the border between South Africa and Namibia. The closest nearest town is Springbok which is approximately 227 kilometres away. The operating hours are 06:00 – 22:00 Monday – Sunday.

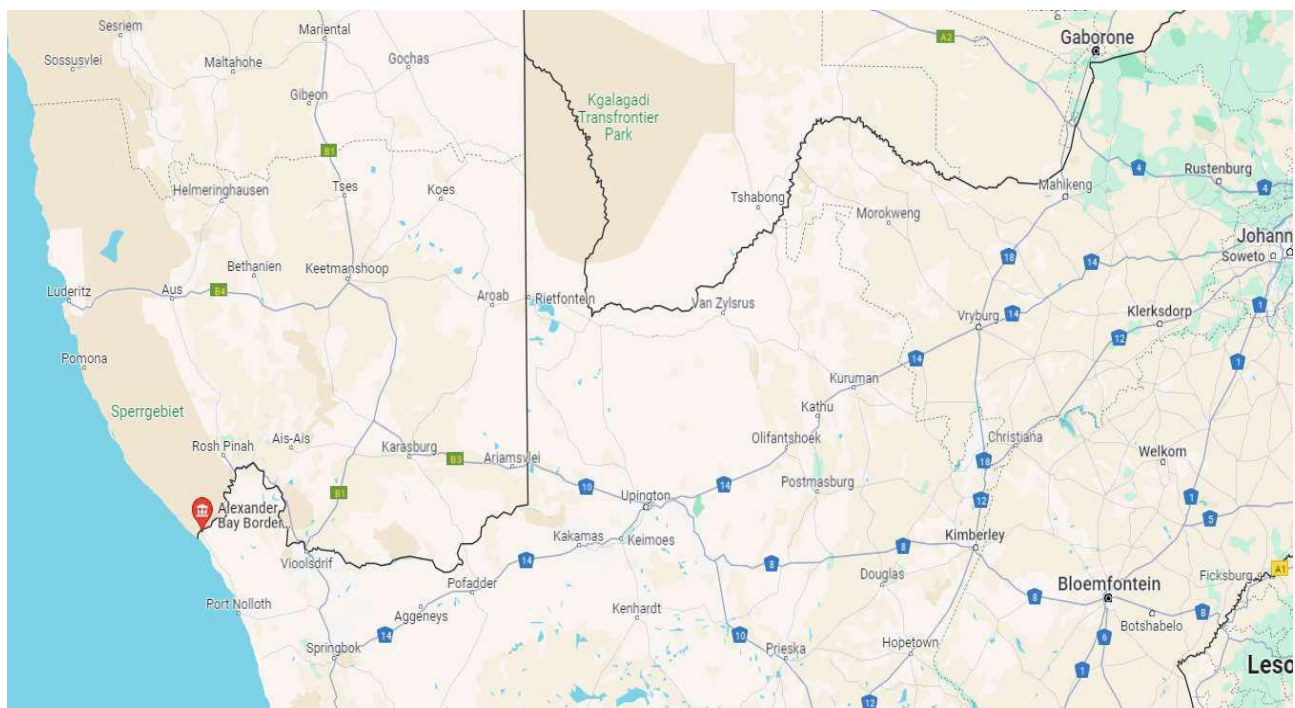


Vioolsdrift Land Port of Entry:

Vioolsdrift LPOE is located at the border between South Africa and Namibia. The closest nearest town is Springbok which is approximately 115 kilometres away. The Ports is operational 24 hours Monday – Sunday.

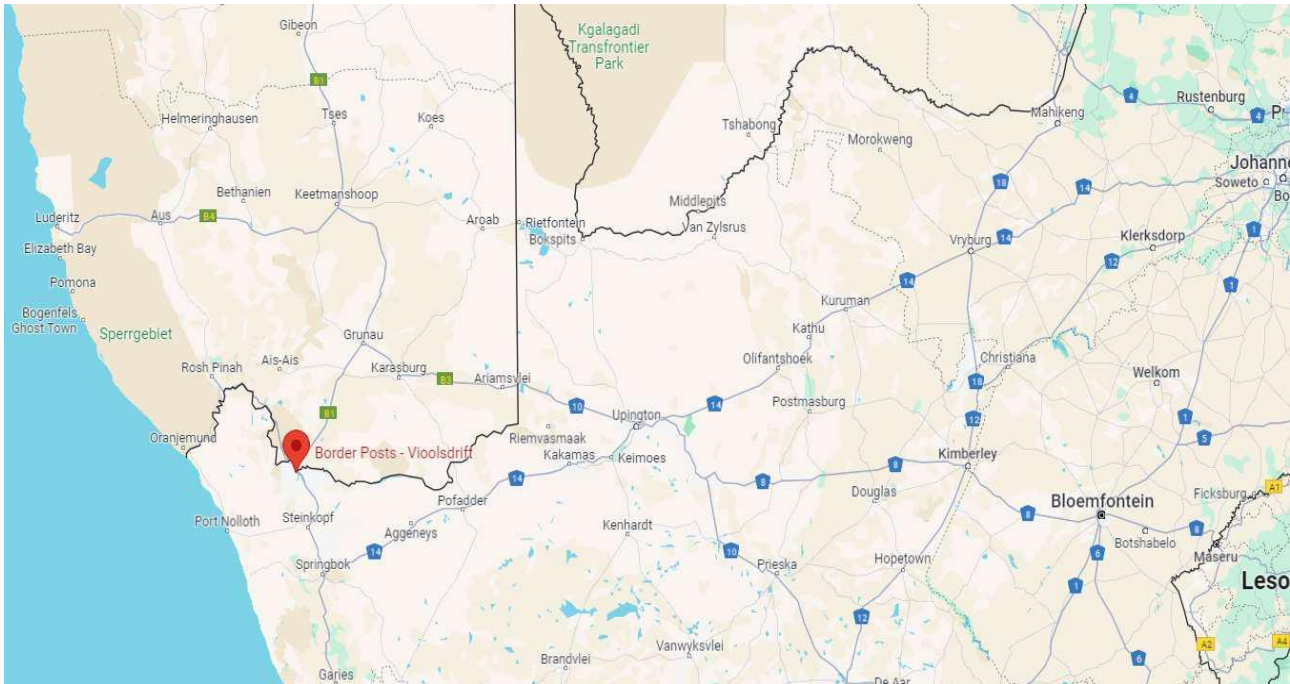

Onseepkans Land Port of Entry:

Onseepkans LPOE is located at the border between South Africa and Namibia. The closest nearest town is Springbok which is approximately 215 kilometres away. The operating hours are 08:00 – 16:30 Monday – Sunday.

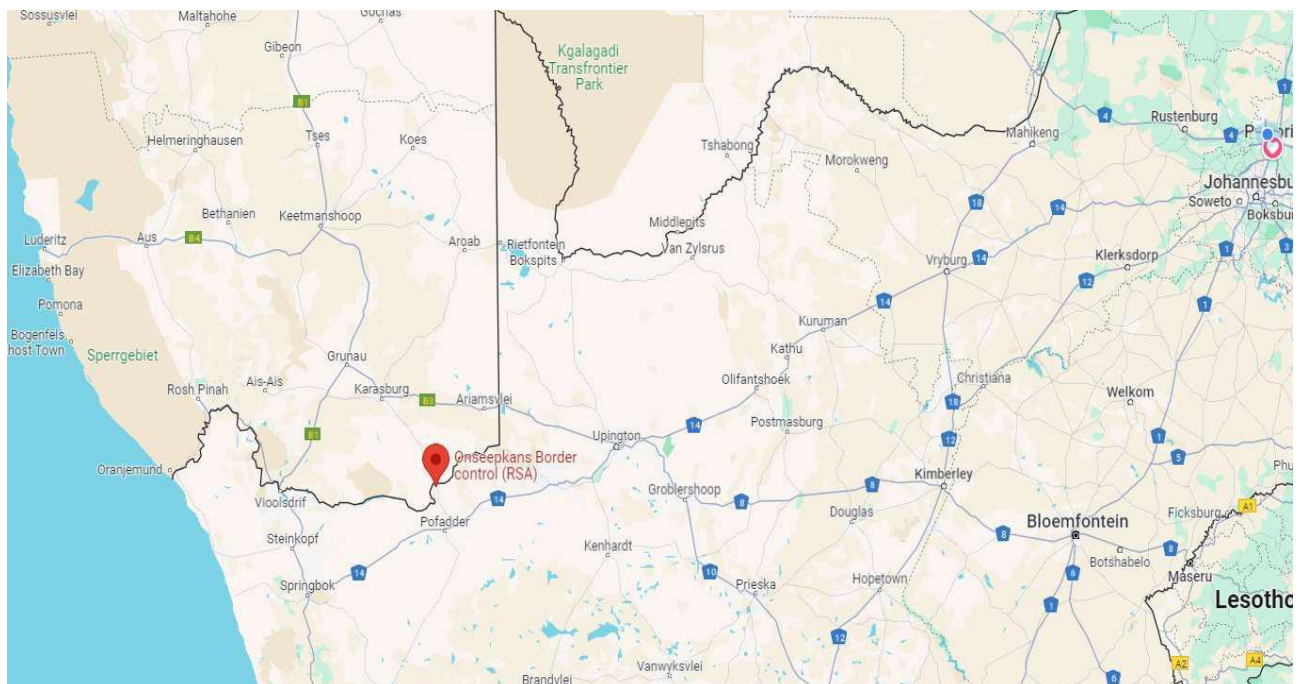


ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

C4.2 SITE LAYOUTS

ALEXANDER BAY, VIOOLSDRIFT AND ONSEEPKANS LAND PORTS OF ENTRY: 36 MONTHS
INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDINGS, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS
(APPOINTMENT OF A CONTRACTOR)

LIST OF SITE LAYOUTS

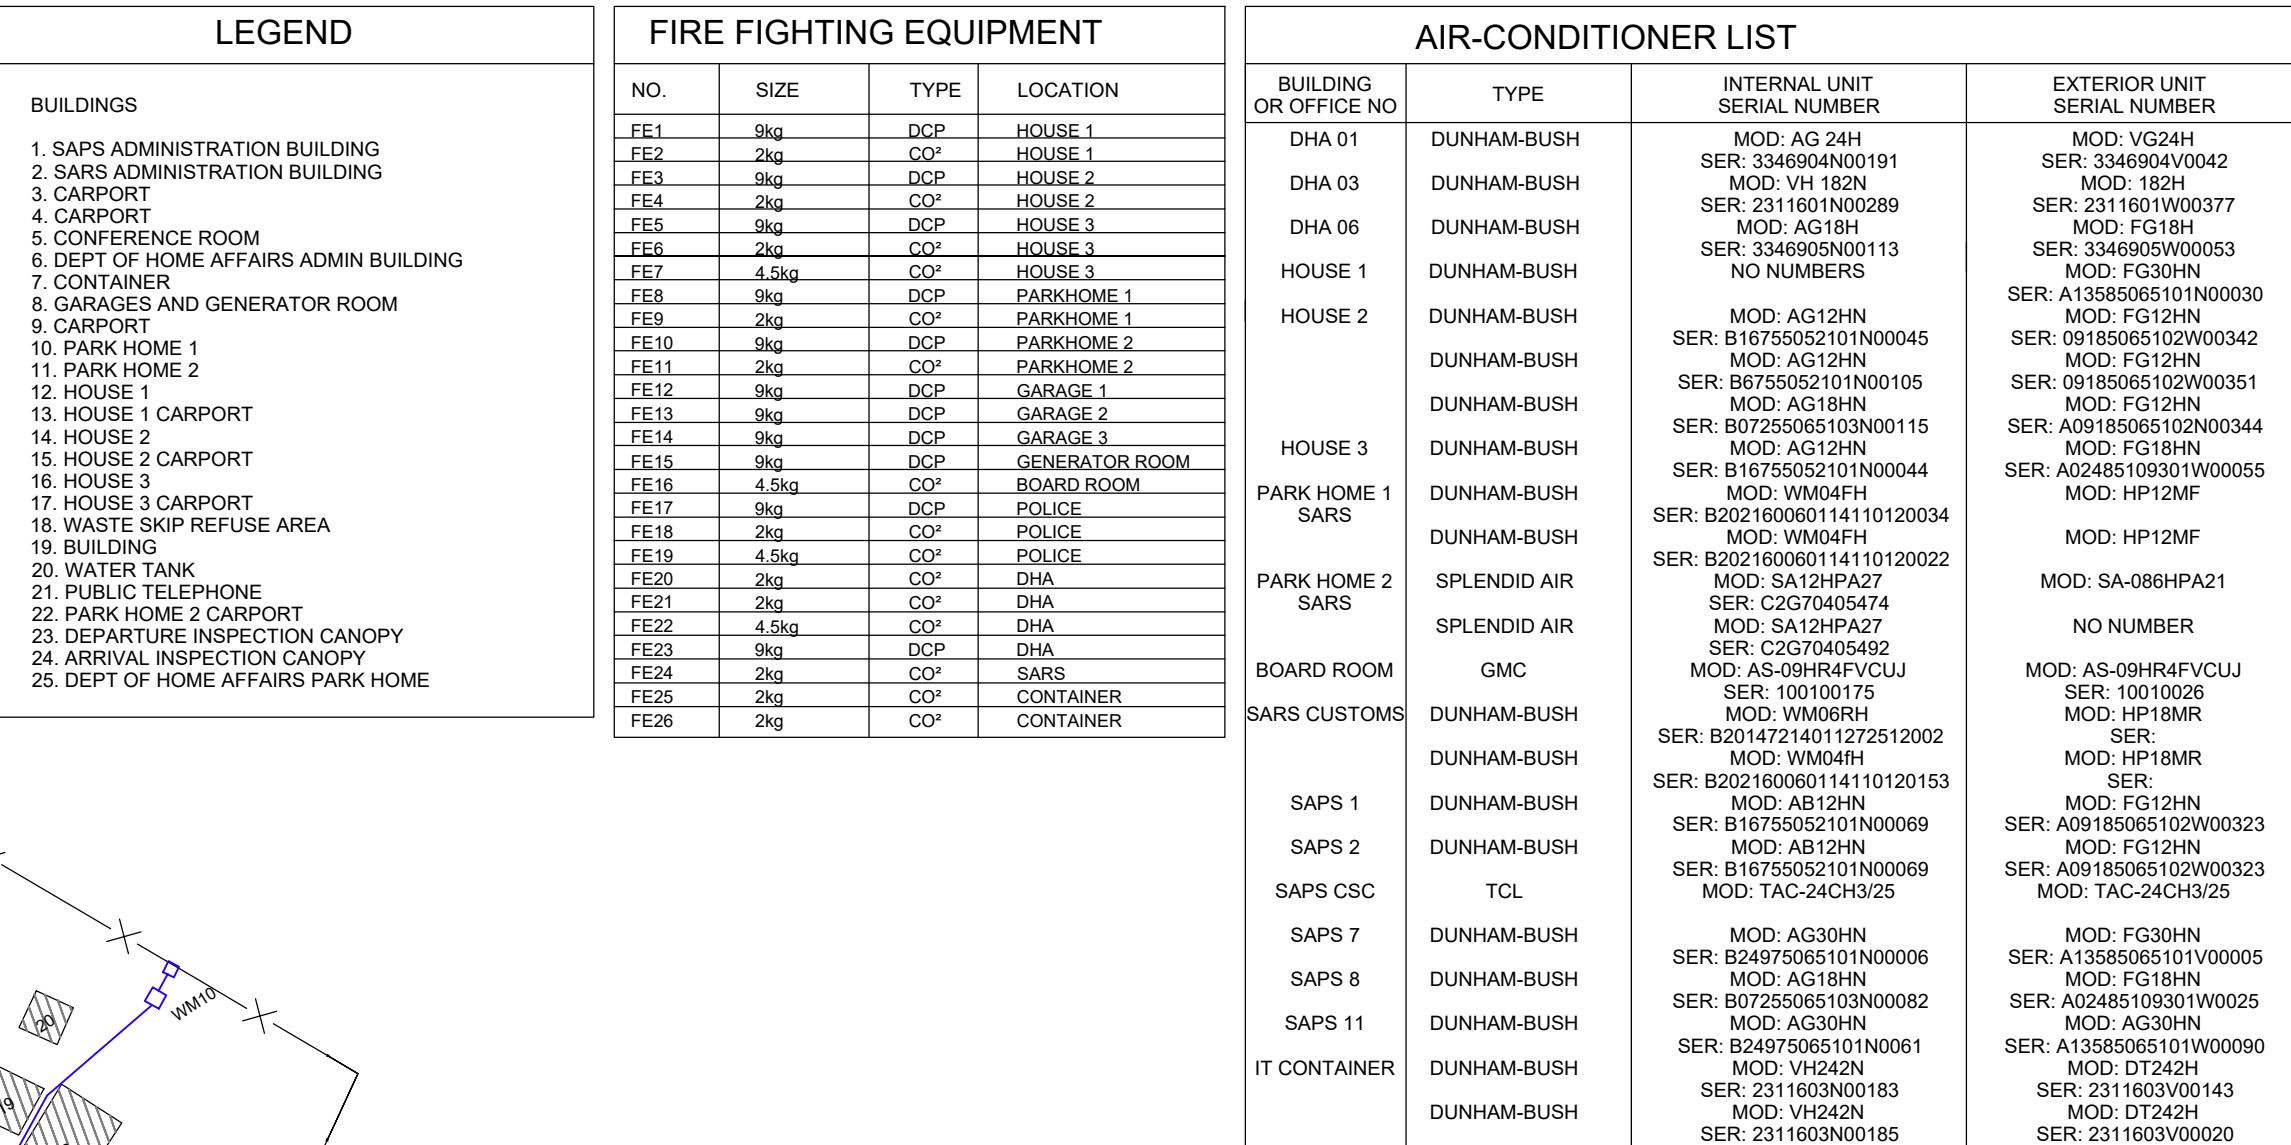

**INFRASTRUCTURE MAINTENANCE AND REPAIRS
OF BUILDING, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS**



**ALEXANDER BAY LPOE
SITE LAYOUT**


station wells doc type n

SCALE 1:500

DRW NO WCS_056397-ALEX-LP-001

Revision

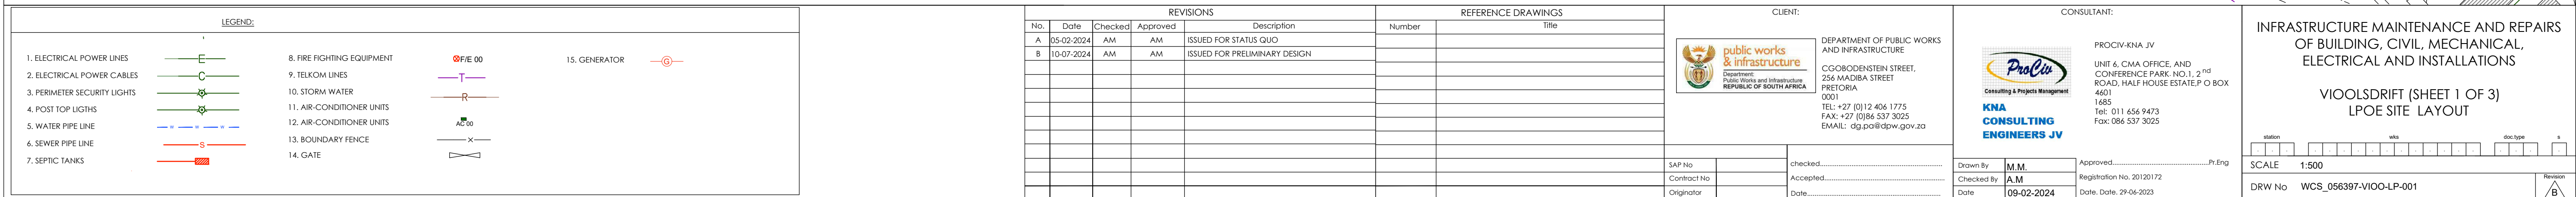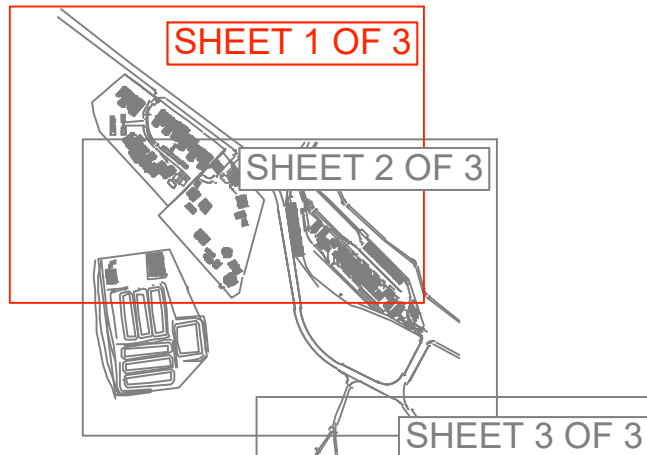

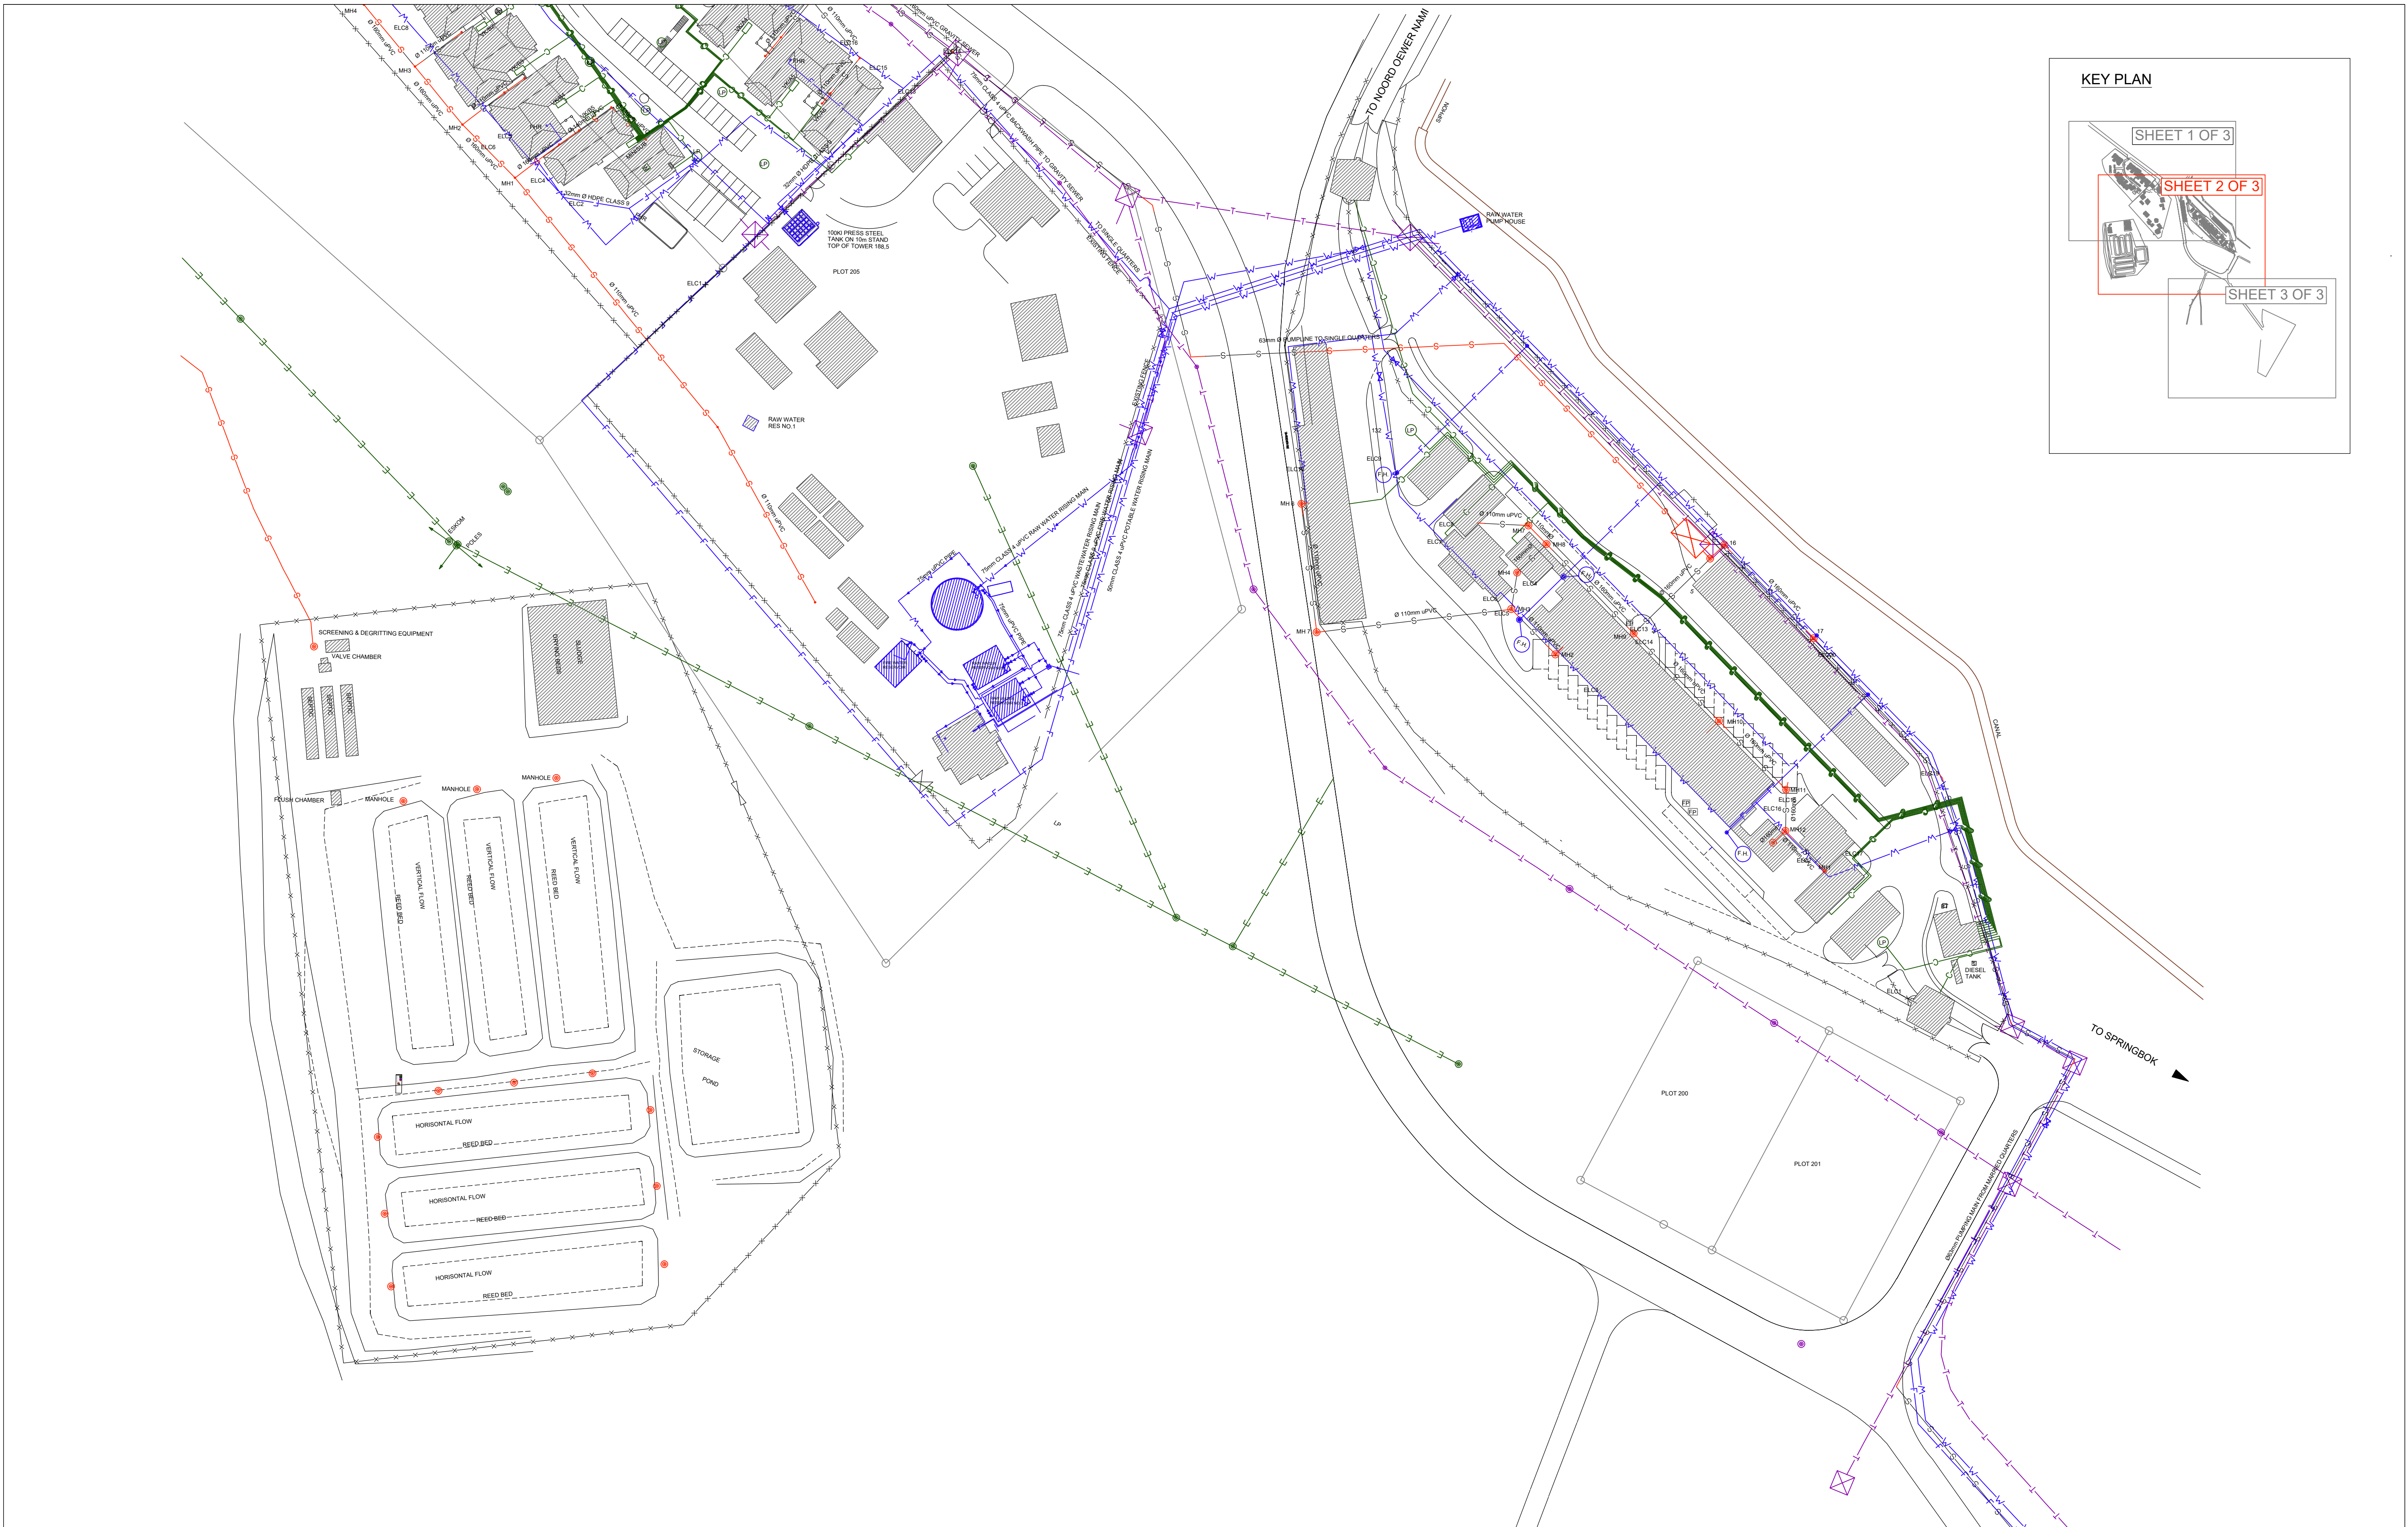LEGEND:			
1. ELECTRICAL POWER LINES		8. FIRE FIGHTING EQUIPMENT	
2. ELECTRICAL POWER CABLES		9. TELKOM LINES	
3. PERIMETER SECURITY LIGHTS		10. STORM WATER	
4. POST TOP LIGHTS		11. AIR-CONDITIONER UNITS	
5. WATER PIPE LINE		12. AIR-CONDITIONER UNITS	
6. SEWER PIPE LINE		13. BOUNDARY FENCE	
7. SEPTIC TANKS		14. GATE	
		15. GENERATOR	

[illegible]

 public works & infrastructure Department of Public Works and Infrastructure REPUBLIC OF SOUTH AFRICA		CUSTOMER: DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE CGOBODENSTREET STREET, 256 MADIBA STREET PRETORIA 0001 TEL: +27 (0)12 406 1775 FAX: +27 (0)86 537 3025 EMAIL: dg.pori@dpw.gov.za
SAP No	checked.....	
Contract No	Accepted.....	
Originator	Date.....	

		CONSULTANT:	
 ProCiv Consulting & Projects Management		PROCIV-KNA JV UNIT & CMA OFFICE, NO. 1, 2nd CONFERENCE PARK, NO. 1, 2nd ROAD, HALF-HOUSE ESTATE, P. O. BOX 4601 1685 Tel: 011 656 9473 Fax: 086 537 3025	
KNA CONSULTING ENGINEERS JV			
Drawn By	M.M.	Approved	Pr.E.
Checked By	A.M	Registration No.	20120172
Date	09-02-2024	Date, Date	29-06-2023

INFRASTRUCTURE MAINTENANCE AND REPAIRS
OF BUILDING, CIVIL, MECHANICAL,
ELECTRICAL AND INSTALLATIONS



VIOOLSDRIET (SHEET 2 OF 3)
LPOE SITE LAYOUT

station	wkts	disc type	x
SCALE	1:500		

DRAW NO WCS_056397-VIOO-LP-002

Revision

B

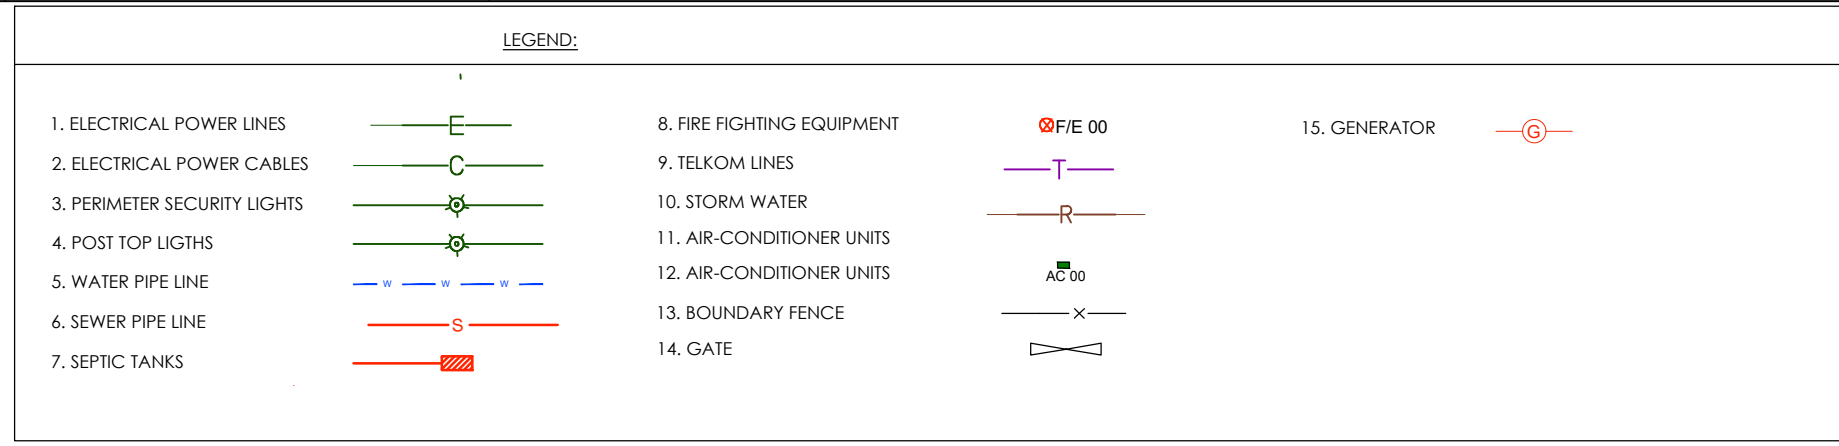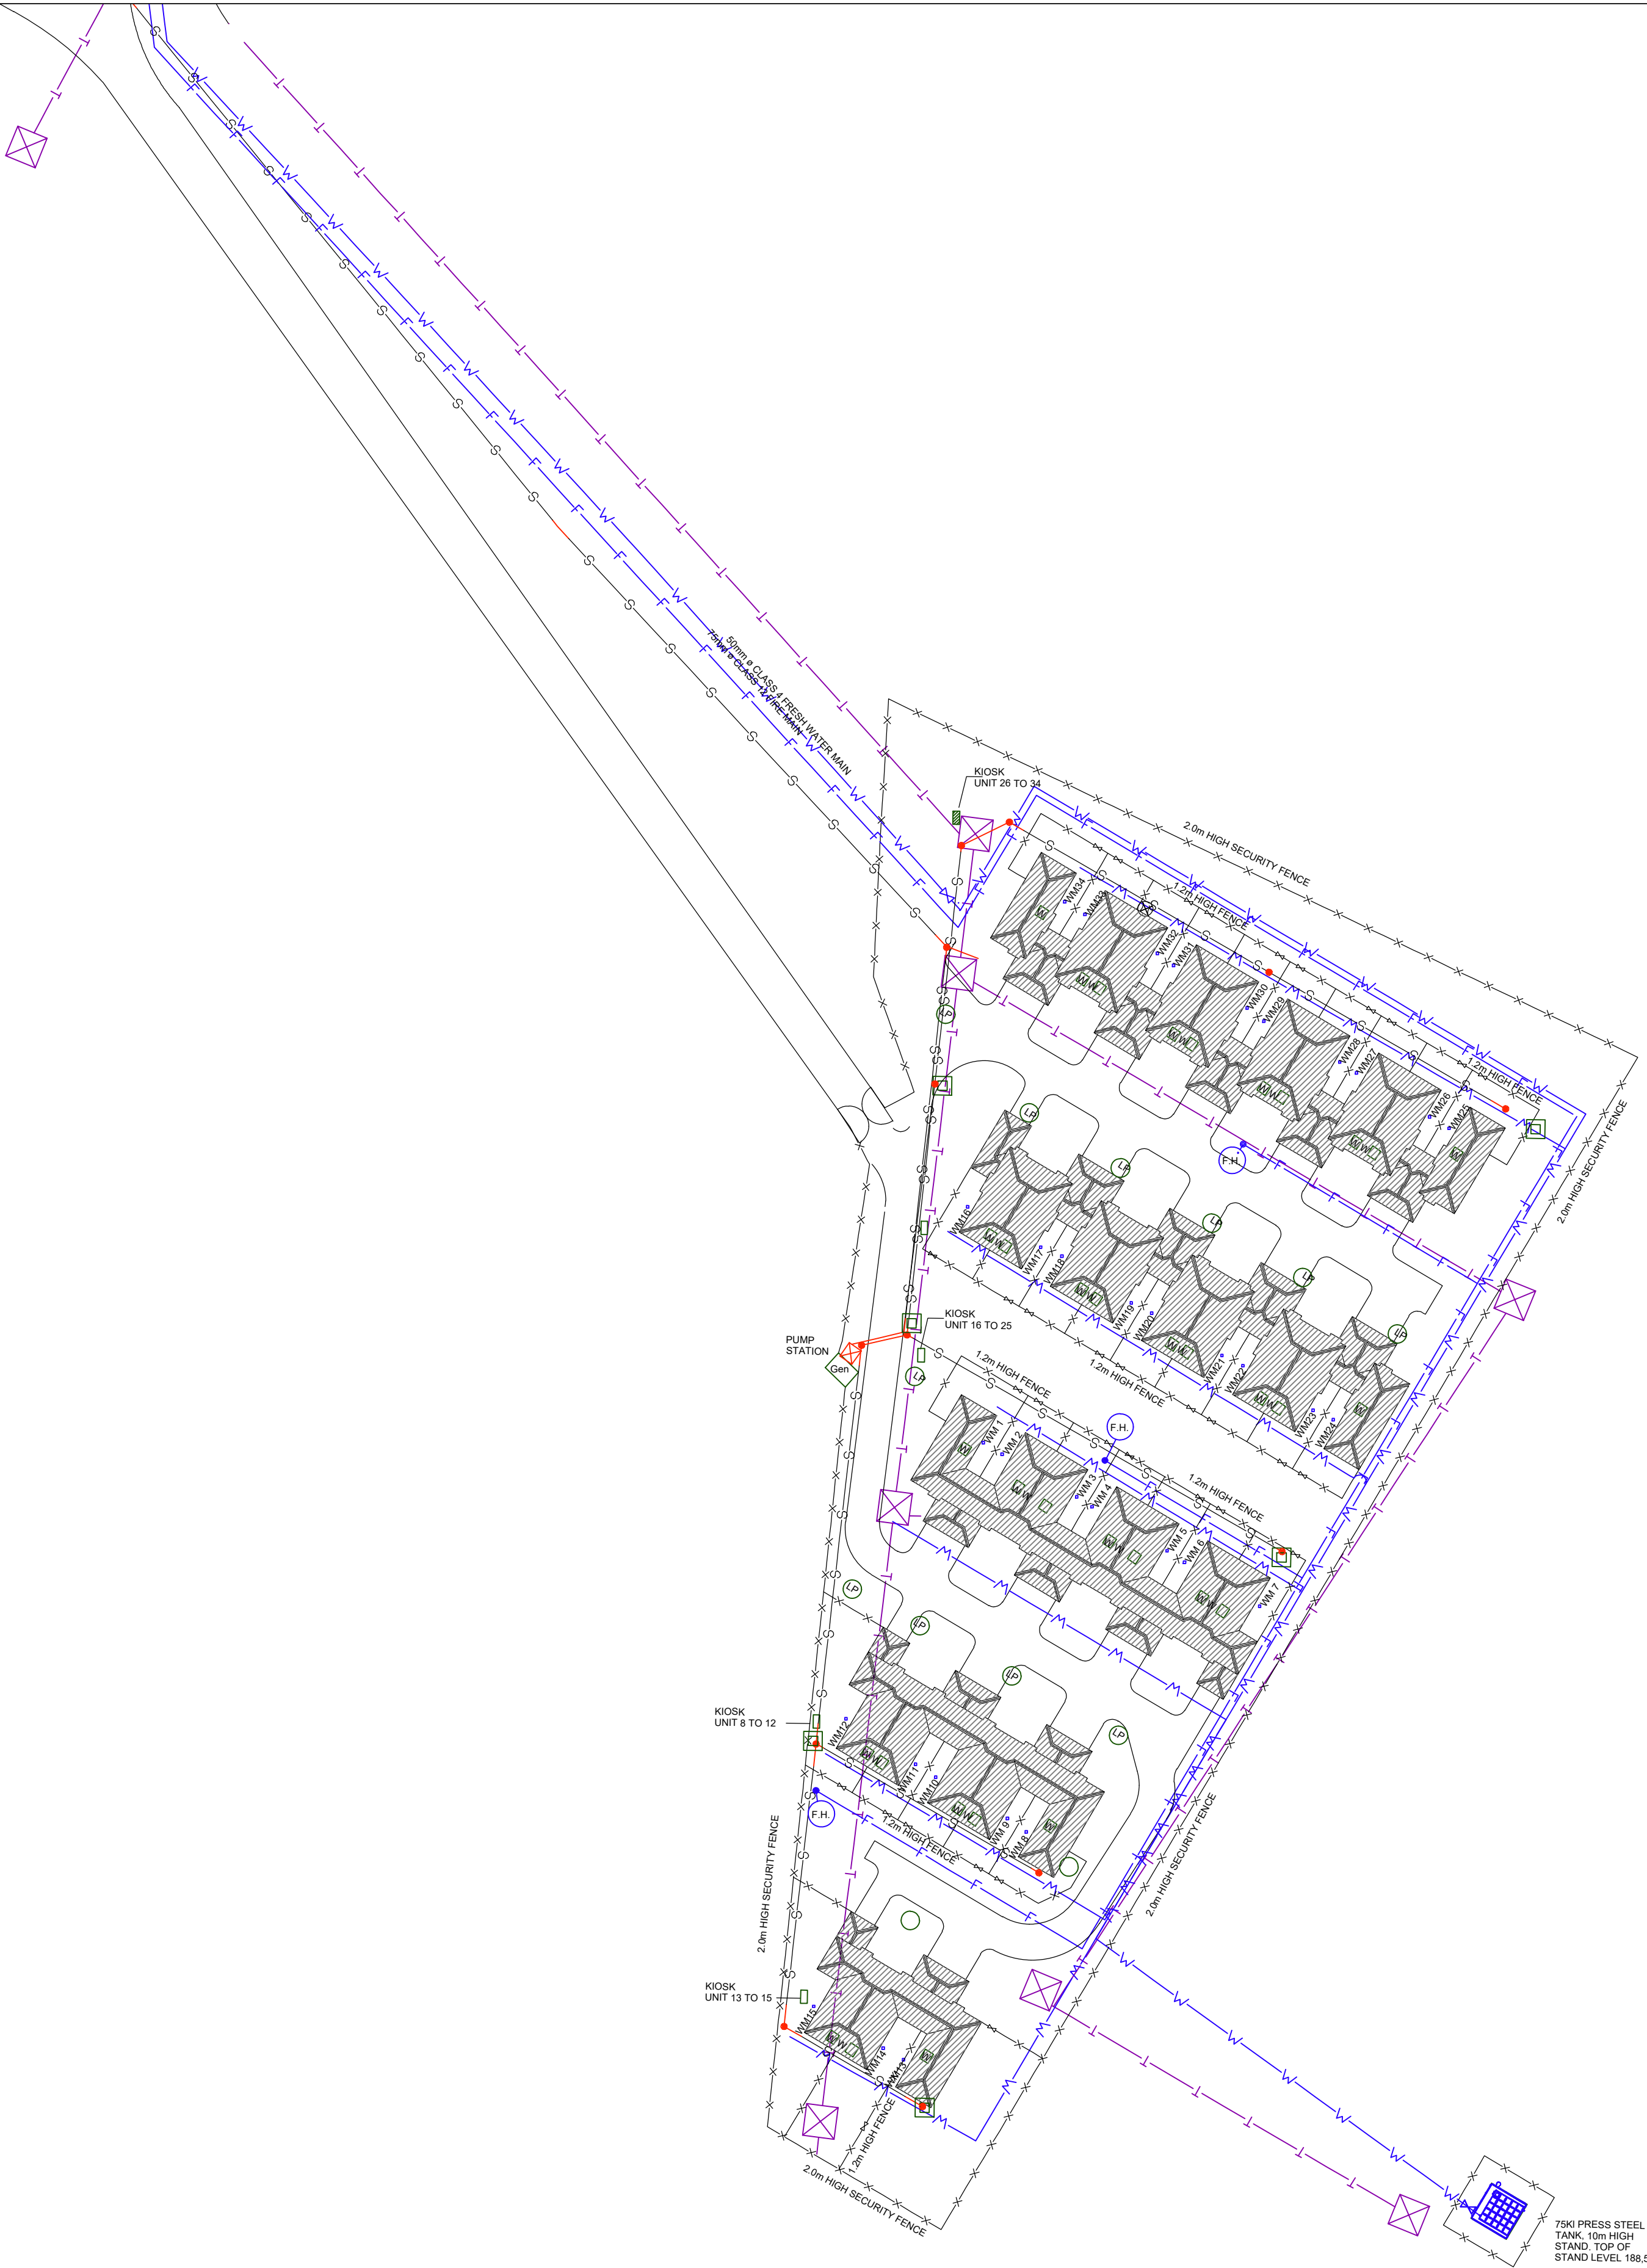[illegible]

 public works & infrastructure Department of Public Works and Infrastructure REPUBLIC OF SOUTH AFRICA		CLIENT: DEPARTMENT OF PUBLIC WORKS AND INFRASTRUCTURE CGOBODENSTEIN STREET, 256 MADIBA STREET PRETORIA 0001 TEL : +27 (0) 12 406 1775 FAX : +27 (0)86 537 3025 EMAIL : dig.pw@dpw.gov.za	
SAP No _____ Contract No _____ Originator _____		checked_____ Accepted_____ Date_____	

CONSULTANT:		PROCIV-KNA JV UNIT 6, CMA OFFICE, AND CONFERENCE PARK NO.1, 2 nd ROAD, HALF HOUSE ESTATE P O BOX 4601 1685 Tel: 011 456 9473 Fax: 086 537 3025	
 ProCiv Consulting & Projects Management			
KNA CONSULTING ENGINEERS JV			
Drawn By	M.M.	Approved.....	Pr.Eng
Checked By	A.M	Registration No.	20120172
Date	09-02-2024	Date	29-06-2023

INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDING, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS

VIOOLSDRIFT (SHEET 3 OF 3) LPOE SITE LAYOUT

FIRE FIGHTING EQUIPMENT			
LOCATION	ROOM NO	TYPE	KG
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5
ADMIN		DCP	4.5

FIRE FIGHTING EQUIPMENT: FIRE HYDRANTS		
LOCATION	ROOM NO	TYPE
ADMIN	1	FIRE HYDRANT
ADMIN	2	FIRE HYDRANT
ADMIN	3	FIRE HYDRANT
ADMIN	4	FIRE HYDRANT
ADMIN	5	FIRE HYDRANT

AIR-CONDITIONER LIST			
Room	Make	Model	Serial nr
Admin Office	LG	UT18	805KED00012
Agriculture Office	LG	809 AM	901ASV0002
Agriculture Office	LG	512AM	901AXX0014
Agriculture Office	LG	512AM	805KED00232
BM Personal Assistant	LG	520AM	801KAAU00086
BM Port Coordinator	LG	512A11	811KAE00048
Board Room	LG	M724AH	803KAAU0048
Chief of Staff	LG	695AM	901KAC00027
Chief Immigration	LG	UT18	804KASPT0478
Customer Departures	LG	UT 60	805KAA00085
Customer Departures	LG	M724AH	804KAAU00085
Customers Records	LG	UT18	805KAS00001
Customs	LG		
Customs Branch Manager	LG	M724AH	803KED00044
Customs Office	LG	809AM	901KAA00023
Customs Office	LG	UT18	805KAWD00017
Department of Health	LG	UT18	805KADT00034
Enroute Area	LG		
Gate House	LG	UT18	805KAM00347
Gate House	LG	UT18	805KASV00035
IT	LG		
IT Office	LG	UT18	805KAPD00018
IT Room	LG		
Immigration Departures	LG	UT60	805KAPC00348
Immigration Head Office	LG	UT18	804MLC00008
Interview	LG		
NIA Office	LG		
Operational Commanders Office	LG		
Registry Office	LG	UT 15H	804KAYJ0029
Registry Office	LG	MT012AH	901KAXX01993
Registry Office	LG	MT12AH	804KARU00014
Service Support Service	LG	UT10	805KAF00064
SAPS Office	LG	512AM	
SAPS Finance	LG		
SAPS Office	LG	UT24	804KAYR00306
SAPS office	LG		
SAPS Office	LG	512FN	901KAUU00110
SAPS Office	LG		
SAPS Quality Assurer	LG	UT 18	805KED00026
Scanner Search	LG	UT18	805KAYN00231
Scanner Search	LG	UT18	805KJFX00220
Store	LG		
Store	LG		
Store Supervisor	LG	UT18	805KAPJ00025
Supply Chain	LG	UT05	805KAMJ00027
Tax Refund	LG	509H8M	805KARV00038
Team Leader	LG		
Team Leaders	LG		
Ware House	LG	509AM	101KAXX00091
Ware House	LG	312AM	901KAYR11122
Ware House	LG	512A11	901KADT00021
Ware House	LG		

[illegible]

		CONSULTANT:	
		PROCIV-KNA JV UNIT 6, CMA OFFICE, AND CONFERENCE PARK, NO.1, 2 nd ROAD, HALF HOUSE ESTATE- P O BOX 4601 1465 Tel: 011 656 9473 Fax: 086 537 3025	
Drawn By	M.M.	Approved	Pr.Eng
Checked By	A.M	Registration No.	20120172
Date	09-02-2024	Date.	29-06-2023

INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDING, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS

VIOOLSDRIFT LPOE SITE LAYOUT PLANS LIST

INFRASTRUCTURE MAINTENANCE AND REPAIRS OF BUILDING, CIVIL, MECHANICAL, ELECTRICAL AND INSTALLATIONS																			
ONSEEPKANS LPOE SITE LAYOUT PLANS LIST																			
station		site								doc.type						#			
		-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-	-
SCALE		1:500																	
DRW No.		WCS		056397-ONSEEPKANS-LP-001															
		 Revision																	
